

Weekly News Letter October 21, 2016



A Week In Review

- Site Work:
 - Poured concrete walls in East half of courtyard
 - Started forming concrete walls in West half of courtyard
- Shelter:
 - Finishing putting up sheet rock and started taping and bedding
 - Started interior painting behind the tape and bed
 - Continued installing fire sprinkler mains and branch lines
 - Continue working on interior Hardie board panels
 - Continued storefronts and glazing
 - Completed installing roof insulation in West half of building
 - Continue running gas lines and installing plumbing fixtures
 - Installing accessories and toilet partitions in gang bathrooms
 - Installed overhead doors
 - Painted ceiling in East half of building
- Building infill in middle of shelter
 - Completed roofing and finished up MEP rough-in


What's Next?

- Site Work:
 - Completing all underground utilities in the courtyard
 - Completing existing water line repairs on South side of site
 - Continue pouring concrete for concrete in the courtyard
 - Begin concrete flatwork
- Building:
 - Continue roof repairs
 - Begin painting of exterior wall panels
 - Begin floor prep followed by hard surface flooring installation
 - Light fixtures
 - Install toilet partitions
 - Setting plumbing fixtures
 - Casework to be installed
 - Continue painting
 - Start installing doors

Community Impacts

- Work Hours: 6AM - 4:30 PM
- SRM daily operations have moved to 19 and 21 W Las Vegas to allow for the demolition and remodel of the shelter
- Site access is limited throughout:
 - A construction fence has been placed up in the courtyard to safely isolate construction activities
- Nunn Construction has hired four members of the SRM program!!! The three newest hires are members of a security team that will help keep the project site secure throughout the remaining duration

Construction Site Overview

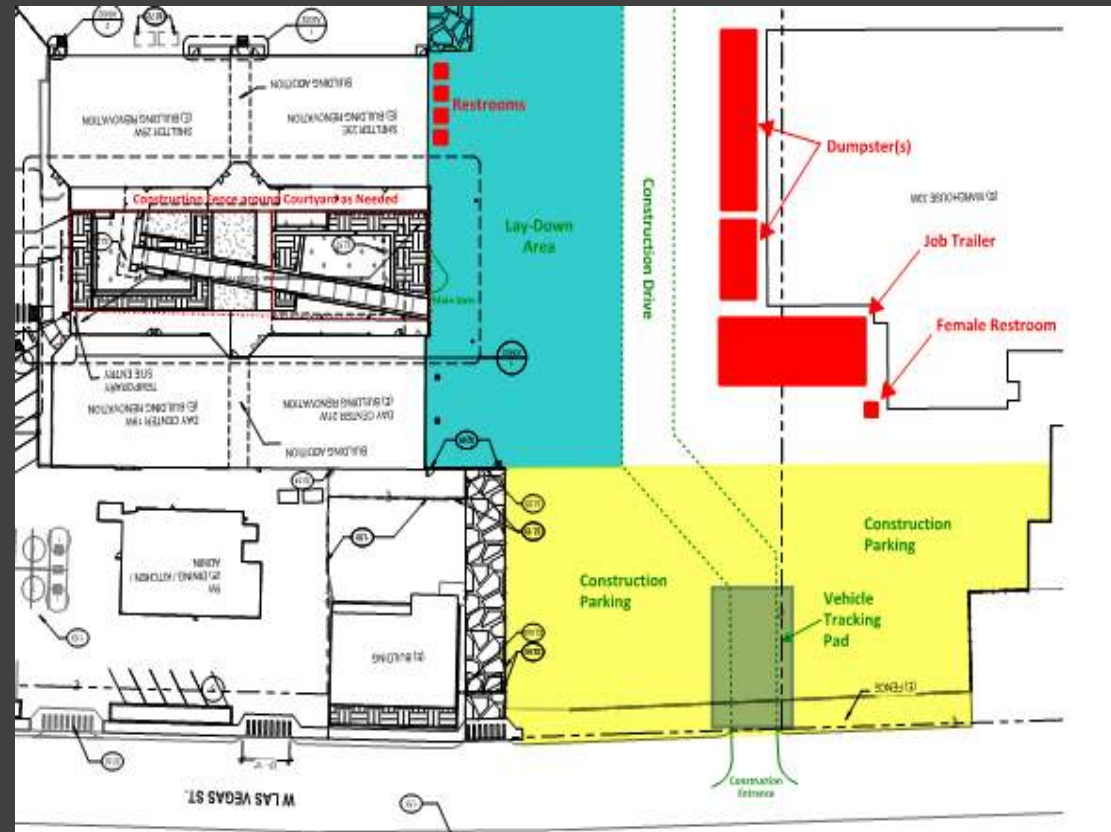

Subcontractors On Site

- *Gen Contractor:* Nunn Construction
- *Dewatering:* Rain for Rent
- *Utilities:* A&R, CSU
- *Dirt work:* Lambert & Sons
- *Plumbing:* Olson Plumbing
- *Electrical:* Greiner Electric
- *Mechanical:* Colorado Sheet Metal
- *Metal Framing:* Tri City Drywall
- *Concrete:* Peak Concrete
- *Roofing:* Central States
- *Steel:* Kutch Steel
- *Insulation:* MATO Insulation
- *Painting:* NCJ Painting

Daily Weather History & Observations


2016	Temp. (°F)			Dew Point (°F)			Humidity (%)			Sea Level Press. (in)			Visibility (mi)			Wind (mph)			Precip. (in)	Events
Oct	high	avg	low	high	avg	low	high	avg	low	high	avg	low	high	avg	low	high	avg	high	sum	
16	86	68	49	28	18	14	38	23	7	29.70	29.60	29.52	10	10	10	32	12	37	0.00	
17	86	65	44	31	22	10	45	26	6	29.80	29.51	29.34	10	10	10	37	17	55	0.00	
18	59	50	41	25	20	17	45	32	19	30.07	29.94	29.78	10	10	10	26	14	32	0.00	
19	58	49	40	33	27	17	73	48	23	30.40	30.18	29.95	10	10	10	36	11	44	0.00	
20	58	45	31	25	22	18	64	44	23	30.53	30.40	30.29	10	10	10	21	8	28	0.00	
21	71	48	33	19	14	8	56	35	10	30.27	30.17	30.10	10	10	10	10	7	-	0.00	



Steel frame being
installed for reception
desk in building 25



Toilets installed in
Women's gang
restroom, building 25



Overhead door
installed in building
23

Exterior of both
buildings painted



Storefront doors
installed and
interior paint
going up in
building 23





Concrete planter
in the courtyard
