Stormwater Advisory Committee

Projects Update 2023 Q3






IGA Projects Summary

Project Status Q3, 2023				
Complete	Construction	Design	Planning	Future
36	4	14	11	6
51%	6%	20%	15%	8%



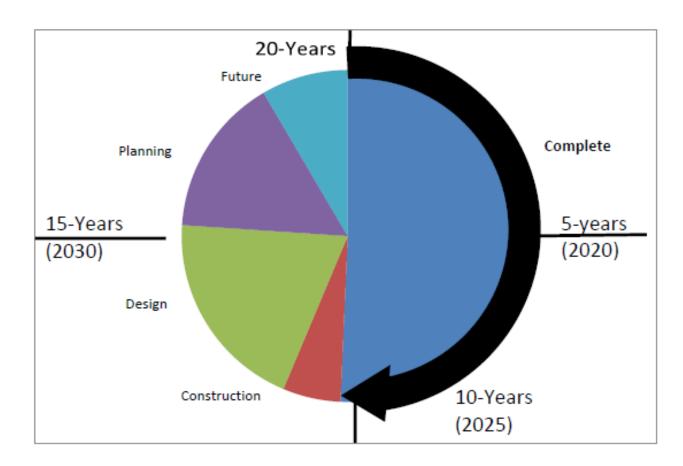

Notes:

- * 71 planned projects
- * Average of 3.5 projects per year over 20 years
- * Based on average, 24 projects to be completed by end of 2023
- * Planning includes 10% concept designs, easement acquisitions and stakeholder coordination.



- Fairfax detention Pond Complete by Dec 31st
- Cottonwood Creek APTS Complete by Dec 31st
- Pine Creek Phase II Complete by Spring, 2025

Construction Planned for Winter/Spring 24'



- Middle Tributary at I-25
- Black Squirrel Creek at USAFA, PH II (Non-IGA Project)
- Barnes Outfall Water Quality Pond (CD Project)
- South Douglas Creek below Sinton Road

Currently Planning for Construction Fall 24'

- Park Vista (Partial ARPA Funding)
- North Nevada Drainage Improvements (ARPA)
- Downtown Drainage Improvements (ARPA)
- Cottonwood Creek at Powers
- Hancock Training Facility



These projects are moving forward with Design and/or Construction in the Winter/Spring 2024

- EF Sand Creek at Powers
- EF Sand Creek at Wildflower Park
- South Douglas Natural Channel Downstream of Centennial
- South Douglas Concrete Channel
- Monument Branch Voyager to USAFA
- Hancock Expressway Peterson Field Concrete Channel
- Village Seven Concrete Channel at North Carefree Circle
- SC Peterson Field Channel at Sand Creek
- Hancock Expressway Concrete Channels
