INVITATION FOR BID

Construction

B20-141MZ

Date issued: September 23, 2020

NORTH CHELTON ROAD DRAINAGE IMPROVEMENTS

THE CITY OF COLORADO SPRINGS

The City of Colorado Springs hereby solicits Fixed Unit Price Bids, as detailed in this Invitation for Bids (IFB), for North Chelton Road Drainage Improvements.

SECTION I – BID INFORMATION

1.0 BID INFORMATION

Section I provides general information to potential Bidders, such as bid submission instructions and other similar administrative elements. This Invitation for Bid (IFB) is available on BidNet (www.bidnetdirect.com). All addenda or amendments shall be issued through BidNet and may not be available through any other source.

1.1 SPECIAL TERMS

Please note the following definitions of terms as used herein:

The term "City" means the City of Colorado Springs.

The term "Contractor" or "Consultant" means the Bidder whose offer is accepted and is awarded the contract to provide the products or services specified in the IFB.

The term "Offer" or "Bid" means a bid submitted in response to this IFB.

The term "Offeror" or "Bidder" means the person, firm, or corporation that submits a formal bid or offer and that may or may not be successful in being awarded the contract.

The term "Project" refers to North Chelton Road Drainage Improvements.

The term "Invitation for Bid" or "IFB" means this solicitation of formal, competitive, sealed bids from prospective bidders in which the intent is to award a contract to the resultant lowest responsible and responsive bidder.

1.2 BID ISSUE DATE

Invitation for Bid (IFB) Number B20-141MZ is being issued and posted on www.bidnetdirect.com on September 23, 2020

1.3 SUBMISSION OF BIDS

A. Bids are to be submitted electronically online to the Rocky Mountain E-Purchasing System (www.bidnetdirect.com).

B. Bids shall be received on or before: 2:00PM October 21, 2020

C. Bid bond is required if total bid exceeds $50,000.00. (Also see 1.22)

D. The cost of Bid preparation is not a reimbursable cost. Bid preparation shall be at the Bidder's sole expense and is the Bidder's total and sole responsibility.

1.4 PRE-BID CONFERENCE

A virtual pre-bid conference will be held for this Bid at 1:00PM on September 30, 2020. Please use the following link to attend the meeting

Join Microsoft Teams Meeting

You may also join via telephone by calling 720-617-3426 and enter conference ID 684 906 772#

1.5 LATE BIDS/LATE MODIFICATIONS OF BIDS

Bids, withdrawals or modifications of Bids received after the time set for opening, as designated in 1.3 above, are considered "late bids", and will not be accepted by the City, except as provided for in the City of Colorado Springs Procurement Rules and Regulations and approved by the Procurement Services Manager. Bidders are solely responsible for insuring their bids arrive on time and to the place specified in this Invitation for Bid.

1.6 MISTAKES IN BIDS - CONFIRMATION OF BID

If it appears from a review of a Bid that a mistake has been made, the Bidder may be requested to confirm its Bid in writing. Situations in which the confirmation may be requested include obvious, apparent errors on the face of a Bid or a Bid unreasonably lower than the other Bids submitted. All mistakes in Bids will be handled in accordance with the City of Colorado Springs Procurement Rules and Regulations**.**

1.7 PROCUREMENT RULES AND REGULATIONS

All formal IFBs advertised by the City of Colorado Springs are solicited in accordance with the City's Procurement Rules and Regulations. The City's Procurement Rules and Regulations can be reviewed and/or downloaded from the City's Procurement Services Division website www.coloradosprings.gov. Any discrepancies or conflicting statements, decisions regarding bidding irregularities, or clarifications regarding clauses or specifications will be rectified utilizing the City's Procurement Rules and Regulations, when applicable. It is the Bidder's responsibility to advise the Contracts Specialist listed in this IFB of any perceived discrepancies, conflicting statements, or problems with clauses or specifications prior to the Bid opening date and time.

1.8 MINOR INFORMALITIES/IRREGULARITIES IN BIDS

A. A minor informality or irregularity is one that is merely a matter of form and not of substance. It also pertains to some immaterial defect in a Bid or variation of a Bid from the exact requirements of the invitation that can be corrected or

waived without being prejudicial to other Bidders. The defect or variation is considered immaterial when the effect on price, quantity, quality, or delivery is negligible when contrasted with the total cost or scope of the goods and/or services being acquired.

B. If the City Procurement Services Division determines that a Bid submitted contains a minor informality or irregularity, then the Procurement Services Manager shall either give the Bidder an opportunity to cure any deficiency resulting from the minor informality or irregularity or waive the deficiency, whichever is to the advantage of the City. In no event will the Bidder be allowed to change the Bid amount. Examples of minor informalities or irregularities include but are not limited to the following:

(1) Bidder fails to sign the Bid, but only if the unsigned Bid is accompanied by other material evidence, which indicates the Bidder's intention to be bound by the unsigned Bid (such as Bid security, or signed cover letter which references the Bid Number and amount of Bid).

(2) Bidder fails to acknowledge an Amendment, although this may be considered a minor informality only if the Amendment, which was not acknowledged, involves only a matter of form or has either no effect or merely a negligible effect on price, quantity, quality, or delivery of the item or services bid upon.

1.9 REJECTION OF BIDS

The Procurement Services Manager has the authority to reject any Bid based on, but not limited to, the following:

A. Any Bid that fails to conform to the essential requirements of the Invitation for Bids shall be rejected.

B. Any Bid that does not conform to the applicable specifications shall be rejected unless the IFB authorizes the submission of alternate bids and the items or services offered as alternates meet the requirements specified in the IFB.

C. A Bid that fails to conform to the specified delivery schedule.

D. A Bid shall be rejected when the Bidder imposes conditions that would modify requirements of the IFB or limit the Bidder's liability to the City, since to allow the Bidder to impose such conditions would be prejudicial to other Bidders.

For example, Bids shall be rejected in which the Bidder:

(1) Protects against future changes in conditions, such as increased costs, if total possible costs to the City cannot be determined. This includes failure to completely fill out required bid schedule.

(2) Fails to state a price and indicates that price shall be “price in effect at time delivery”.

(3) States a price but qualifies it as being subject to “price in effect at time of delivery”.

(4) Takes exceptions to the IFB terms and conditions.

(5) Inserts the Bidder’s terms and conditions.

(6) Limits the rights of the City under any Contract/Invitation for Bid clause.

E. Any Bid in which the price is considered to be unreasonable or is over budget.

F. Any Bid if the prices are determined to be unbalanced.

G. Bids received from any person or contractor that is suspended, debarred, proposed for debarment, or under investigation for fraud, including failure to pay federal, state, local or city taxes.

H. When a bid guarantee is required and the bidder fails to furnish the guarantee in accordance with the requirements of the IFB.

I. Low Bids received from bidders who are determined to be non-responsible in accordance with the City’s Procurement Rules and Regulations.

J. Any Bid that was prepared and submitted by a vendor who has been determined by the Procurement Services Manager to have an unfair advantage over other Bidders. Examples of an unfair advantage include, but are not limited to, the following:

(1) A previous or prior employee who in the last six 96) months was directly involved in the design or specification preparation of the competed procurement.

(2) A vendor who was directly involved in design or specification preparation of the competed project either for pay or voluntarily.

1.10 ESTIMATED QUANTITIES

If the Bid Form (Schedule A) herein contains estimated quantities, this provision is applicable. The quantities listed for each of the items in the Bid Form are only estimated quantities. Contractors are required to bid a firm unit price for each item

specified. The actual quantities ordered may fluctuate up or down. The unit prices proposed by each Bidder will remain firm and will not be re-negotiated if the estimated quantities are not met or are exceeded. This clause will take precedence over any/all other estimated quantity clauses that conflict with this clause.

For bidding purposes, if there is a conflict between the extended total of an item and the unit price, the unit price shall prevail and be considered as the amount of the Bid. All unit prices shall include all necessary overhead and profit. Items not listed in the Bid Form such as overhead, profit, mobilization, de-mobilization, bonding, etc. shall be distributed throughout the Bidder's Unit Prices for the items listed on the Bid Form.

1.11 NUMBER OF COPIES

Bids are to be submitted electronically online to the Rocky Mountain E-Purchasing System (www.bidnetdirect.com).

1.12 IDENTIFICATION OF BID

Bids are to be submitted electronically online to the Rocky Mountain E-Purchasing System (www.bidnetdirect.com).

1.13 SALES TAX

The successful Offeror, if awarded a contract, shall apply to the Colorado Department of Revenue for a tax-exempt certificate for this project. The certificate does not apply to City of Colorado Springs Sales and Use Tax which shall be applicable and should be included in all bids and proposals. The tax exempt project number and the exemption certificate only apply to County, PPRTA (Pikes Peak Rural Transportation Authority), and State taxes when purchasing construction and building materials **to be incorporated into this project**.

Furthermore, the exemption **does not** include or apply to the purchase or rental of equipment, supplies or materials that **do not become a part of the completed project or structure**. In these instances, the purchase or rental is subject to full taxation at the current taxation rate.

The Offeror and all subcontractors shall include in their Offer City of Colorado Springs Sales and Use Tax on the work covered by the offer, and all other applicable taxes. Any increase in applicable sales or use tax occurring after the contract has been let shall be borne by the contractor and not passed through to the City.

Forms and instructions can be downloaded at the City of Colorado Springs Website: https://coloradosprings.gov/sales-tax/page/construction-contractors Questions can

be directed to the City Sales Tax Division at (719) 385-5903 or Construction_SalesTax@coloradosprings.gov).

Our Registration Numbers are as follows:
City of Colorado Springs
Federal I.D.: 84-6000573
Federal Excise: A-138557
State Sales Tax: 98-03479

1.14 PREPARATION OF BID OFFER

A. Bidders are expected to examine the drawings, specifications, bid documents, proposed contract forms, terms and conditions, and all other instructions and solicitation documents. Bidders are expected to visit the job-site to determine all requirements and conditions that will affect the work. Failure to do so will not relieve a Bidder from their responsibility to know what is contained in this Invitation for Bid, or site conditions affecting the work.

B. The Bidder certifies that it has checked all of its figures and understands that the City will not be responsible for any errors or omissions on the part of the Bidders in preparing its Bid.

C. All items, (unless the invitation specifically states otherwise) including any additive or deductive alternates on the Bid Form, must be completely filled out or the Bid will be determined non-responsive and ineligible for consideration for award.

D. The Bidder declares that the person or persons signing this Bid is/are authorized to sign on behalf of the firm listed and to fully bind the Bidder to all the requirements of the IFB.

E. The Bidder certifies that no person or firm other than the Bidder or as otherwise indicated has any interest whatsoever in the Bid or the contract that may be entered into as a result of the Bid and that in all respects the Bid is legal and firm, submitted in good faith without collusion or fraud.

F. By submitting a Bid the Bidder certifies that it has complied and will comply with all requirements of local, state, and federal laws, and that no legal requirements have been or will be violated in making or accepting this Bid. Bidders are expected to review the City's Procurement Rules and Regulations, which will be used when determining whether a Bidder is responsive and responsible and awarding contracts in the best interest of the City.

G. If there is a discrepancy between the unit price and the total price, the unit price shall be used to determine the applicable total price. Bidders are responsible for including profit and overhead associated with the project when determining their unit prices.

1.15 BASIS OF AWARD

A. The City of Colorado Springs intends to award a contract to the lowest responsive and responsible Bidder whose Bid meets the requirements and the criteria set forth in the Invitation for Bids and is determined to be in the best interest of the City.

B. The City reserves the right to reject any or all Bids and to waive informalities and/or irregularities in a Bid. Whether or not a contract is awarded as a result of this Invitation for Bid, as stated above, Bid preparation costs are not reimbursable.

C. Total Bid will be evaluated and awarded as follows: It is the City's intent to award this bid based on the TOTAL BASE BID, not on a line item by line item basis.

1.16 PERIOD OF ACCEPTANCE

The Bidder agrees that its Bid shall remain open for acceptance by the City for a period of sixty (60) calendar days from the date specified in the IFB for receipt of Bids.

1.17 CONTRACT AWARD

The signature of the Bidder indicates that within ten (10) calendar days from acceptance of its Bid, it will execute a contract with the City and, if indicated in this IFB, furnish a project specific Certificate of Insurance naming the City as Additional Insured, furnish Performance, Labor and Materials, Payment and Maintenance Bonds and any other documents required by the Specifications or Contract Documents.

1.18 NOTICE TO PROCEED

Work may not start under any awarded contract until a written notice to proceed is issued by the City. The City may issue the Notice to Proceed any time after the contract is signed and, if required, insurance and bonds have been provided in accordance with 1.22 below.

1.19 AMENDMENTS TO THE SOLICITATION

Amendments are also referred to as addendum or addenda; and these terms shall be considered synonymous. It is the Bidder's responsibility to contact the Contracts Specialist listed in 1.21 below to confirm the number of Amendments which have been issued.

A. If this solicitation is amended, then all specifications, terms and conditions, which are not specifically amended, remain unchanged.

B. Bidders shall acknowledge receipt of any amendment to this solicitation by signing and returning the amendment and by identifying the amendment number and date in the space provided on the form for submitting a Bid.

C. Acknowledged amendments must be received prior to Bid opening. Bidders are encouraged to include signed addenda or initialed acknowledgment with returned Bids.

1.20 EXPLANATIONS TO PROSPECTIVE OFFERORS

Any prospective Bidder desiring an explanation or interpretation of the IFB documents, drawings, specifications, etc., must request it in writing within ten days of the Bid due date to allow enough time for a reply to reach all prospective offerors before the time for submission of offers. Oral explanations or instructions given before the opening of Bids will not be binding. Any information provided to a prospective Bidder during the Bid preparation stage will be promptly furnished to all other prospective Bidders as an amendment to the solicitation, if that information is necessary in submitting Bids or if the lack of it would be prejudicial to other prospective Bidders.

1.21 QUESTIONS AND OTHER REQUESTS FOR INFORMATION

All questions shall be submitted in writing to the following Contract Specialist. All questions must be submitted by email and must be received no later than **1:00 PM October 7, 2020.**

All questions shall be directed to: (Contract Specialist)	**Michael Zeller** **Michael.zeller@coloradosprings.gov**

DO NOT CONTACT ANY OTHER INDIVIDUAL AT THE CITY OF COLORADO SPRINGS REGARDING THIS SOLICITATION.

1.22 SECURITY REQUIREMENTS

A. Bid Security

(1) If the total amount of the accumulative Bid is more than $50,000, or a bond is required elsewhere in this IFB, the Bidder is required to furnish with their Bid a bid security in the form of a bank certified check, bank cashier's check or a one-time bid bond underwritten by a company licensed to issue bonds in the State of Colorado and acceptable to the City in an amount equal to at least 5% of the total amount of the Bid

payable without condition to the City.

(2) The Bid security shall guarantee that the Bid will not be withdrawn or modified for a period of sixty (60) calendar days after the time set for the receipt of Bids, and, if the Bid is accepted within those sixty (60) calendar days, that the person, firm or corporation submitting same shall within ten (10) calendar days after being notified of the acceptance of its Bid, enter into a Contract and furnish the required bonds and all insurance certificates called for under this Invitation for Bid.

(3) The Bid bonds of unsuccessful Bidders will not be returned to the respective Bidders unless a self-addressed, stamped envelope is provided along with a written request for bid bond return. However, if a certified check or a cashier's check is submitted as Bid security, it will be returned as soon as possible after the lowest responsive and responsible Bidder is determined and a contract is executed.

(4) In the event the Bidder whose Bid is accepted fails to enter into the contract and/or furnish the required contract bonds, its certified check, cashier's check or bid bond will be forfeited in full to the City.

B. Performance, Labor and Materials Payment, and Maintenance Bonds

(1) For contracts in excess of $50,000, the Contractor shall furnish to the City each of the following: a Performance Bond, a Labor and Materials Payment Bond, and a Maintenance Bond. Each such bond shall be in the amount of one hundred percent (100%) of the contract price. Bonds shall be submitted within ten (10) calendar days after notification of award of a Contract. The cost of all bonds shall be included in Contractor's Bid.

(2) Bonds shall:

a) Be for the full amount of the Contract price.
b) Guarantee the Contractor's faithful performance of the work under the Contract, and the prompt and full payment for all labor and materials involved therein.
c) Guarantee protection to the City against liens of any kind.
d) Be from a surety company operating lawfully in the state of Colorado and accompanied by an acceptable "Power-of-Attorney" form attached to each bond copy.
e) Be issued from a surety company that is acceptable to the City.
f) Be submitted using the forms in the Exhibit section of this IFB or such forms as are approved by the City Attorney's Office.

1.23 SPECIFICATIONS AND DRAWINGS

No Fee solicitations: Specifications and Drawings are normally included in the IFB. If Specifications and Drawings are too large to be included in the IFB, all interested Bidders may obtain one copy of the Project Specifications and a set of the Project Drawings for use in preparing Bids from the City Procurement Services Division office. If the Bidder requires additional sets, it is the Bidder's responsibility to duplicate any additional copies, at its own expense.

1.24 TYPE OF CONTRACT

As a result of this Invitation for Bids, it is the City's intention to award a fixed unit price contract based on the prices offered by the lowest responsive and responsible bidder. Contract prices shall remain firm and fixed throughout the Contract performance period.

1.25 F.O.B. DESTINATION

Unless otherwise specified in the Invitation for Bid, all goods, materials, supplies, equipment or services covered by this IFB shall be delivered F.O.B. Destination shall be the location indicated in the awarded Contract or Purchase Order.

1.26 BID RESULTS

The City does not mail Bid results or tabulations. However, Bid tabulations are posted and can be downloaded from BidNetDirect (www.bidnetdirect.com). Bidders submitting Bids in response to this solicitation may also request the Bid tabulation for this solicitation via email to the Contracts Specialist indicated as the point of contact for this solicitation.

1.27 APPROPRIATION OF FUNDS

A. In the event funds are not appropriated in whole or in part sufficient for performance of the City's obligations under this IFB, or appropriated funds may not be expended due the City Charter spending limitations, then the City, without compensation to Bidders, may terminate or cancel this IFB or not award any contracts under this IFB.

B. In accordance with the Colorado Constitution and City Charter, performance of the City's obligations under any resultant Contract will be expressly subject to appropriations of funds by the City Council, and, in the event the budget or other means of appropriation for any year of the Contract fails to provide funds in sufficient amounts to discharge such obligations, such failure (i) shall act to terminate the Contract at such time as the then-existing and available appropriations are depleted, and (ii) neither such failure nor termination shall constitute a default or breach of the Contract, including any sub-agreement, attachment, schedule, or exhibit thereto, by the City.

1.28 PERIOD OF PERFORMANCE

The Contractor shall complete all work within **150 Calendar Days** after the Notice to Proceed. The Contractor will start work promptly after receipt of the Notice to Proceed and Pre-Construction meeting and continue to work diligently until all work is completed and accepted by the City.

1.29 BID OPENING

The City will host a virtual bid opening via Microsoft Teams using the following link:

Join Microsoft Teams Meeting

You may also join via telephone by calling 720-617-3426 and enter conference ID 684 906 772#

1.30 BID DOCUMENTS

The following comprise this Invitation for Bid.

Schedule A – Bid Form
Schedule B – General Construction Terms and Conditions
Schedule C – Technical Specifications
Schedule D – Scope of Work
Schedule E – Construction Plan Set
Schedule F – Scope of Work
Schedule G -- Exhibits

The following listed documents must be included with your Bid in order for your Bid submittal to be considered responsive.

Schedule A -- Bid Form
Exhibit 2 – Minimum Insurance Requirements Form
Exhibit 3 – Qualification Statement
Exhibit 4 -- Representations and Certifications
Exhibit 5 -- Bid Bond if applicable (see 1.22)
Acknowledged Addendums, if issued

SECTION II – SCHEDULES

Schedule A – Bid Form
Schedule B – General Construction Terms and Conditions
Schedule C – Technical Specifications
Schedule D – Scope of Work
Schedule E – Construction Plan Set

SCHEDULE A -- BID FORM – TO BE COMPLETED ON BIDNET

SCHEDULE B – GENERAL CONSTRUCTION TERMS AND CONDITIONS

GENERAL CONSTRUCTION TERMS AND CONDITIONS

SECTION 100 DEFINITIONS AND TERMS

Titles used in these specifications having a masculine gender, such as “workmen” and the pronouns “he” or “his”, are for the sake of brevity and are intended to refer to persons of any gender.

The titles or headings of the sections and subsections herein are intended for convenience of reference and shall not have any bearing on their interpretation.

When the Contract indicates that something “shall” be done, the action is required and is not discretionary.

Calendar Day	Each and every day shown on the calendar, beginning and ending at midnight.
Change Order	A written order issued to the Contractor by the City covering contingencies, extra work, increases or decreases in Contract quantities, and additions or alterations to the plans or specifications, within the scope of the Contract, and establishing the basis of payment and time adjustments for the work affected by the changes. The Change Order is the only method authorized for changing the Contract.
City	The City of Colorado Springs, Colorado.
Contract Documents	Contract Documents include the Request for Proposal, Instructions to Offerors, Proposal, Amendments, the signed Contract, surety bonds, insurance documents, all terms, conditions, and provisions, and the Specifications, including all modifications thereof incorporated in any of the documents before execution of the agreement.
Contract	The executed written agreement between the City and the Contractor setting forth the obligations of the parties for the performance of the work and the basis of payment. The Contract includes the Contract Documents, Notice to Proceed, and executed Change Orders, all of which constitute one instrument.

Contractor	The person, persons, firm, or corporation to whom a Contract is awarded by the City and who is subject to the terms of said Contract. Contractor shall include the agents, employees, workmen, subcontractors and any assignees of said Contract.
Engineer	An engineer of the City of Colorado Springs.
Notice	Any written notice served pursuant to the terms of the Contract. Notice shall be deemed to have been duly served if delivered in person or by registered mail to: The Project Manager assigned to the Contract, City of Colorado Springs, City Engineering, 30 South Nevada Ave., Room 403, Colorado Springs, CO 80903. Notice to the Contractor will be to the Authorized Representative of the Contractor at the site of the Project in person; or by registered mail to the Contractor's principal place of business as indicated in the Contractor's proposal certifications; or as to the Surety on the performance bond by registered mail to the Surety at the home office of such surety.
Plans	The drawings, or reproductions, provided by the City that show the location, character, dimensions, and details of the work to be done.
Project Manager	An individual representing the City responsible for managing and oversight of the Contract. .
Project	The entire improvement outlined in the Scope of Services which is to be constructed in whole or in part pursuant to the Contract.
Subcontractor	A person, firm, or corporation, other than the Contractor, supplying labor or materials, or both, or equipment furnished at the site of the project under an Agreement with the Contractor.
Surety	The person, firm, or corporation that has executed as surety the Contractor's Proposal, Performance, Payment and Maintenance Bonds.
Work	Work performed under the Contract.

Working Days	Days of the week, not including weekends and City holidays, unless otherwise stated.

SECTION 101 CONTRACT DOCUMENT INTERPRETATION

101.00 INTENT OF CONTRACT DOCUMENTS

The sections of the Contract Documents are complementary, and what is called for by any one shall be as binding as if called for by all. The intent of the Contract Documents is to include the cost of all labor and materials, water, fuel, tools, plants, equipment, light, transportation, and all other expenses as may be necessary for the proper execution of the work. If the Contract Documents should be contradictory in any part, the order of precedence shall be as described in the Contract.

Any work shown on the Plans and not covered in the specifications, or included in the Specifications and not shown on the Plans, shall be executed by the Contractor as though shown both on the Plans and included in the Specifications.

If the Contractor, in the course of the work, finds any discrepancy between the Plans and the physical layout, or any errors or omissions in Plans or layout, he shall immediately so inform the Project Manager and the Project Manager will promptly verify them. Any work done after such discovery without written consent of the Project Manager authorizing the same shall be done at the Contractor's risk and sole expense.

Any incidental and/or appurtenant items not specifically called for in the Plans and Specifications, but which are necessary to complete the work in accordance with the requirements of good practice, as determined by the Project Manager, shall be included as a part of the Contractor’s proposal price and furnished at no additional cost to the City.

In interpreting the Contract Documents, words describing materials or work which have a well-known technical or trade meaning, unless otherwise specifically defined in the Contract documents, shall be constructed in accordance with such well known meaning recognized by architects, engineers, and the trade.

101.01 SPECIAL PROVISIONS, SPECIAL SPECIFICATIONS

Special Provisions or Special Specifications may be written to expand upon, modify or cancel these general provisions or the standard specifications.

101.02 STANDARD MANUFACTURER

Wherever the terms "standard", "recognized" or "reputable" manufacturers are used, they shall be construed as meaning manufacturers who have been engaged in the business of fabricating materials, equipment, or supplies of the nature called for by the Specifications for a reasonable period of time prior to the date set for submission of proposals, and who can demonstrate to the satisfaction of the City that said manufacturer has successfully installed equipment, materials, or supplies of the type proposed to be furnished in at least three instances and that the performance of such materials, equipment, or supplies for a period of over twelve months prior to the date fixed for submission of proposals shall, prima facie, be deemed to have been engaged in such business for a reasonable length of time.

101.03 "OR EQUAL" CLAUSE

Whenever in any section of the Contract documents, any article, material, or equipment is defined by describing a proprietary product, or by using the name of manufacturer or vendor, the term "or equal" if not inserted, shall not be construed in such a manner as to exclude manufacturers' products of comparable quality, design, and efficiency, subject to review and approval by the Project Manager. The Project Manager may require that proposed equals be submitted for review and approval.

SECTION 102 COMPLIANCE WITH LAWS

102.00 PUBLIC IMPROVEMENT ASSESSMENT

If the cost of the improvement to be constructed under the Contract is to be assessed upon the owners of land benefited by such improvement, upon complaint of any such landowner that the improvement is not being constructed in accordance with the Contract, the City Council may consider the complaint and make such order in the premises as shall be just to ensure compliance with the Contract.

102.01 ALL LEGAL PROVISIONS INCLUDED

It is the intention and agreement of the parties to this Contract that all legal provisions of law required to be inserted, shall be and are inserted. However, if by mistake or otherwise, some such provision is not inserted, or is not inserted in proper form, then upon application of either party, the Contract shall be amended so as to strictly comply with the law and without prejudice to the rights of either party.

102.02 LICENSES AND PERMITS

It shall be the responsibility of the Contractor to obtain, at its expense, all necessary licenses and permits to do the Project, in accordance with applicable Federal, State and local laws, regulations and ordinances. Typical permits and fees include, but are not limited to, Excavation/Boring Permits, Concrete Construction Permits, Fugitive Dust Permits, Regional Building Permits, Pavement Degradation fees, as well as Traffic Control and Barricade Plans to be approved by the City Traffic Division for all work within public rights-of-way and easements i.e. (curb and gutter, sidewalks, pedestrian ramps and cross pans).

SECTION 103 AWARD AND EXECUTION OF CONTRACT

103.00 CONTRACT EXECUTED

A single original Contract to include the Contractor's Performance, Labor and Material Payment and Maintenance Bonds may be executed and maintained in the official Contract file located in the City Contracts office. The original copy of the Contract maintained in the City Procurement Services file shall take precedence for purposes of interpretation or determining what the Contract says. After all required signatures are obtained; photocopy counterparts (copies) will be made and distributed to the following, as applicable:

(a) Contractor
(b) Project Manager
(c) City Finance Department
(d) Inspector

Each Bond shall have an original Power of Attorney attached. The Contractor shall provide compensation insurance and public liability and property damage insurance as outlined in the Contract. The costs of executing the bonds, Contract, and insurance, including all notaries' fees and expense, are to be paid by the Contractor to whom the Contract is awarded. Bonds shall be furnished on forms prepared by the City. Copies of the City's Bond Forms are included in the Exhibits Section of the Request for Proposal, if applicable.

103.01 VERBAL AGREEMENTS

No verbal agreements or conversations with any agent or employee of the City either before or after execution of the Contract shall affect or modify any of the terms or obligations contained in any of the documents comprising the Contract.

103.02 CONTRACT SECURITY

The Contractor shall furnish good and sufficient Performance, Labor and Material Payment and Maintenance Bonds on the form attached hereto in an amount not

less than the full amount of the Contract price as security for the faithful performance of the Contract, for the payment of all persons performing labor and furnishing material in connection with the work, and for all guarantees of materials and workmanship required in the Contract. If at any time during the continuance of the Contract a surety on the Contractor's bond or bonds becomes irresponsible, as determined in the City's sole and absolute discretion, the City shall have the right to require additional and sufficient sureties which the Contractor shall furnish within ten (10) days after written notice to do so. Any additional surety bonds shall cover the entire original Contract amount and any increases thereto.

103.03 INDEPENDENT CONTRACTOR

In the performance of the Contractor's obligations under this Contract, it is understood, acknowledged and agreed between the parties that the Contractor is at all times acting and performing as an Independent Contractor, and the City shall neither have nor exercise any control or direction over the manner and means by which the Contractor performs the Contractor's obligations under this Contract, except as otherwise stated within the Contract terms. The City shall not provide any direction to the Contractor on the work necessary to complete the Project. Contractor understands that it is an independent contractor responsible for knowing how to perform all work or tasks necessary to complete Project. The Contractor understands and agrees that the Contractor and the Contractor's employees, agents, servants, or other personnel are not City employees. The Contractor shall be solely responsible for payment of salaries, wages, payroll taxes, unemployment benefits or any other form of compensation or benefit to the Contractor or any of the Contractor's employees, agents, servants or other personnel performing services or work under this Contract, whether it be of a direct or indirect nature. Further in that regard, it is expressly understood and agreed that for such purposes neither the Contractor nor the Contractor's employees, agents, servants or other personnel shall be entitled to any City payroll, insurance, unemployment, worker's compensation, retirement or any other benefits whatsoever.

SECTION 104 THE CONTRACT: FOLLOWING EXECUTION

104.00 MATERIALS

Unless otherwise stipulated in the Contract, the Contractor shall provide and pay for all materials, labor, water, tools, equipment, light power, transportation, and other facilities necessary for the execution and completion of the work. The Contractor shall, if required, furnish satisfactory evidence as to the kind and quality of materials.

104.01 SCHEDULE

In the event of contradictions or inconsistencies, this clause shall take precedence over any language relevant to scheduling included anywhere else in this Contract.

The Contractor shall be responsible for planning, scheduling, and reporting the progress of the work to ensure timely completion of the work as called for in the Contract Documents. The Contractor shall prepare a detailed Project schedule ("Project Schedule") that shall be used for coordination, for evaluation of progress, and for the evaluation of changes to the Contract. The Project Schedule shall include all activities, including those of subcontractors, Contractor's engineers and surveyors, and suppliers. Seasonal and weather constraints, utility coordination, railroad restrictions, right of way restrictions, traffic constraints, environmental constraints, other project interfaces, expected job learning curves and other constraints shall be considered when preparing the Project Schedule, including any phasing or sequencing of the work specified in the Contract Documents. Days scheduled as no work days shall be indicated. The Project Schedule shall consist of a Methods Statement as defined in subsection (a) below and a progress schedule consisting of (1) a Critical Path Method ("CPM") schedule as defined in subsection (b) below, or (2) a Bar Chart schedule as defined in subsection (c) below. A CPM Schedule shall be required if the Contract exceeds $250,000 or if the construction period exceeds 150 Calendar Days, unless the Contract Documents stipulate otherwise. The CPM Schedule shall utilize Primavera's Suretrak Project Manager software (or other software designated by the Project Manager), or be capable of being read and manipulated by Suretrak Project Manager software (or other software designated by the Project Manager). The Project Schedule shall show all work completed within the Contract Period of Performance. The City reserves the right to approve or disapprove any proposed schedule. If disapproved, the Contractor must make requested changes and resubmit the schedule for approval within five working days of the disapproval by the City.

After award, the Contractor shall submit two copies of all required schedule information as described below. Schedules, schedule updates, diagrams and reports using CPM shall also be submitted electronically in the appropriate software format. All schedules, diagrams, and reports shall include a title, project number, date of preparation, and the name of the Contractor.

The Bar Chart or CPM 90-day schedule shall be submitted at least 14 Calendar Days prior to the start of the work. The Project Manager's review will not exceed five working days. Work shall not begin until the Project Schedule is accepted in writing, unless otherwise approved by the Project Manager.

(a) Methods Statement. A Methods Statement shall be prepared for the prominent features listed in the Contract Documents, and for any feature not listed in the Contract Documents that the Contractor considers a

controlling factor for timely completion. The Methods Statement shall be a detailed narrative describing each feature and all work necessary to complete the feature. The Methods Statement shall be submitted with the Contractor's schedule. The following format is required:

1. Feature: Name of the feature;

2. Responsibility: Contractor, subcontractor, supplier, utility, etc. responsible for the feature;

3. Procedures: Procedures to be used to complete the work. The procedure to be used shall include general information regarding methods such as forming, excavation, pouring, heating and curing, backfill and embankment, trenching, protecting the work, etc. When separate or different procedures are to be employed by the Contractor due to seasonal or Project phasing requirements, such differing procedures shall be described in the procedure statement;

4. Production Rates: The planned quantity of work per day for each feature;

5. Labor Force: The labor force planned to do the work;

6. Equipment: The number, types, and capacities of equipment planned to do the work;

7. Work Times: The planned time for the work to include:
   (a) number of work days per week
   (b) number of shifts per day
   (c) number of hours per shift

At the Project Manager's request, the Contractor shall update the Methods Statement, or any part thereof, and submit it with the Job Progress Narrative Report or Schedule Update, whichever is earlier.

(b) Critical Path Method. CPM is a scheduling method which shows the interdependencies between work activities. The critical path is that path through the schedule which, if delayed, will cause a delay to project completion.

The progress schedule shall include as a minimum the prominent features of this Project as listed in the Contract Documents. The progress schedule shall include all activities for all work on the Project, including subcontracted work, delivery dates for critical material, submittal and review periods, milestone requirements and no work periods. Where the Project has

specific phases, each phase shall be described separately for each applicable prominent feature.

Construction activity duration shall not exceed 15 Calendar Days unless approved by the Project Manager. Series of activities that have aggregate durations of five Calendar Days or less may be grouped in a single activity. For example, “form, reinforce, and pour pier” could be defined as a single activity rather than three. Single activities or a series of grouped activities of at least one Calendar Day duration may also need to be included in the Project Schedule as determined by the Project Manager (e.g. same activities but noted separately by location).

Time Scaled Logic Diagram: This diagram shall show the logical progression of all activities required to complete the work defined in the Contract Documents. Activity information shall include activity ID, description, duration, early start and finish dates, late start and finish dates, total float, and responsibility.

1. 90-Day Schedule. The 90-Day Schedule shall provide all necessary detail for procurement, construction and submittal activities required during the first 90 days of the Period of Performance. This submittal shall include a Time Scaled Logic Diagram.

2. Project Schedule, as described above.

   The Project Schedule shall cover the entire Period of Performance.

3. Schedule Updates. The Contractor shall update the 90-Day Schedule or the Project Schedule to reflect actual construction progress of all work activities on the project. Updates shall show the previous 30 days progress and a 60-day projection for all work started, completed, or in progress during this three month window.

   The Project Schedule shall be updated as of the cutoff date for the monthly progress pay estimate and submitted to the Project Manager before the payment of the progress pay estimate is approved.

   Each of the diagrams, charts, and reports shall comply with the requirements for the Project Schedule above, except that they shall also include the actual completion dates and percentages of completion for the appropriate activities.

(c) Bar Chart. The Bar Chart shall be time scaled and shall show the following:

1. The prominent features, as listed in the Contract Documents.

2. Any feature not listed in the Contract Documents that the Contractor considers a controlling factor for timely completion.

3. The number of days required to complete each feature and its relationship in time to other features.

4. Sufficient space for each feature to permit two additional plots parallel to the original time span plot.

5. The anticipated delivery dates for equipment or materials in any feature that could affect timely completion of the project.

6. Critical completion dates for any activity within any feature that could affect timely completion of the project.

7. Connecting lines between features that show the intended progression of activities.

The Project Schedule shall cover the time from the Day of Notice to Proceed to the predicted completion date. The Project Schedule shall be updated as of the cutoff date for the monthly progress pay estimate and submitted to the Project Manager before the payment of the progress pay estimate is approved. The Contractor shall provide a copy of the original bar chart showing, for each feature, the days actually worked and the anticipated days required to complete.

(d) Project Coordination. The Contractor shall coordinate and schedule its work to include anticipated utility work. Various City and private utility entities may be working to install and/or inspect their utilities within the Project area. Reasonable delays should be expected for utility lowering, relocations and placement. These delays shall not be reason for granting any monetary change or performance time alteration to the Contract. As a minimum, the Contractor's Project Schedule shall reflect coordination with the following:

1. City of Colorado Springs City Engineering Division

2. City of Colorado Springs Traffic Engineering Division

3. Colorado Springs Utilities (water, wastewater, gas, electric)

4. City of Colorado Springs Parks, Recreation and Cultural Services Department

5. Private Utility and Telecommunication Companies

(e) Contractor Early Finish or Voluntary Acceleration. Early finish or voluntary acceleration of the schedule by the Contractor is acceptable provided:

1. At the time the Contractor submits the Project Schedule indicating an early finish or voluntary acceleration, the City is notified in writing of actions on the City's part necessary to accommodate the change(s).
2. The City agrees to such change(s) in writing.
3. The City is compensated by the Contractor for any inconvenience or expense associated with the change(s).
4. There is no increase to Contract cost.

A Job Progress Narrative Report shall be submitted bi-weekly as a minimum and with all Project Schedule updates. It shall detail the description of job progress, problem areas, current and anticipated delaying factors and their anticipated effects, impacts to job milestones or Project completion, any corrective action proposed or taken, and any minor revisions to the Project Schedule. If the Job Progress Narrative Report indicates problem areas and impacts to job milestones or Project completion, a revised Project Schedule shall also be submitted as specified below.

Revision of the Project Schedule may be required, as determined by the Project Manager, for: a major revision in the schedule logic or methods of construction; the addition, deletion, or revision of activities required by Contract modification; delays in milestones or the completion of the Project; or for prosecution of work that revises the phasing or staging which is represented on the plans or on the progress schedule. If in the opinion of the Project Manager, the Contractor falls behind the approved Project Schedule, the Contractor shall take steps necessary to improve Project progress, including those steps that may be required by the Project Manager, without additional costs to the City. In those circumstances where the Contractor is behind schedule, the City may require the Contractor to increase the number of shifts, overtime operations, days of work, and/or the amount of construction planned and to submit such changes and revisions to the Project Schedule to the Project Manager for approval that will demonstrate how the approved rate of required progress will be regained. Failure of the Contractor to comply with the requirements of the Project Manager under this subsection shall be grounds for a determination by the City that the Contractor is not prosecuting the work with sufficient diligence to ensure timely completion of the Contract as required.

If it is determined that a revision to the Project Schedule is required, it shall be provided to the Project Manager for review within 15 Calendar Days of Contractor receiving written notification of the requirement from the Project Manager. The Project Manager's review of the revised schedule will not exceed 5 working days. Revisions required as a result of the Project Manager's review shall be submitted

within 5 working days. When accepted by the Project Manager in writing, the revised schedule shall become the Project Schedule.

The Contractor shall participate in the Project Manager's review and evaluation of the submittals. Meetings will be held to review progress and planning when requested by the Project Manager or Contractor. The Project Manager may request additional project scheduling information and documentation as deemed necessary, including reports and other information that may be reasonably generated using CPM software if required by the Contract.

The Contractor shall prosecute the work according to the Project Schedule. The Contractor shall be responsible for assuring that its subcontractors, suppliers, and engineers/surveyors, at any tier, also prosecute the work according to the Project Schedule. The City shall be entitled to rely on the Project Schedule for planning and coordination.

Acceptance of the Contractor's Project Schedule by the Project Manager is not to be construed as relieving the Contractor of obligation to complete the Contract work within the Contract time allowed for the portion of the work or the entire Contract, or granting, rejecting or in any other way acting on the Contractor's request for extension of Contract time, or claims for additional compensation.

All costs relating to preparation, submittal, and acceptance of the Project Schedule, reports and revisions, and all requirements of this subsection will not be paid for separately, but shall be included in the work.

Failure of the Contractor to comply with the requirements of this subsection may be grounds for a determination by the Project Manager that no further progress payments are to be made until the Contractor is in full compliance.

104.02 SCHEDULE OF VALUES

Promptly following the execution of the Contract Documents for all Firm Fixed Price, lump sum Contracts, the Contractor shall prepare and transmit to the Project Manager two copies of an itemized Project cost breakdown showing the unit quantities of each major construction item and the corresponding unit prices. Such unit prices shall contain all costs including profit and overhead of each item complete in place. The total cost of all the items shall equal the Contract price for the Project. This breakdown, once approved by the Project Manager, will be used primarily in determining payment due the Contractor as provided herein. If, in the opinion of the Project Manager, any unit price submitted by the Contractor is unbalanced, a detailed breakdown of the items contained in the unit will be required.

For Contracts executed on a fixed unit price basis, payment shall be made based on the actual number of units installed or performed that are complete, however,

payment shall not exceed the total Contract amount unless previously approved by Change Order.

104.03 SURVEYS

Unless otherwise specified in the Contract Documents, the City will furnish all site surveys, easements, pipeline licenses, etc., necessary to authorize construction of any permanent works required in the Contract, where such work is to be done on property other than the City's.

The Project limits of construction shall be within the public right-of-way and/or City easements. The Contractor shall not trespass on premises outside of the limits of construction for this Project, unless permission to do so is granted by the property owner in writing. Copies of any such grant shall be furnished to the City prior to the performance of any work outside the limits of construction.

104.04 SUBCONTRACTS

The Contractor will be permitted to subcontract a portion of the Contract; however, the Contractor shall perform work amounting to 30 percent or more of the original total cost of proposal items. Any items designated in the Contract as “specialty items” may be performed by subcontractor. The cost of “specialty items” so performed by subcontractor may be deducted from the original total cost of proposal items before computing the amount of work required to be performed by the Contractor.

The calculation of the percentage of subcontracted work shall be based on the Contract unit prices rather than subcontract unit prices. Proportional value for a subcontracted partial Contract item will be verified by the Project Manager. For the purpose of calculating the value of subcontracted work, the cost of procuring materials and manufactured products can be included in either the Contract or subcontract. However, when a firm both sells material to a Contractor and performs the work of incorporating the materials into the Project, these two phases shall be considered in combination and as constituting a single subcontract.

The Contractor shall as soon as practical after signing the Contract notify the Project Manager in writing, giving the names and qualifications, of all subcontractors proposed to do work on the Project within fifteen (15) business days of notice of award. The City shall have the right to reject subcontractors who are debarred or suspended from doing business with the federal government, State government, or the City of Colorado Springs. The Contractor shall notify the Project Manager of each subcontract he awards, giving:

(a) Name, address, and telephone number of the subcontractor

(b) Branch of work covered

(c) Total price of subcontract
(d) Date of subcontract

It shall be the responsibility of the Contractor to file with the Project Manager copies of applicable permits and licenses required to do the subcontracted work. Subcontracts or transfer of Contract obligations shall not release the Contractor of liability under the Contract and bonds.

104.05 OTHER CONTRACTS

The City may undertake or award other Contracts for additional work at or near the site of the work under this Contract. The Contractor shall fully cooperate with the other Contractors and with City employees and shall carefully adapt their scheduling and performance of the work to accommodate the additional work, heeding any direction that may be directed by the Project Manager. The Contractor shall not commit or permit any act, which will interfere with the performance of work by any other contractor.

SECTION 105 CONSTRUCTION SITE

105.00 LANDS TO BE USED FOR WORK

The Contractor shall confine the work activities to the area shown in the construction drawings. The Project Manager will furnish the Contractor with copies of all executed right of way (ROW) and easement documents for the Project. The established work zone shall be marked and secured with orange safety fence. Any additional work area required within adjoining private properties must be acquired by the Contractor by written permission from the property owner. The Contractor shall restore any damage or disruption to other properties utilized in the performance of this Project to an equal or better than pre-construction condition at no cost to the City. The Contractor shall indemnify and hold the City harmless from any claims or losses from damage or disruption of private property.

Contractor shall provide, at its expense and without liability to the City, any additional land and access thereto that may be required for temporary construction facilities or for storage of materials. All such costs will be considered incidental to the work and will not result in additional cost to the City. Contractor personnel shall not unnecessarily enter upon private property without the express written consent of the landowner. The Contractor shall provide the Project Manager with a copy of the written permission. The Contractor shall indemnify and hold the City harmless from any claims or losses related to Contractor trespassing.

105.01 STORAGE OF MATERIALS

The Contractor shall confine its equipment, apparatus, the storage of materials and operations of Contractor's workmen to limits indicated by law, ordinances, permits, or directions of the City and shall not encumber the Project site with materials or equipment not necessary for the Project.

105.02 LOADING OF STRUCTURES

The Contractor shall not load or permit any part of a structure to be loaded with a weight that will endanger the structure's safety. The Contractor shall enforce the Project Manager's instructions regarding signs, advertisements, fires, and smoke.

105.03 SANITARY PROVISIONS

The Contractor shall provide and maintain on the construction site at all times suitable sanitary facilities for use of those employed on this Contract without committing any public nuisance. All toilet facilities shall be subject to the approval of the El Paso County Public Health Department. All portable toilet facilities for this Project shall be kept on City or State right-of-way as directed by the Project Manager.

105.04 ACCIDENT PREVENTION

The Contractor shall be solely responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the Work. The Contractor shall submit to the City an acceptable, comprehensive Safety Plan for review prior to commencement of the Work. The Contractor shall take all necessary precautions for the safety of, and shall provide the necessary protection to prevent damage, injury, or loss to:

a.) All persons on or about the Site or who may be affected by the Work;

b.) All Work and materials and equipment to be incorporated therein, whether in storage on or off the Site; and

c.) Other property at the site or adjacent thereto, including buildings, real property, trees, shrubs, lawns, walks, pavements, roadways, structures, utilities, and underground facilities not designated for removal, relocation, or replacement in the course of the Work.

Notwithstanding the foregoing, the City reserves the right to direct the Contractor to stop work and correct an unsafe condition at any time that any person present at the job site identifies any unsafe condition or action. For this purpose only, any

person at the job site is authorized to act on behalf of the City, but such intermittent delay shall not be grounds for an increase in the Contract price or schedule.

Precaution shall be exercised at all times for the protection of persons, including employees, and property. The safety provisions of all Federal, State and Municipal laws and any other codes relating to the public safety, shall be strictly observed, and the Contractor shall, at all times, whether or not so specifically directed by the Project Manager, take the necessary precautions to ensure the protection of the public.

Piling, sheeting and shoring shall be utilized where required to prevent any excessive widening or sloughing of a trench which may be detrimental to human safety, traffic flow, a pipe being placed, trees, or to any existing structure.

Excavated materials shall be placed a safe distance from the sides of the trench. Heavy equipment shall not be used or placed near the sides of a trench unless the trench is adequately braced.

The Contractor shall not load or permit any part of a structure to be loaded with a weight that will endanger the structure's safety.

The Contractor shall designate a qualified and experienced safety representative at the Work site(s) whose duties and responsibilities shall be the prevention of accidents and the maintaining and supervising of safety plans and programs.

105.05 PROTECTION OF THE PUBLIC WORKS AND PROPERTY

The Contractor shall provide and maintain all necessary watchmen, barricades, lights, and warning signs and take all necessary precautions for the protection of the public. The Contractor shall continuously maintain adequate protection of all work from damage, and shall take all reasonable precautions to protect the City's property from injury or loss arising in connection with the Contract. The Contractor shall make good any damage, injury, or loss to their work and to the property of the City resulting from lack of reasonable protective precautions except such as may be due to errors in the Contract Documents, or caused by agents or employees of the City. The Contractor shall check all cautionary signs at least once a day during this Contract.

The Contractor shall continuously maintain adequate protection of all their work from damage and shall protect the City's and adjacent property from injury arising in connection with this Contract.

The Contractor will be responsible for any and all damage to property, public or private, that may be caused by its operations in the performance of this Contract, and the Contractor shall defend any suit that may be brought against itself or the

City on account of damage inflicted by its operations, and shall pay any judgments awarded to cover such damage and shall indemnify the City for any losses arising out of such damage or related claims.

The Contractor shall be responsible for the restoration of all existing surface or subsurface improvements damaged as a result of construction at no additional cost to the City.

105.06 PUBLIC ROADS

The Contractor in executing the work on this Project shall not unnecessarily impede or interfere with traffic on public highways or streets. Detours, including surfacing, guard rails, temporary bridges and culverts, as may be shown on the drawings, or ordered by the Project Manager to accommodate the general public, residents adjacent to the improvements, and the United States mail shall be provided and maintained by the Contractor in a good workmanlike manner. Any call out of City Barricade Crews shall be charged to and paid for by the Contractor.

All work done within the public right-of-way and/or easements requires n Traffic Control Plan approved by the City Traffic Engineering Division.

The Contractor shall provide and maintain in place all barricades, warning signs, lights and other safety devices required to protect the work, divert traffic, and warn pedestrians of open excavation, unfilled trenches, and other areas or conditions which might be hazardous or dangerous. Detour routings must first be submitted to the City Traffic Engineer for review and approval and shall be signed for the entire route of the detour as required to return the traffic to their street or origination. Detours shall be maintained throughout the period of construction in such a manner as to provide the least amount of disruption to normal traffic flow.

All signing and barricading shall conform to the latest editions of the following:

(a) Manual of Uniform Traffic Control Devices for Street and Highways (MUTCD)

(b) City of Colorado Springs Traffic Signage and Markings Manual

(c) City of Colorado Springs Construction Traffic Control Manual

The City Traffic Engineer may require flag persons or off-duty police officers for traffic direction.

105.07 PROTECTION OF EXISTING CURBS, GUTTERS AND DRIVEWAYS

The Contractor shall exercise care in protecting existing curbs, gutters and driveways. Curbs, gutters and driveways damaged by the Contractor's operations shall be removed and replaced by the Contractor at Contractor's expense.

105.08 PROTECTING AND REMOVING PLANTINGS

The Contractor shall protect all existing trees, shrubs and other plantings from above ground and root structure damage during the construction activities. Plantings which are considered to be slightly damaged shall be properly pruned and sealed according to accepted nursery practices. Contractor shall be liable for the costs of any unnecessary damage to plants or trees as determined by the Project Manager. Where plantings are in conflict with new work, as determined by the City Forester (plantings in the public right-of-way) or by the inspector or owner (plantings on private property), the Contractor shall at his expense remove the planting. The Contractor shall coordinate with the City Forester prior to working in the vicinity of plantings in the public right of way.

In all cases, the proper planting season shall be observed to assure proper establishment and growth of the plantings.

Tree branches shall be trimmed back to the trunk, all around, to a minimum height of 8’ above the adjacent walkway. Work shall be done only by a licensed Tree Service as provided in City Code Chapter 2, Article 3, Part 3.

105.09 PUBLIC CONVENIENCE AND SAFETY

The Contractor shall make every effort to minimize the inconvenience to property owners and to the traveling and pedestrian public, and shall conduct the Work to minimize obstruction to traffic and inconvenience to property owners affected by the Work.

The Contractor shall notify and coordinate the closing and construction of the driveways, curb, gutter and sidewalks with the Project Manager and the adjoining property owners in advance of Work in writing. The Contractor shall provide 72 hours written notice in advance of any construction that may affect access, parking and/or existing structures, including fences adjacent to that property.

Suitable access and parking will be maintained at all times. Access may be limited to half the existing driveway width for limited periods during concrete driveway and street construction. An additional verbal notice shall be provided to each business or property owner 30 minutes prior to the actual access drive closure.

Relocating of fences and structures shall be coordinated with property owners and shall include miscellaneous items including, but not limited to, utility services, street signs and mailboxes, sod replacement, sprinkler system modifications, control boxes, railroad tie walls, etc. If no such items are specifically included in the Contract, these items will be considered incidental to the work and are to be included in the unit prices. The Contractor shall coordinate the salvaging of any materials suitable for re-use with the City Inspector and, if on private property, with the respective property owners.

Any restrictions on street parking or traffic movement shall be coordinated with the City Traffic Engineer.

105.10 FAILURE TO MAINTAIN SAFE SITE

If the City becomes aware of failure to comply with applicable safety regulations, the Project Manager may inform the Contractor who shall take immediate steps to remedy the noncompliance. The Project Manager shall give written notification to the Contractor directing it to correct the unsafe acts or conditions. If the Contractor fails to comply with such a notification, the Project Manager may issue a Stop Work order in accordance with this Contract, and work shall only be resumed after adequate corrective actions have been taken to correct the safety deficiencies the Contractor has been notified of. Stoppage of work because of noncompliance with prescribed accident precaution measures shall not be considered a changed condition or changes in work, nor reason for extension of completion time.

In case of injury to persons or property by reason of failure to erect and to maintain necessary barricades, safeguards, and signals, or by reason of any act or omission of the Contractor, or Contractor's subcontractors, agents, or employees, during the performance of this Contract, the City may withhold payments due the Contractor so long as shall be reasonably necessary to indemnify the City on account of any such injuries, but the City's payment or failure to pay any sum shall not be considered a waiver of its right to indemnity under the this Contract.

105.11 EROSION AND DRAINAGE CONTROL

Contractor shall provide for the drainage of stormwater and such water as may be applied or discharged on the site in performance of the work per the latest revision of the City of Colorado Springs Drainage Criteria Manual, Volume II. Drainage facilities shall be adequate to prevent damage to the work, the site, and adjacent property.

The Contractor shall prevent the pollution of drains and watercourses by sanitary waste, sediment, debris or other substances resulting from this work. Contractor shall be required to clean up and isolate such materials on a continuing basis to prevent risk of washing into such drainage ways.

Should the affected areas of the Project exceed one acre, a Stormwater Discharge Permit shall be required. Affected area includes excavations, material stockpiles and areas where equipment and vehicles disturb the ground. An exact definition of the affected area should be obtained from the Colorado Department of Public Health and Environment (CDPHE).

105.12 POLLUTION

The Contractor shall at all times ensure compliance with applicable Federal, State, and Municipal air, water, and noise pollution laws and ordinances. The Contractor shall at all times have the proper sprinkling equipment available and shall apply water in the amount determined by each site condition or as directed by the Project Manager. The Contractor shall obtain all necessary permits at Contractor's expense, which may include, but not be limited to, El Paso County or a State Air Emission permit, State of Colorado Construction Activity permit, State of Colorado Dewatering permit and Section 404 Corp of Engineers permit, unless otherwise specified in the RFP.

105.13 TEMPORARY CONSTRUCTION

All temporary facilities, including the Contractor's field office which it may maintain at the site, and additional offices erected by subcontractors, shall be neatly constructed and arranged on the site in an orderly manner. The Contractor shall prepare and submit to the Project Manager, for approval prior to starting work, a construction plan layout, showing arrangement of storage areas, temporary buildings, equipment, and work areas. The Contractor shall provide suitable weather-tight storage sheds of capacity required to contain all materials which might be damaged by storage in the open. The Contractor shall at all times keep copies of all Contract Documents readily accessible at its office at the site.

105.14 TEMPORARY WATER SUPPLY

The Contractor shall provide, at Contractor's own expense, temporary water connections and water supply necessary for the prosecution of the work and permit all contractors on the work to use this supply at a reasonable prorated charge, or by sub-metering. The Contractor shall pay for all water consumed in the work, and shall arrange with Colorado Springs Utilities for temporary connections and payment of service charges. Upon completion of the Contract work, all temporary waterlines shall be removed. The City will devise a method and plan to monitor and enforce the proper use of temporary water. The City will inspect for compliance.

105.15 TEMPORARY ELECTRICITY

The Contractor shall arrange with the Colorado Springs Utilities for temporary electricity necessary for the prosecution of the work. The Contractor shall pay for

all electric current consumed, and shall permit all contractors on the work to use this supply at a reasonable prorated charge, or by sub-metering.

105.16 TEMPORARY HEAT

The Contractor shall provide adequate, temporary heat required during construction. Until the building or work area is enclosed, heavy tarpaulin shall be used to enclose any space requiring heating or protection from weather during construction operations. After the heating plant is in operating condition and the building is enclosed, heat may be provided from the permanent heating plant if such is approved by the Project Manager. In such case, the Contractor shall arrange to operate the plant, connect permanent or temporary radiation or unit heaters, and so maintain the plant during operation that it will be turned over to the City undamaged at the completion of the work. The Contractor shall provide all fuel required. In no case shall salamander heating be used in finished or plastered surfaces; instead, gas-steam radiators, unit heaters, or other suitable and approved means shall be used if the permanent heating plant is not available. This applies only to structures. It does not apply to road improvements or other outdoor improvements.

105.17 TEMPORARY ENCLOSURES

The Contractor shall provide and maintain temporary enclosures for the work as may be required to permit continuation of interior work during inclement weather, if wall and roof construction has progressed sufficiently to make interior work possible. This applies only to structures. It does not apply to road improvements or other outdoor improvements.

105.18 CLEAN-UP

The Contractor shall at all times keep the work area including storage and staging areas, free from accumulations of waste materials. The Contractor is also responsible for any costs associated with cleanup of debris from the work site or storage areas that may inadvertently be scattered outside the area by weather or vandalism. Upon completion of the work, the Contractor shall leave the work area in a clean neat and orderly condition satisfactory to the Project Manager.

SECTION 106 ROYALTIES, PATENT INFRINGEMENTS, SPECIAL LICENSES AND PERMITS

106.00 ROYALTIES AND PATENTS

The Contractor shall pay all applicable royalties and license fees. The Contractor shall defend all suits or claims for infringement of any patent rights and save the City harmless from loss on account thereof except that the City may be responsible for any such loss when a particular process, design, or the product of a particular

manufacturer or manufacturers is specified, unless the City has notified the Contractor prior to the signing of the Contract that the particular process, design, or product is patented or is believed to be patented.

SECTION 107 WORK PROVISIONS AND RULES

107.00 COMMENCEMENT AND COMPLETION OF WORK

(a) Preconstruction Conference. After issuance of Notice to Proceed, or as otherwise established by the City, a preconstruction conference ("Preconstruction Conference") shall be held for review of the construction schedule, Contractor's written list of subcontractors and suppliers, written list of all required permits, project contracts, utility support plan, water control plan, Traffic Control Supervisor name and telephone number, gradations, test results, certifications, review procedures for handling shop drawings and other submittals, processing applications for payment, and other pertinent items.

(b) At the Preconstruction Conference, the Contractor shall furnish the Project Manager a written list of all permits required for the proper completion of the Contract. The list shall clearly identify the type of permit or permits that must be obtained before work on any particular phase or phases of work can be started.

(c) The Contractor shall commence work within ten (10) Calendar Days of the date specified on the Notice to Proceed and complete the Contract within the number of Calendar Days or by the date specified in the proposal form. Unless otherwise noted in the Contract, the number of days are Calendar Days.

(d) The dates fixed for commencement and completion of the work may be extended by the Project Manager. All requests for extension of time by the Contractor shall be made in writing to the Project Manager and shall set forth the reasons for such requests. The Project Manager may fix the period of extension, if any. In addition, the Project Manager may grant a period of extension upon an execution of a Change Order. Any Project Manager's decision on extensions of time shall be binding upon the parties hereto. Requests for extension of time received twenty (20) or more days after the occurrence of the delay will not be honored. No requests for extension of time shall be honored if submitted after the completion date.

(e) If satisfactory execution and completion of the Contract shall require work or materials in greater amounts or quantities other than those set forth in the Contract, then the Contract time may be adjusted at the time of the execution of the Change Order. No allowance will be made for delays or suspension of the prosecution of the work due to the fault of the Contractor.

107.01 FAILURE TO COMPLETE WORK ON TIME, LIQUIDATED DAMAGES

If the Contractor fails to fully perform and complete the work in conformity to the provisions and conditions of the Contract within the specified time limit set forth in the Contract, including any extensions granted hereto, the Contractor may be subject to a stop work order, as provided in this Contract. In addition, the Contractor shall pay to the City for each Calendar Day of delay until such time the Contract is complete, liquidated damages at the applicable daily rate below. The amounts shown are considered to be liquidated damages to reimburse the City for the additional cost of construction engineering and Contract administration services and in no case are considered a penalty.

Original Contract Amount	Amount of Liquidated Damages Per Day
Less than $50,000	$300.00
$50,000 to $100,000	$500.00
$100,000 to $500,000	$700.00
$500,000 to $1,000,000	$900.00
Over $1,000,000	$1500.00

107.02 WORK IN BAD WEATHER

No construction work shall be done during stormy, freezing, or inclement weather, except such as can be done satisfactorily, and in a manner to secure first class construction throughout, and then only subject to permission of the Project Manager.

The granting of a time extension for inclement weather does not imply or guarantee that additional compensation for incidental and appurtenant work caused by such weather will be approved or authorized by the Project Manager. Weather delays that can be reasonably anticipated shall not result in increased cost to the City. The Project Manager will be the sole judge as to the reasonableness of delays for inclement weather.

107.03 EXCUSABLE DELAYS

The Contractor's right to proceed will not be terminated, and the Contractor will not be charged with damages, for delays in completing the work that arise from unforeseeable causes beyond the control and without the fault or negligence of the Contractor. Examples of such causes include:

(a) Acts of God or of the public enemy,

(b) Acts of the government in either its sovereign or Contractual capacity,

(c) Acts of another contractor in the performance of a contract with the government,

(d) Fires,

(e) Floods,

(f) Epidemics,

(g) Quarantine restrictions,

(h) Strikes of employees other than Contractor's employees,

(i) Freight Embargos,

(j) Unusually severe weather, or

(k) Delays of subcontractors or suppliers at any tier arising from unforeseeable causes beyond the control and without the fault or negligence of both the Contractor and the subcontractors or suppliers.

107.04 COMPENSATION FOR COMPENSABLE DELAYS

If the Project Manager determines that a delay is compensable in accordance with the Contract, monetary compensation will be determined in accordance with this subsection.

(a) These categories represent the only costs that are recoverable by the Contractor. All other costs or categories of costs are not recoverable:

1. Actual, reasonable wages and benefits, including FICA, paid for additional non-salaried labor;

2. Reasonable and actual costs for additional bond, insurance and tax;

3. Increased, reasonable, and actual costs for materials;

4. Reasonable equipment costs calculated in accordance with the current edition of the Rental Rate Blue Book of Rental Rates for Construction Equipment for Contractor-owned equipment and based on invoice costs for rented equipment;

5. Reasonable and actual costs of extended job site overhead;

6. Reasonable subcontractor's claims (the same level of detail as specified herein is required for all subcontractors' claims)

7. An additional 10 percent will be added to the total of items (1), (2), (3), (4), (5), and (6) as compensation for items for which no specific allowance is provided, including profit, overhead, and general and administrative expenses.

(b) In adjustment for costs as allowed above, the City will have no liability for the following items of damages or expense:

1. Profit in excess of that provided in (a) above;

2. Loss of profit;

3. Additional cost of labor inefficiencies in excess of that provided in (a) above;

4. Home office or other overhead or general and administrative expenses in excess of that provided in (a) above;

5. Consequential damages, including but not limited to loss of bonding capacity, loss of bidding opportunities, and insolvency;

6. Indirect costs or expenses of any nature in excess of that provided in (a) above;

7. Attorney's fees, claim preparation fees, and expert fees.

All costs claimed must be documented and accompanied by a written certification from the Contractor.

107.05 EMERGENCY WORK

In an emergency affecting the safety of life or of the work or of adjoining property, the Contractor is, without special instructions or authorization from the Project Manager, hereby permitted to act at Contractor's discretion to prevent such threatening loss or injury. Contractor shall also act, without appeal, if so authorized or instructed by the Project Manager. Any reasonable compensation claimed by the Contractor on account of emergency work shall be determined by mutual agreement or in accordance with the Changes provision of this Contract.

107.06 VALUE ENGINEERING CHANGE PROPOSALS BY THE CONTRACTOR

The Contractor is encouraged to develop and offer proposals for improved construction techniques, alternative materials and other innovations. Proposals

must provide a project comparable to the City's original design either at lower cost, with improved quality, or both. If a Value Engineering Change Proposal (VECP) Proposals shall be submitted only after contract award. If a VECP is rejected, the work shall be completed in accordance with the Contract at the Contract price. The Contractor shall have no claim against the City for compensable or noncompensable delay to the Contract based on the failure to respond to a VECP.

The Contractor may submit either a full VECP or a preliminary Conceptual VECP, followed by a full proposal. The City Engineer will provide timely review of all VECPs and advise the Contractor whether the VECP is complete or incomplete. When the VECP is complete, the Project Manager will advise the Contractor of either the approval of the VECP or the reasons for rejection of the VECP.

Cost savings generated to the Contract as a result of VECPs offered by the Contractor and accepted by the Project Manager shall be shared equally between the Contractor and the City.

If the Project Manager determines that the time for response indicated in the submittal under item (c)5 below is insufficient for review, the Contractor will be promptly notified. Based on the additional time needed by the Project Manager for review and the effect on the Contractor's schedule caused by the added time, the Project Manager will evaluate the need for a non-compensable time adjustment to the Contract.

(a) VECPs that will be considered are those that would produce savings to the City or provide improved Project quality without impairing essential functions and characteristics of the Project. Essential functions include but are not limited to: service life, economy of operation, ease of maintenance, desired appearance, safety, and impacts to the traveling public or to the environment during and after construction.

(b) *Submittal of Conceptual Proposal.* For VECPs that require a significant amount of design or other development resources, the Contractor may submit an abbreviated conceptual proposal for preliminary evaluation. The Project Manager will evaluate the information provided and advise the Contractor if any conditions or parameters of the conceptual proposal are found to be grounds for rejection. Preliminary review of a conceptual proposal reduces the Contractor's risk of subsequent rejection but does not commit the City to approval of the full VECP. The following information shall be submitted for each conceptual proposal.

1. A statement that the proposal is submitted as a conceptual VECP.

2. A general description of the difference between the existing Contract and the proposed change, and the advantages and disadvantages of each, including effects on cost, service life, economy of operation, ease of

maintenance, desired appearance, safety, and impacts to the traveling public or to the environment during and after construction.

3. A set of conceptual plans and a description of proposed changes to the Contract specifications.

4. An estimate of the anticipated cost savings or increase.

5. A statement specifying:

   a. when a response to the conceptual proposal from the City is required to avoid delays to the existing contract prosecution,

   b. the amount of time necessary to develop the full Proposal,

   c. the date by which a Change Order must be executed

      to obtain maximum benefit from the VECP, and

   d. the VECP's impact on time for completing the Contract.

(c) *Submittal of Full Value Engineering Change Proposal.* The following materials and information shall be submitted with each VECP.

1. A statement that the proposal is submitted as a VECP.

2. A description of the difference between the existing Contract and the proposed change, and the advantages and disadvantages of each, including effects on service life, economy of operation, ease of maintenance, desired appearance, safety, and impacts to the traveling public or to the environment during and after construction.

3. A complete set of plans and specifications showing the proposed revisions relative to the original Contract. This portion of the submittal shall include design notes and construction details. The proposed plans and specifications shall be signed and sealed by the Contractor's engineer.
4. A complete analysis indicating the final estimated costs and quantities to be replaced by the VECP compared to the new costs and quantities generated by the VECP. All costs and proposed unit prices shall be documented by the Contractor.

5. A statement specifying the date by which a Change Order must be executed to obtain the maximum cost reduction during the remainder of the Contract.

6. A statement detailing the effect the VECP will have on the time for completing the Contract.

7. A description of any previous use or testing of the proposed changes and the conditions and results. If the VECP was previously submitted on another City project, the VECP shall indicate the date, Contract number, and the action taken by the City.

8. An estimate of any effects the VECP will have on other costs to the City.

9. A statement of life cycle costs, when appropriate. Life cycle costs will not be considered as part of cost savings but shall be calculated for additional support of the VECP. A discount rate of four percent shall be used for life cycle calculations.

10. A statement specifying when a response from the City is required to avoid delays to the prosecution of the Contract.

(d) *Evaluation.* VECPs will be evaluated in accordance with the following:

1. The Project Manager will determine if a VECP qualifies for consideration and evaluation. The Project Manager may reject any VECP that requires excessive time or costs for review, evaluation, or investigations. The Project Manager may reject proposals that are not consistent with the City's design policies and criteria for the Project.

2. VECPs, whether or not approved by the City, apply only to this Contract and become the property of the City. VECPs shall contain no restrictions imposed by the Contractor on their use or disclosure. The City has the right to use, duplicate and disclose in whole or in part any data necessary for the utilization of the Proposal. The City retains the right to utilize any accepted VECP or part thereof on other projects without obligation to the Contractor. This provision is subject to rights provided by law with respect to patented materials or processes.

3. If the City is able to demonstrate that it is already considering certain revisions to the Contract, prior to receipt of the VECP, or has approved certain changes in the Contract for general use that are subsequently proposed in a VECP, the Project Manager will reject the VECP and may proceed to implement these changes without obligation to the Contractor.

4. The Contractor shall have no claim against the City for additional costs or delays resulting from the rejection or untimely acceptance of a VECP. These costs include but are not limited to: development costs, loss of anticipated profits, increased material or labor costs, or untimely response.

5. VECP will be rejected if equivalent options are already provided in the Contract.

6. VECP that only reduce or eliminate Contract pay items will be rejected.

7. The savings generated by the VECP must be sufficient to warrant a review and processing, as determined by the Project Manager.

8. A VECP changing the type or thickness of the pavement structure or changing the design of a bridge will be rejected.

9. Additional information needed to evaluate VECPs shall be provided in a timely manner. Untimely submittal of additional information will result in rejection of the VECP. Where design changes are proposed, the additional information shall include results of field investigations and surveys, design and computations, and changed plan sheets required to develop the design changes.

(e) *Payment.* If the VECP is accepted, the changes and payment will be authorized by a Change Order. Reimbursement will be made as follows:

1. The changes will be incorporated into the Contract by changes in quantities of unit items, new agreed unit price items, or both, as appropriate, under the Contract.

2. The Price of the contract will be revised to reflect the changes in the VECP. The City will pay the Contractor 50 percent of the savings to the City upon completion of the Project. The savings to the City shall be the difference between the cost of the revised work and the cost of the related construction required by the original Contract computed at Contract prices.

3. Costs incurred by the Contractor for development, design, and implementation of the VECPs will not be reimbursed.

4. When work performed under an approved VECP is modified to fit field or other conditions, the maximum amount paid for the work will be limited to that which would have been paid if the work had been performed under the original Contract provisions. The rejection or limitation of reimbursement shall not constitute the basis of any claim against the City for delay or for other costs except as allowed under the original Contract.

107.07 AUTHORITY OF THE PROJECT MANAGER

The Project Manager will decide all questions regarding the quality and acceptability of materials furnished, work performed, and the rate of progress of the work, all interpretation of the plans and specifications, and the acceptable

fulfillment of the Contract. The Project Manager will perform technical inspection of the work and shall have authority to reject all work and materials which do not conform to the Contract.

The Project Manager has authority to stop the work whenever such stoppage may be necessary to insure the proper execution of the Contract or for the convenience of the City. The Project Manager may order the Contractor, by giving ten (10) days written notice, to suspend, delay, or interrupt all or any portion of the work required by the Contract for a period of up to (10) ten Calendar Days at no additional cost to the City. The Project Manager may immediately stop the work when it is determined that the public's safety and welfare is in jeopardy.

The Project Manager will, within a reasonable time after their presentation to the Project Manager, make decisions in writing on all claims submitted to the City by the Contractor and on all other matters relating to the execution and progress of the work or the interpretation of the Contract Documents. The Project Manager's decisions shall be final.

107.08 DUTIES OF THE INSPECTOR

Inspectors employed by the City are authorized to inspect all work done and materials furnished. Any such inspection may extend to all or any part of the work and to the preparation, fabrication or manufacture of the materials to be used. An inspector is not authorized to alter or waive the provisions of the Contract. An inspector is not authorized to issue instructions contrary to the provisions of the Contract or to act as foreman for the Contractor.

107.09 CONSTRUCTION OBSERVATION AND INSPECTION

The Project Manager shall at all times have access to the work, and the Contractor shall provide proper equipment, materials and labor as required for such access and inspection.

All equipment, material, and articles incorporated into the work covered by this Contract shall be new and of the most suitable grade for the purpose intended, unless otherwise specifically provided in this Contract. The Project Manager shall have the right to reject materials and workmanship, which are defective, or require their correction. Rejected workmanship shall be satisfactorily corrected and rejected materials shall be removed from the premises and replaced without charge to the City. If the Contractor does not correct such rejected work and remove rejected materials within a reasonable time fixed by written notice, the City may remove them and charge the expense to the Contractor.

Should it be considered necessary or advisable by the Project Manager at any time before final acceptance of the entire work to make an examination of work already

completed, by removing or tearing out same, the Contractor shall on request promptly furnish necessary facilities, labor and materials. If such work is found to be defective in any material respect due to fault of the Contractor or his subcontractors, he shall defray all the expenses of such examination and of satisfactory reconstruction. If, however, such work is found to meet the requirements of the Contract, the actual, reasonable cost of labor and material necessarily involved in the examination and replacement, plus ten (10) percent, will be allowed the Contractor.

All materials to be incorporated in the work, all labor performed, all tools, appliances, and methods used shall be subject to the inspection and approval or rejection of the Project Manager.

If the Project Manager points out to the Contractor, Contractor's foreman, or agent any neglect or disregard of the Contract provisions, such neglect or disregard shall be remedied and further defective work be discontinued immediately.

The Contractor shall execute the work only in the presence of the Project Manager or authorized representative, unless provision has been made for the work to proceed without complete engineering supervision or inspection. The presence of the Project Manager or authorized representative shall in no way relieve the Contractor of any responsibility under this Contract.

The observation of the work by the Project Manager is intended to aid the Contractor in applying labor, materials, and workmanship in compliance with the Contract provisions. Such observation, however, shall not relieve the Contractor from any of Contractor's Contract obligations.

107.10 CONTRACTOR COOPERATION

All work under this Contract shall be performed in a skillful and professional manner. The Project Manager shall have the authority to order the Contractor to remove from the work site any employee the Project Manager deems incompetent, careless, or otherwise objectionable to the general public or the City by notify the Contractor of such order in writing.

(a) Workmen, Methods and Equipment: Permission from the Project Manager to use any particular methods, equipment or appliances shall not be so construed as to relieve the Contractor from furnishing other equipment or appliances or adopting other methods when those in use prove unsatisfactory to the Project Manager, or as to bind the Project Manager to accept work which does not comply with the Contract.

107.11 CONTRACTOR'S RESPONSIBILITY FOR WORK

Until the work is accepted by the Project Manager as evidenced by the issuance of the Certificate of Completion, the Contractor shall have the charge and care thereof and shall take every necessary precaution against injury or damage to any part thereof by action of the elements or from any other cause, whether arising from the execution or from the non-execution of the work. The Contractor shall rebuild, repair, restore, and make good all injuries or damages to any portion of the work occasioned by any of the above causes before its completion and acceptance and shall bear the expense thereof.

The Contractor shall be responsible for the preservation of all public and private property, trees, fences, monuments, and other property, along and adjacent to the improvements and shall use suitable precautions necessary to prevent damage to pipes, conduits, and other underground structures. When or where any direct or indirect damage or injury is done to public or private property by or on account of any act, omission, neglect or misconduct in the execution of the work, or inconsequence of the non-execution thereof on the part of the Contractor, such property will be restored by the Contractor and at Contractor's expense to a condition similar, or equal to that existing before such damage or injury to the satisfaction of the City's Project Manager.

It shall be the responsibility of the Contractor, when moving or operating equipment, to make all arrangements for temporary crossings of telephone, transmission, pipe lines, railroad tracks, and irrigation ditches. This work shall not be paid for as a separate item but shall be considered as incidental to the project.

107.12 PROTECTION OF UTILITIES

The Contractor's attention is directed to the fact that utilities may encroach on the construction of this Project, and also to the importance of protecting all public/private utilities encountered on this project. These may include telecommunications, cablevision, traffic signal lines, power lines, water lines, sewer lines, gas lines, railroad tracks, and other overhead and underground utilities.

The City does not warrant any survey work or location of utilities or other underground apparatuses whether performed by the City, its agent, or an independent contractor. Contractor understands and agrees any survey or location work performed by the City, its agent, or other independent contractor is provided for guidance purposes only, so as to show the approximate location of underground utilities or apparatuses. Contractor understands the existence or exact location of underground utilities or apparatuses may not be known to the City or the design engineer of record. Contractor, therefore, agrees that it shall verify the existence and location of any underground utilities or apparatus along the route of work. Verification shall be done by potholing or using other methods which will

detect the exact depth, dimensions, and location of any underground utilities or apparatus.

Contractor shall be liable for any damages, loss, or claims of whatsoever kind caused by its failure to pothole or use other methods of identifying the exact depth, dimensions, and location of any underground utilities or apparatus. Contractor agrees that any claim of any kind whatsoever, damages, loss, lawsuit, demand, or request for equitable adjustment ("Claims"), shall be waived and the City shall be forever released and discharged from such Claims if Contractor fails to comply with its obligations under this section. Contractor agrees that if it fails to maintain all records or other evidence establishing that it potholed or otherwise determined the exact location, depth, and dimensions of all underground utilities and apparatuses, then it shall not be permitted to make any Claim arising from or related to the location of underground utilities or apparatus.

The size and location of all existing utilities as known to the Project Manager have been noted on the plans for the information and guidance of the Contractor. The Contractor shall be responsible for the location and protection of all utilities located within his working area regardless of whether or not their existence or location is shown or noted on the drawings.

It is the Contractor's responsibility to complete required work and to schedule inspections during normal working hours. The Contractor is responsible for contacting each affected utility for their inspectors' working hours. The Contractor is responsible to request an inspection two (2) working days in advance of the inspection. In the case of an overtime inspection, the request must be in writing. All overtime costs for inspection by Colorado Springs Utilities, or other utilities personnel, shall be the Contractor's expense. The City will not entertain any requests for time extensions for delays caused by the Contractor's failure to properly notify the affected utility of a required inspection or the Contractor's failure to complete the required work by the time of the scheduled inspection.

Any information concerning underground utilities shown on the drawings is intended to be merely an aid to the Contractor. The accuracy of information with respect to underground utilities is not guaranteed. The Contractor shall make their own investigation, including exploratory excavations, to determine the locations and type of existing mains or service laterals or appurtenances when their presence can be inferred from the presence of other visible facilities, such as building, manholes, inlets, meters and junction boxes, on or adjacent to the site of the work. If the Contractor discovers utility facilities not identified in the plans or specifications or in a position different from that shown in the plans and specifications, the Contractor shall immediately notify, verbally and in writing, the Project Manager and Owner of the utility facility.

Before any excavation is begun in the vicinity of water lines, railroad tracks, or structures, sewer lines, telecommunication conduits or cablevision line, each utility

company, including Colorado Springs Utilities (if applicable), department, or company concerned must be notified in advance of such excavation, and such excavation shall not be made until an authorized representative of the utility concerned is at the site.

All utilities encountered must be kept in operation by the Contractor and must be protected and/or repaired at the Contractor's own expense, unless otherwise specified in the Contract documents. The Contractor shall be held liable for all damages to any and all public utilities encountered on the project, which damages are due to the Contractor's operations. Such damages shall include all physical damages to utilities and also all damages due to interruption of service of such utilities, when such damages and interruptions are caused by the Contractor's operations.

Where alterations or moving of utilities is not required to permit construction of the project, the Contractor shall take such measures as the Project Manager may direct to properly protect these utilities throughout his construction operations and shall cooperate at all times with the proper authorities and/or owners in maintaining service of railroads, conduits, pole lines, transmission lines, pipe lines, sewers, etc., affected by this project.

The costs of damages due to the Contractor's operation shall not be allowable under this Contract and shall result in no additional cost to the City. The cost of protecting utilities where alteration or relocation is not required to permit construction of the project shall be considered as included in the original Contract price for the project and shall result in no additional cost to the City.

Should any pipe line, water lines, or gas mains, electrical conduits, sewer pipes, overhead wiring, telecommunication lines, power lines, or any other such utilities, not specifically mentioned and provided for elsewhere as a part of this Contract, have to be moved, repaired, reconditioned, or revised due to the construction, or moved temporarily to permit construction of the project the party or parties owning and operating such utilities shall perform the actual work of moving, repairing, reconditioning, or revising such utilities. Any such work would be added via change order, and the cost of this work will be borne by Colorado Springs Utilities, the utility companies involved, or other means arranged by the City.

(a) Existing Utilities

1. Existing Gas Lines: As of April 1, 1983, Federal law requires anyone who uncovers a gas line to report it to the gas company and allow it to be inspected by the gas company personnel before it is backfilled. Colorado Springs Utilities or other provider is to be notified prior to any excavation around gas lines. A Colorado Springs Utilities. or other applicable provider. inspector is to be notified and present on site prior to construction activities around gas lines.

2. Existing Sewer Mains and Services: All relocation, replacement protection shown on the plans or determined necessary by the inspector shall be performed according to the latest Colorado Springs Utilities Wastewater Standard Specifications. Minimum 48 hours' notice must be given to Colorado Springs Utilities prior to any related work.

3. The Contractor shall adjust sanitary sewer manhole rims to an elevation acceptable to Colorado Springs Utilities. The Contractor shall contact Colorado Springs Utilities twenty-four (24) hours prior to manhole rim adjustments.

4. Existing Water Mains and Services: All relocation, replacement or protection shown on the plans or determined necessary by the inspector shall be performed according to the latest Colorado Springs Utilities Water Standard Specifications and the Water Service Standard Specifications. Minimum 48-hour notice must be given to Colorado Springs Utilities prior to any related work. Colorado Springs Utilities reserves the right to schedule any operations at their discretion and to provide for any requirements determined necessary to perform the work. The Contractor shall coordinate with the Colorado Springs Utilities and receive their approval prior to performance of the work.

(b) Utility Support Systems:

1. If required by the Contract documents, or requested by the Project Manager, the Contractor shall submit shop drawings for the method of temporary support for all existing utilities during construction. The temporary support details for existing utilities shall be submitted for review and approval prior to performance of the work. Shop drawings must bear the seal of a Professional Project Manager registered in the State of Colorado, unless so waived by the City.

2. Regardless of City approved shop drawings, the Contractor shall be responsible for the satisfactory support of the utility system and any damages that may occur to the utility involved.

(c) Electric Utility Installation:

1. Any electric facilities unless otherwise noted are to be relocated or modified by Colorado Springs Utilities. The Contractor shall coordinate the work with Colorado Springs Utilities and Colorado Springs Utilities Contractor.

2. Light Pole Installation or Relocation:

a. The Contractor is responsible for coordinating with Colorado Springs Utilities, removing existing light pole foundations, constructing new light pole foundations, installing new conduits, and installing lighting junction boxes. The Contractor is responsible for coordinating with Colorado Springs Utilities for the de-energizing and removal of existing light poles.

b. Colorado Springs Utilities will remove the existing light standards, reset the light standards upon completion of the new foundations, conduit and junction boxes, pulling wire, and beginning operations of the lighting within the project limits. The Contractor is responsible for scheduling and coordination with Colorado Springs Utilities crews for reinstallation and re-energizing completed light poles.

(d) Gas Utilities: The Contractor is responsible for coordinating with Colorado Springs Utilities for the relocation of existing Gas lines. Colorado Springs Utilities will relocate the existing gas lines as necessary to install project improvements within the project limits. The Contractor is responsible for scheduling and coordination with Colorado Springs Utilities crews.

(e) Telecommunication Agencies: Any telephone facilities unless otherwise noted are to be relocated or modified by the respective private utility company. The Contractor shall coordinate the work with the respective private utility company.

(f) Cablevision: The television utilities are to be relocated by the cable provider. The Contractor shall coordinate the work with any affected cable provider.

107.13 FEDERAL FUNDS

If this Contract is a federally assisted construction contract all applicable federal requirements, terms and conditions, provisions and forms shall apply. Additionally, during the performance of this Contract, the Contractor agrees as follows:

1. The Contractor will not discriminate against any employee or applicant for employment because of race, color, religion, sex, sexual orientation, gender identity, or national origin. The Contractor will take affirmative action to ensure that applicants are employed, and that employees are treated during employment, without regard to their race, color, religion, sex, sexual orientation, gender identity, or national origin. Such action shall include, but not be limited to the following: employment, upgrading, demotion, or transfer; recruitment or recruitment advertising; layoff or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship. The Contractor agrees to post in conspicuous places,

available to employees and applicants for employment, notices to be provided by the contracting officer setting forth the provisions of this nondiscrimination clause

2. The Contractor will, in all solicitations or advancements for employees placed by or on behalf of the Contractor, state that all qualified applicants will receive consideration for employment without regard to race, color, religion, sex, sexual orientation, gender identity, or national origin.

3. The Contractor will not discharge or in any other manner discriminate against any employee or applicant for employment because such employee or applicant has inquired about, discussed, or disclosed the compensation of the employee or applicant or another employee or applicant. This provision shall not apply to instances in which an employee who has access to the compensation information of other employees or applicants as a part of such employee's essential job functions discloses the compensation of such other employees or applicants to individuals who do not otherwise have access to such information, unless such disclosure is in response to a formal complaint or charge, in furtherance of an investigation, proceeding, hearing, or action, including an investigation conducted by the employer, or is consistent with the contractor's legal duty to furnish information.

4. The Contractor will send to each labor union or representative of workers with which he has a collective bargaining agreement or other Contract or understanding a notice advising the labor union or workers representative of the Contractor's commitments under Section 202 of Executive Order No. 11246 of September 24, 1965, and shall post copies of the notice in conspicuous places available to employees and applicants for employment.
5. The Contractor will comply with all provisions of Executive Order 11246 of September 24, 1965, and of the rules, regulations, and relevant orders of the Secretary of Labor.

6. The Contractor will furnish all information and reports required by Executive Order 11246 of September 24, 1965, and by the rules, regulations and orders of the Secretary of Labor, or pursuant thereto, and will permit access to his books, records, and accounts by the Secretary of Labor, State of Colorado Civil Rights Commission and any other governmental agency entity which may be assisting with the funding under this Contract for purposes of investigation to ascertain compliance with such rules, regulations and orders.

7. In the event of the Contractor's noncompliance with the nondiscrimination clauses of this Contract or with any such rules, regulations, or orders, this Contract may be cancelled, terminated, or suspended in whole or in part, and the Contractor may be declared ineligible for further government Contracts or Federally assisted

construction Contracts in accordance with the procedures authorized in Executive Order No. 11246 of September 24, 1965, and such other sanctions may be imposed and remedies invoked as provided in Executive Order No. 11246 of September 24, 1965, or by rule, regulation, or order of the Secretary of Labor, or otherwise provided by law.

8. The Contractor shall include the provisions of Paragraphs (1) through (8) in every subcontract or purchase order unless exempted by rules, regulations, or orders of the Secretary of Labor issued pursuant to Section 204 of Executive Order No. 11246 of September 24, 1965, so that such provisions will be binding upon each subcontractor or vendor. The Contractor will take such action with respect to any subcontract or purchase order as the city, state, or any federal governmental entity may direct as a means of enforcing such provisions, including sanctions for noncompliance. Provided, however, that in the event the Contractor becomes involved in, or is threatened with, litigation with a subcontractor or vendor as a result of such direction, the Contractor may request the city, the state, or the United States to enter into such litigations to protect the interests of such governmental entity.

107.14 SUPERINTENDENCE

The Contractor shall give the work the constant attention necessary to facilitate the progress thereof and shall cooperate with the Project Manager and with other contractors or Colorado Springs Utilities employees in every way possible. The Contractor shall have at all times, on the work, as Contractor's agent, a competent superintendent capable of reading and thoroughly understanding the Plans and Specifications, and who shall have the necessary authority to receive and promptly execute the instructions and orders from the Project Manager or the Project Manager's authorized representative. Such superintendent shall be furnished irrespective of the amount of work sublet. The Contractor shall supply the Project Manager with a list of phone numbers at which the Contractor and its superintendent and foreman can be reached at any time. The assigned superintendent must adhere to the cooperation requirements specified in this Contract and is subject to removal if so ordered in writing by the Project Manager.

107.15 PREPARATION

All vegetation, stumps, and debris and other objectionable objects shall be removed from the area staked out by the Project Manager, and where necessary from the area immediately adjacent thereto. Such debris shall be hauled from the site of the construction and wasted as directed by the Project Manager.

107.16 STAKING WORK

The Project Manager may provide reference points (horizontal and vertical control) only, unless otherwise noted in the proposal and project specifications. The Contractor shall engage the services of a licensed surveyor or surveying firm (hereinafter referred to as the Surveyor) to be approved by the Project Manager. The Surveyor shall perform all detailed construction layout and staking including the staking of all storm sewer, street improvements, and utility relocations in accordance with the plans and specifications. The Contractor shall be responsible for the correctness and accuracy of the detailed layout of finished structures.

Any instrument man or survey assistant employed on the work by the Contractor or his subcontractors, who are judged by the Project Manager to be incompetent, shall be removed from the work and replaced by a competent individual.

107.17 DEVIATION ALLOWED

Finished surfaces in all cases shall conform to lines, grades, cross sections and dimensions shown on the approved drawings or described in the Specifications. Deviations from the approved drawings and working drawings as may be required by the expediencies of construction, in all cases, must be determined by the Project Manager and authorized in writing. If the Project Manager deems it inexpedient to correct work injured or done in an unauthorized manner, an equitable deduction from the Contract price of the work done shall be made by the Project Manager subject to approval of the City Procurement Services Manager.

107.18 RIGHT-OF-WAY

The City's right-of-way will in general be adequate for construction purposes. Nothing marked on the drawings shall be interpreted as giving the Contractor exclusive occupancy of the territory provided by the City. The City and its employees for any purpose, and other contractors of the City, for any purpose required by their respective contracts, may enter upon or occupy any portion of the land furnished by the City. When the territory of one contract is a necessary or convenient means of access for the execution of another contract, such privileges of access or any other reasonable privilege shall be granted by the Contractor to the extent, amount, in the manner and at times necessary. No such joint occupancy or use of the territory shall be made as the basis of any claim for delay or damages.

107.19 SHOP DRAWINGS AND SUBMITTALS

The Contractor shall submit to the Project Manager all shop drawings and submittals required for the work, including those pertaining to structural and reinforcing steel within fifteen (15) Calendar Days from the date of the Notice of

Award. The Contractor shall make any corrections in the drawings required by the Project Manager and resubmit the same without delay.

Three final copies of all shop drawings (if applicable), submittals (if applicable) and schedules shall be submitted to the Project Manager, who after checking will retain two copies and return one copy to the Contractor. The Project Manager's approval of shop drawings of equipment and material shall extend only to determining the conformity of such equipment and materials with the general features of the design drawings prepared by the Project Manager. It shall be the responsibility of the Contractor to determine the correctness of all dimensions and minor details of such equipment and materials so that when incorporated in the work, correct operations will result.

107.20 RECORD DRAWINGS

The Contractor shall maintain an up-to-date set of Contract drawings and Contract records, legibly marked; depicting all constructed improvements at the site or as otherwise specified and shall submit a complete set labeled "Project Record" to the Project Manager upon completion of the Project.

(a) Drawings:

1. Depths of various elements of foundation in relation to finish floor datum.

2. Horizontal and vertical locations of underground utilities and appurtenances, referenced to permanent surface improvements and Project survey control.

3. Location of internal utilities and appurtenances concealed in the construction, referenced to permanent surface improvements and project survey control.

4. Field changes of dimensions and detail.

5. Changes made by Change Order.

6. Details not on original Contract drawings.

(b) Specifications and Addenda:

1. Manufacturer, trade name, catalog number, and supplier of each product and item of equipment actually installed.

2. Changes made by Change Order.

107.21 MATERIALS

Unless otherwise stipulated in the Specifications, all workmanship, equipment, materials, and articles incorporated in the work covered by this Contract are to be new and of the best grade of their respective kinds for the purpose. The Contractor shall furnish to the Project Manager for the Project Manager's approval, the name of the manufacturer of machinery, mechanical and other equipment, which he contemplates installing, together with their performance capacities and other pertinent information including but not limited to instruction manuals pertaining to the use and operation of such machinery, mechanical and other equipment.

When required by the Specifications, or when called for by the Project Manager, the Contractor shall furnish for approval full information concerning the materials or articles which he contemplates incorporating in the work. Samples of materials shall be submitted for approval when so directed. Machinery, equipment, materials, and articles installed or used without such approval shall be at the risk of subsequent rejection.

107.22 MATERIAL INSPECTION AT PLANT

If the Project Manager inspects the materials at the source, the following conditions shall be met:

(a) The Project Manager shall have the cooperation and assistance of the Contractor and the materials producer.

(b) The Project Manager shall have full entry to all parts of the plant necessary for the manufacture or production of the materials being furnished.

(c) Adequate safety measures shall be provided and maintained.

The City reserves the right to retest all materials which have been previously tested or inspected. The retesting may be prior to or after incorporation of the materials into the work. Those materials inspected and tested after delivery on the Project or after incorporation into the work that do not meet the requirements of the Contract will be rejected and replaced at no additional cost to the City.

107.23 HANDLING MATERIALS

All materials shall be handled so their quality and fitness for the work is preserved. Aggregates shall be transported to the work in vehicles constructed to prevent loss or segregation of materials.

107.24 CITY FURNISHED MATERIALS

Material furnished by the City will be made available to the Contractor at the points specified in the Contract.

The cost of handling and placing materials after they are made available to the Contractor shall be considered as included in the Contract price for the item, and shall result in no additional cost to the City.

The Contractor will be held responsible for all material received until it is incorporated into the work and accepted.

Demurrage charges resulting from the Contractor's failure to accept the material at the designated time and point of delivery will be deducted from monies due the Contractor.

107.25 BUY AMERICA REQUIREMENTS

All manufacturing processes, including the application of a coating, for all steel and iron products permanently incorporated in the work shall have occurred in the United States of America. All manufacturing processes are defined as "processes required to change the raw ore or scrap metal into the finished, in-place steel or iron product". This requirement will not prevent a minimal use of foreign steel or iron provided the total project delivered cost of all such steel and iron which includes the cost of delivering the steel and iron to the Project, does not exceed one-tenth of one percent of the total Contract cost or $2,500, whichever is greater.

With every steel or iron product that requires pre-inspection, pretesting, certified test results, or certificate of compliance, the Contractor shall provide a certification by each supplier, distributor, fabricator, and manufacturer that has handled the steel or iron product that every process, including the application of a coating, performed on the steel or iron product either has or has not been carried out in the United States of America. These certifications shall create a chain of custody trail that includes every supplier, distributor, fabricator, and manufacturer that handles the steel or iron product. The lack of these certifications will be justification for rejection of the steel or iron product. Upon completion of the Project, the Contractor shall certify in writing of compliance with this requirement and provide evidence of the Project delivered cost of all foreign steel or iron permanently incorporated into the Project.

107.26 TESTING OF MATERIALS

Tests and Inspections. The City will employ and pay for the services of an approved testing laboratory to perform specified services for the field testing of:

(a) Soil Compaction Control

(b) Cast-in-Place Concrete

(c) Asphalt Concrete Pavement

The Contractor shall perform, or arrange for the performance, and pay all costs in connection therewith, all other tests and inspections required by the Contract documents. The Contractor shall pay for all testing laboratory services in connection with tests verifying conformance of proposed materials and installation with project requirements including, but not limited to, mix designs, riprap, gradation tests for embedment, fill and backfill materials. The City shall pay for testing laboratory services in connection with tests on materials after incorporation into the project, unless retesting of materials is necessary because of the failure of the materials to meet the Project requirements. The Contractor shall obtain the City's written acceptance of the testing laboratory before having services performed.

(a) Requirements for Independent Testing Consultants.

1. Consultants shall comply with "Recommended Requirements for Independent Laboratory Qualifications", latest edition, published by the American Council of Independent Laboratories, and basic requirements of ASTM E-329, "Standards of Recommended Practice for Inspection and Testing Agencies for Concrete, Steel, and Bituminous Materials as Used in Construction", latest edition.

2. The Contractor shall submit to the City for prior approval, the name and address of the proposed testing laboratory with description of personnel, facilities, equipment and other qualification data, including certificate of calibration of applicable testing equipment made by an accredited calibrated agency no more than twelve (12) months prior to submittal date.

(b) Test Reports

1. Testing agency shall be instructed to submit directly to the City three (3) copies of all reports of tests or inspections made, showing compliance, irregularities or deficiencies, identifying Project, date of test, location in Project, applicable specification section, applicable standard(s) for compliance, observations relating to compliance, name and signature of inspector.

(c) Contractor Responsibilities

1. Furnish access to the work, materials, equipment and labor required to accommodate inspections and tests when testing laboratory is retained by the City. In the event retesting of materials or recompaction is

necessary because of the failure of the materials or compaction to meet the Project requirements, the cost of said retesting shall be borne by the Contractor. Cost of said retest will be deducted from the final payment amount due the Contractor, or invoiced directly to the Contractor at the City's discretion.

(d) Reliance on Technical Data

Without warranty or representation as to the accuracy or completeness of any information or data, Contractor may rely upon the general accuracy of the “technical data” contained in the reports, specifications and drawings. The “technical data” is identified in the work technical specifications, drawings and reports that are signed and sealed by a registered Professional Engineer, Architect or Landscape Architect in the State of Colorado. Except for the reliance on the general accuracy of the “technical data,” Contractor may not rely upon or make any claim against the City with respect to:

1. the accuracy or completeness of such reports and drawings for Contractor’s purposes, including, but not limited to, any aspects of the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor, and safety precautions and programs incident thereto; or

2. other data, interpretations, opinions, and information contained in the reports or shown or indicated in such drawings; or

3. any Contractor interpretation of or conclusion drawn from any "technical data" or any such other data, interpretations, opinions, or information.

107.27 UNANTICIPATED CIRCUMSTANCES

Contractor understands that this is a firm fixed price contract and so long as there are no changes in the scope of work or unanticipated circumstances as provided in subsection A-C below, Contractor must deliver the project for the agreed price. The parties agree that not every circumstance can be anticipated or known at the time this Contract was executed. Compensation for unanticipated circumstances, limited to subsections A –C, shall, at the City’s sole discretion, be provided by the following method(s): (1) Unit prices previously approved; (2) allowing additional

compensation on a time and materials method, not to exceed an agreed-to amount; (3) an agreed lump sum; and/or (4) the actual cost of:

(a) labor (including foreman and additional supervision, if necessary);

(b) materials necessary for incorporation into the Project:

(c) rental cost of construction plant and equipment used for work:

(d) Power and fuel required for operation of power equipment necessary to perform work;

(e) Contractor shall provide to the City physical evidence of all costs, including, but limited to, payroll, invoices, vouchers, estimates, bills, accounting records, or other relevant records. Contractor agrees that its failure to provide evidence of a claimed cost shall be a waiver of such cost(s) and the City shall be released and forever discharged from any claim of any kind whatsoever, loss, damages, request for equitable adjustment, or demand related thereto. Contractor further agrees that, at the City's discretion, a fixed fee, not to exceed 10% of the costs of work shall be added to such costs as compensation for the cost of management, insurance, benefits, bond, profit, and any other expenses.

To the extent unanticipated circumstances arise, Contractor shall follow the procedures and processes set forth herein and, if applicable, the Dispute Resolution provisions of this Contract. Contractor agrees that its failure to follow the processes set forth herein and the Dispute Resolution process shall forever waive, release, and discharge the City from any claim of any kind whatsoever, damages, losses, lawsuits, or demands known or unknown. Additionally, the terms "detail" or "particularity" mean specificity, providing the exact basis and reason therefor with citations to the Contract or Contract Documents. Vague or ambiguous references such as "other matters" or "other costs" shall not be permitted and are not subject to any compensation method whatsoever.

A. Differing Site Conditions or Changed Conditions: A differing site condition or changed condition means subsurface, latent, or unknown physical site conditions that are materially different than that which is indicated in the contract and which is not ordinarily encountered and generally recognized in the work provided for in the Contract.

Contractor understands the City must be permitted the opportunity to timely investigate all differing site/changed condition matters; document conditions as they existed on the site at the time; take measurements, photographs, witness statements and the like; negotiate a compromise resolution with the

Contractor and/or subcontractors; and avoid the cost, expense and delay of formal litigation.

Upon discovering a differing site condition, the Contractor shall not disturb the conditions and immediately contact the Project Manager. Within five days of discovering the condition, the Contractor shall provide written notice to the Project Manager of the condition. The written notice shall describe the condition with particularity; provide the precise material difference of the condition from the Contract, design plans, and/or other Contract Documents; describe, in detail, how the condition is not a condition that would be ordinarily encountered and generally recognized in the work provided for in the Contract; and provide a detailed explanation, including all accounting and other evidence supporting, Contractor's losses, costs, delays, and changes in time required for performing the work. Contractor agrees that any claim, loss, damage, delay, or change in time that is not supported by evidence shall be disallowed. Contractor waives and forever releases and discharges the City from any claim of whatsoever kind, loss, damages, demand, and/or request for equitable adjustment whether known or unknown by disturbing the condition before notifying the Project Manager and by failing to provide timely detailed written notice as required herein. Any issue which is not provided for, in detail, in the written notice shall also be waived and the City shall be forever released ad discharged from any claim whatsoever, loss, damage, or request for equitable adjustment, or demand arising therefrom.

After Contractor fully complies with the provisions in this section and after receiving the written notice, the Project Manager shall promptly investigate the condition and determine whether such condition materially differs from that indicated in the Contract Documents and whether it is a condition that would not ordinarily be encountered and generally recognized in the work provided for in the Contract. If the Project Manager determines the condition is a "differing site condition," then a Change Order shall be issued describing the differing site condition and compensation method agreed to by the parties. By signing the Change Order, Contractor agrees the City shall be released and fully discharged from any claim whatsoever, loss, damage, request for equitable adjustment, or demand arising from the matters described in the Change Order. The parties shall also sign a document which describes in detail each condition and each claim, loss, damage, delay, or change in time related to that particular condition which was agreed to and fully resolved as well as any condition and each claim loss, damage, delay, or change in time related to that particular condition which is disputed.

If the Contractor disputes, disagrees with, or otherwise considers unfair any decision or ruling by the City, then Contractor shall, within 10 Calendar Days, provide the City with written notice of the dispute as set forth in the

dispute section of this Contract and shall follow the dispute resolution process provided therein.

B. Defective or Deficient Construction Plans or Documents: A defective or deficient construction plan or document means a material error, mistake, oversight, or omission in the design plans or documents providing the specifications depicting the general and detail features of the work to be performed.

Upon discovering a defect or deficiency, the Contractor shall immediately contact the Project Manager. Within five days of initially advising the Project Manager of the defect or deficiency, the Contractor shall provide written notice to the Project Manager. The written notice shall describe the defect or deficiency with particularity explaining why it is a material defect or deficiency; provide precise detail explaining why the defect or deficiency is not something Contractor should know how to do or why the defect or deficiency is not a condition that would be ordinarily encountered and generally recognized in the work provided for in the Contract; and provide a detailed explanation, including all accounting and other evidence supporting, Contractor's losses, costs, delays, and changes in time required for performing the work. Contractor agrees that any claim, loss, damage, delay, or change in time that is not supported by evidence shall be disallowed. Contractor agrees that it shall waive and forever release and discharge the City from any claim of whatsoever kind, loss, damages, demand, and/or request for equitable adjustment whether known or unknown by failing to immediately notifying the Project Manager and by failing to provide timely detailed written notice as required herein. Any issue which is not provided for in the written notice shall also be waived and the City shall be forever released ad discharged from any claim whatsoever, loss, damage, or request for equitable adjustment, or demand arising therefrom.

After Contractor fully complies with the provisions in this section and after receiving the written notice, the Project Manager shall promptly investigate the condition and determine whether such matter is a "defective or deficient design plan or document" as defined herein. If the Project Manager determines the matter is a "defective or deficient design plan or document," then a Change Order shall be issued describing the defective or deficient design plan or document, the correction and compensation method agreed to by the parties. By signing the Change Order, Contractor agrees the City shall be released and fully discharged from any claim whatsoever, loss, damage, request for equitable adjustment, or demand arising from the matters described in the change order. The parties shall also sign Form A of this Contract which describes in detail each condition and each claim, loss, damage, delay, or change in time related to that particular condition which was agreed to and fully resolved as well as any condition and each

claim loss, damage, delay, or change in time related to that particular condition which is disputed.

If Contractor disputes, disagrees with, or otherwise considers unfair any decision or ruling by the City, then Contractor shall, within 10 Calendar Days, provide the City with written notice of the dispute as set forth in the Dispute Resolution section of this Contract and shall follow the dispute resolution process provided therein.

C. Changes in Work and Additional/Extra Work (fixed price contract): When additional information through excavation, testing, site investigation, differing site conditions, or otherwise is obtained the City shall have the right to alter, change the location, re-design, change the work, add to the work, accelerate work, or reduce work, change the method or manner of performance, change services, and/or change materials described in the Contract (collectively "Changed Work").

If the City changes work, then a Change Order shall be issued by the Project Manager. Contractor shall not be required to perform any Changed Work without a Change Order issued by the Project Manager. Such Changed Work shall be performed under the terms set forth in the original Contract and compensated as agreed in this section of the Contract.

If Contractor disputes any Changed Work or compensation method for such Changed Work requested by the City or set forth in a Change Order, Contractor shall, without delay, perform such work. Within 10 Calendar Days of receiving the Change Order, Contractor shall provide the City with written notice of the dispute as set forth in the Dispute Resolution section of this Contract and shall follow the dispute resolution process provided therein. Contractor further agrees that any issue not provided for, in detail, in the written notice shall also be waived and the City shall be forever released ad discharged from any claim whatsoever, loss, damage, or request for equitable adjustment, or demand arising therefrom. Any matter resolved through the Dispute Resolution process shall be set forth in Form A of this Contract which describes in detail each Changed Work, including the compensation method, which was agreed to and fully resolved. By signing Form A, Contractor agrees that the City shall be released and fully discharged from any claim whatsoever, loss, damage, request for equitable adjustment, or demand arising from the matters described in Form A.

If Contractor does not dispute any Changed Work or the compensation method for such work, then Contractor shall sign the Change Order and agrees that the City shall be released and fully discharged from any claim

whatsoever, loss, damage, request for equitable adjustment, or demand arising from the matters described in the Change Order.

Contractor agrees that the Project Manager shall have the authority to make minor changes in the work which do not involve additional costs and are not inconsistent with the purpose and scope of the work.

If the City finds it necessary or advisable, the City may omit, increase, or decrease any items as it may deem necessary or desirable without changing the unit prices in the proposal, provided such increase or decrease does not exceed 15% of the total monetary value of the original Contract. If material or labor involved in such change is not included in the unit prices of the Contract, but forms an inseparable part of the work to be done under this Contract, and the delay involved in asking for the bids or proposals and the letting of a new contract therefore might result in damage, injury, or impairment of the plant, work system, or other property belonging to the City, the City may in its discretion declare an emergency and require Contractor to proceed with such alterations and additions. The Contract shall not be required to perform such work or furnish extra materials without a Change Order issued by the Project Manager.

107.28 DISPUTE RESOLUTION

Mindful of the high cost of litigation, not only in dollars, but also in time and energy, the parties intend to and do hereby establish the following out-of-court alternate dispute resolution procedure to be followed in the event any dispute, claim of any kind, loss, damage, demand, request for equitable adjustment, or controversy should arise out of, or relating to this Contract or relating to any Change Order or other changes or addendums to this Contract. During the dispute resolution procedure provided in this section, Contract shall continue to perform the work as provided for in this Contract as modified by any Change Order or Contract amendment. Nothing in this section precludes the parties from pursuing any other remedy afforded by the laws of the State of Colorado once the remedies afforded under this Contract have been complied with and exhausted.

A. Disputes Arising from Unanticipated Circumstances: If Contractor disputes, disagrees with, or considers any decision, order, ruling, demand, request, directive, Change Order, or Contract amendment, related to the Unanticipated Circumstances provision of this Contract, and issued by the City, whether verbally or in writing, then Contractor shall:

1. Within 10 days of the City issuing any written or verbal decision, order, ruling, demand, request, directive, Change Order, or Contract amendment, Contractor shall provide written notice to the Project Manager identifying, with specific detail, each disputed matter. Any Unanticipated Circumstance dispute or matter of any kind or nature whatsoever, which Contractor does not identify in detail shall be waived and the City is released and fully discharged from any claim whatsoever, loss, damage, request for equitable

adjustment, or demand arising from any matter not explicitly set forth in the written notice and described in detail;

2. Contractor shall provide to the City all evidence of any claim of whatsoever kind, loss, damages, delay cost, or other costs, including, but not limited to payroll reports, daily logs, invoices, accounting file, receipts, email, or other relevant record or document. Any item claimed by Contractor shall be supported by verifiable evidence described herein. If Contractor requires additional time to obtain or compile such evidence, then the Contractor shall have an additional 30 days, but must identify the exact document(s) or other evidence needed, where it is maintained, and explain why it is not available. The City shall not be responsible for any delay or other damage arising from Contractor's request for additional time to obtain documents. Any item unsupported by verifiable evidence shall be waived and Contractor agrees to release and fully discharge the City from any claim of whatsoever kind, loss, damage, request for equitable adjustment, or demand related to such unsupported item.

3. Upon receipt of Contractor's written notice, the Project Manager will investigate the disputed matter(s) and issue a written decision, ruling, order, and/or directive to Contractor. If Contractor does not dispute the Project Manager's decision, ruling, order, or directive, or a compromise has been reached, then Contractor shall sign Form A. If Contractor disputes or disagrees with the Project Manager's Ruling, then within 20 days of receiving the Project Manager's decision, ruling, order, and/or directive, Contractor must file with the City a written request for review to the City Engineer or City's Manager of the Procurement Services Division. The written request for review shall (a) state in detail the exact issue raised to the Project Manager and the issue(s) related to those matters raised to be reviewed by the City Engineer or Procurement Services Manager; (b) provide an analysis, detailing the basis, reason therefor and the how and why Contractor disagrees with the Project Manager's decision, ruling, order, or directive; and (c) attach all evidence supporting Contractor's dispute. If Contractor fails to provide a timely written request for review to the City Engineer or Procurement Services Manager, then Contractor agrees that it waives, releases, and forever discharges the City from any claim of whatsoever kind, loss, damage, request for equitable adjustment, or demand arising from or related to the Project Manager's decision, ruling, order, or directive.

4. The City Engineer's or Procurement Services Manager's decision shall be final and conclusive for the City of Colorado Springs. If Contractor disputes, disagrees with, or considers such decision unfair, then Contractor shall be free to pursue any other remedy afforded by the laws of the State of Colorado. If Contractor does not dispute the City Engineer's or

Procurement Services Manager's decision, ruling, order, or directive or a compromise is reached, then Contractor shall sign Form A.

5. Contractor shall pay the City reasonable attorney's fees and costs associated with its failure to comply with any part of this alternate dispute process.

B. All Other Claims: If a dispute, disagreement, or controversy of any kind, other than those covered in the Unanticipated Circumstances section of this Contract, arises from or is related to the Contract, shall be resolved under the Disputes section in the Contract.

107.29 REMOVAL AND SUSPENSION FOR DEFECTIVE WORK

All work or material which has been rejected shall be remedied or removed and replaced in an acceptable manner. Additional compensation will not be allowed for such removal and replacement. Any work done beyond the lines and grades shown on the drawings, except as herein provided, will be considered as unauthorized and will not be measured or paid for. Work so done may be ordered removed at the Contractor's expense. Should the Contractor fail to comply promptly with any order of the Project Manager made under the provisions of this paragraph, the Project Manager shall have the authority to cause said work to be removed and to deduct the cost from any money due, or to become due, from the Contractor. At any time during the course of construction of this project if the provisions of the Plans, Specifications, or Contract provisions are being violated by the Contractor or his employees, the Project Manager shall have the right and authority to order all construction to cease or material to be removed, until arrangements satisfactory to the Project Manager are made by the Contractor for resumption of the work in compliance with the provisions of the Contract.

The Contractor shall promptly remove from the premises all materials and work rejected by the Project Manager as failing to meet Contract requirements, whether incorporated in the work or not, and the Contractor shall promptly replace and re-execute Contractor's own work in accordance with the Contract and without expense to the City and shall bear the expense of making good all work of other Contractors destroyed or damaged by such removal or replacement.

All removal and replacement work shall be done at the Contractor's expense. If the Contractor does not take action to remove such rejected work and materials within ten (10) days' time thereafter, the City may, upon ten (10) days written notice, sell such materials at auction or at private sale and retain the proceeds without compensation to the Contractor.

107.30 CLEANING UP AND FINAL INSPECTION

The Contractor shall at the completion of the work, remove all rubbish from and about the work and all tools, equipment, scaffolding, and surplus materials and shall leave the work clean and ready for use. If not completed by Contractor, the City may remove the rubbish and surplus materials and charge the cost to the Contractor.

All sewers, conduits, pipes, and appurtenances and all tanks, pump wells, chambers, buildings, and other structures shall be kept clean during construction and as the work or any part thereof approaches completion, the Contractor shall systematically and thoroughly clean and make any needed repairs to them. Contractor shall furnish at Contractor's own expense, suitable tools and labor for removing all water and cleaning out all dirt, mortar, and foreign substances. Any undue leakage of water into the structures such as to make the work, in the opinion of the Project Manager, fall short of first class work, shall be promptly corrected by the Contractor at Contractor's own expense.

Cleaning and repairs shall be arranged, so far as practicable, to be completed upon finishing the construction work. Notice to begin the final cleaning, and repairing, if such is needed, will be given by the Project Manager, who at the same time will make his final inspection of the work. The Project Manager will not approve the final estimate of any portion of the work until after the final inspection is made and the work is found to be satisfactory.

107.31 CUTTING AND PATCHING

The Contractor shall do all cutting, fitting, or patching of work that may be required to make its several parts fit together or to receive the work of other contractors shown upon, or reasonably implied by the Plans and Specifications for the completed Project.

Cold or wet weather conditions that do not permit a permanent asphalt pavement replacement will require a minimum 2” bituminous pavement patch prior to opening the area to traffic as a temporary measure until the permanent asphalt pavement replacement can be installed. This item shall be incidental to any work requiring such removal of asphalt and will be considered to be included in the unit price of the related item of work.

Any cost caused by defective or ill-timed work shall be borne by the Contractor.

The Contractor shall not endanger any work by cutting, digging, or otherwise and shall not cut or alter the work of any other Contractor without the consent of the Project Manager.

107.32 FINAL TESTS

After completion of the work, the Contractor shall make any and all tests required by the Specifications or by municipal, state, or federal regulations, and where so provided in said regulations shall furnish the City with certificates of inspection by the applicable regulatory bodies. The Contractor shall also make all tests required by the National Board of Fire Underwriters for the purpose of determining insurance rates or other protection of the City or the public.

107.33 CORRECTION OF WORK AFTER FINAL PAYMENT

Neither the final payment nor any provision in the Contract Documents shall relieve the Contractor of the responsibility for negligence or faulty materials or workmanship within the extent and periods provided by law and by this Contract.

107.34 NO WAIVER OF LEGAL RIGHTS

Upon written notice that the Contractor considers all work complete, the Project Manager will make a pre-final inspection with the Contractor and will notify the Contractor in writing of incomplete or defective work revealed by the inspection. The Contractor shall promptly remedy such deficiencies.

After the Contractor has remedied all deficiencies to the satisfaction of the Project Manager and delivered all construction records including record drawings, maintenance and operating instructions, schedules, guarantees, bonds, certificates of inspection and other documents (all as required by the Contract Documents), the Contractor will be promptly issued a Certificate of Completion by the Project Manager stating that the work is acceptable.

Upon completion of the Contract, the City will make final inspection and notify the Contractor of acceptance. Final acceptance shall not preclude the City from correcting any measurement, estimate, or certificate made before or after completion of the Contract, nor from recovering from the Contractor or Surety, or both, overpayments sustained because the Contractor failed to fulfill the obligations under the Contract.

The Contractor shall be liable to the City for latent defects, fraud, or such mistakes as may amount to fraud, or as regards the City's rights under any warranty or guarantee.

For all non-federally funded projects, the following additional requirements shall apply:

(a) All work shall be constructed in compliance with standard construction codes, and all materials and workmanship must be guaranteed for a period

of two years from the date of final acceptance. If any defect in the work in violation of the foregoing warranty arises, Contractor shall, upon receipt of written notice of such defect, promptly furnish, at no cost to the City, design and engineering, labor, equipment, and materials necessary to correct such defect and cause the Work to comply fully with the foregoing warranty and Contract Documents. This obligation shall survive both final completion of and final payment for the Work. The City shall not be invoiced for any of costs of warranty work, and Contractor shall not be entitled to submit any claim for an increased fee arising therefrom. The Contractor guarantee period (two-year warranty period) will not begin until the Contract is 100 percent complete, as determined by the Project Manager. Acceptance of the 100 percent complete work shall be requested in writing by the Contractor. Any item requiring repair and/or replacement prior to expiration of the two-year warranty period shall be guaranteed for a period of one-year after the date of said correction or repair or for the remainder of the two-year warranty period, whichever is longer.

(b) In placing orders for equipment, the Contractor shall purchase such equipment only under a written guarantee from the respective manufacturers that the equipment supplied will function satisfactorily as an integral part of the completed Project in accordance with the Plans and Specifications. Furthermore, the Contractor shall require that the manufacturer agree in writing at the time an order of equipment is placed that manufacturer will be responsible for the proper functioning of the equipment in cooperation with the Contractor, and that whenever necessary during the installation period or tuning up period following construction period, the manufacturer will supply without additional cost to the City, such superintendence and mechanical labor and any adjustments and additional parts and labor needed to make the equipment function satisfactorily, even if the same was not shown on approved shop drawings.

107.35 ACCEPTANCE

(a) *Partial Acceptance.* If, during the performance of the project, the Contractor satisfactorily completes a unit or portion of the Project, such as a structure, an interchange, or a section of road or pavement that can be used advantageously for traffic, the Project Manager may make final inspection of that unit. If the Project Manager finds that the unit has been satisfactorily completed in compliance with the Contract, the Contractor may be relieved of further responsibility for that unit except as otherwise provided in these general provisions. Partial acceptance shall not void or alter any of the terms of the Contract.

(b) *Final Acceptance.* Upon notice from the Contractor of presumptive completion of the entire Project, the Project Manager will make an inspection. If the work provided for by the Contract has been satisfactorily

completed, that inspection shall constitute the final inspection and the Project Manager will notify the Contractor in writing of final acceptance indicating the date on which the Project was inspected and accepted.

If the inspection discloses any unsatisfactory work, the Project Manager will give the Contractor a written list of the work needing correction. Upon correction of the work, another inspection will be made. If the work has been satisfactorily completed, the Project Manager will notify the Contractor in writing of the date of final inspection and acceptance. Final acceptance under this subsection does not waive any legal rights contained in the No Waiver of Legal Rights section of this Contract.

SECTION 108 PAYMENTS AND ACCEPTANCE OF WORK

108.00 PAYMENTS AND RETAINAGE

Payments will be made, and required retainage withheld if applicable, in accordance with this section as the work progresses at the end of each month or as soon thereafter as practicable in compliance with C.R.S. Title 24, Article 91, on statements made and approved by the Project Manager. In preparing statements, only completed work will be taken into consideration. No payment will be made for materials in storage and/or delivered to the site, unless otherwise approved by the City.

Payment for work performed by the Contractor under the Contract Documents will be made at the approved unit price or lump sum price for each of the several items as listed in the proposal and measured as hereinafter specified. Such payment shall compensate the Contractor for all costs in connection with furnishing all labor, equipment and material required and performing the operations necessary to complete the item in accordance with the Contract Documents. All incidental work essential to the completion of the Project in a workmanlike manner, and including cleanup and disposal of waste or surplus material, shall be accomplished by the Contractor without additional cost to the City. The cleanup and disposal of waste or surplus material shall be performed during construction or as soon after as is reasonably possible in order to better maintain the aesthetics and safety of the construction area. Payment will be made for the actual quantities constructed or installed, unless otherwise noted in these Contract Documents. However, any changes to plan quantity must be approved through proper Change Order procedures, said quantities being measured as specified in the Contract Documents.

(1) If the Contract exceeds one hundred fifty thousand dollars ($150,000.00), and is for the construction, alteration, or repair of any highway, public work, or public improvement, structure, and the Contractor has provided Performance and Payment Bonds: the City shall authorize partial progress payments of the amount due under this Contract monthly, or as soon

thereafter as practicable, to the Contractor, if the Contractor is satisfactorily performing the Contract. If the City finds that satisfactory progress is being achieved during any period for which progress is to be made, the City may authorize payment to be made in full without withholding retainage. However, if satisfactory progress has not been made, the City may retain a maximum of ten percent (10%) of the amount of the requested payment until satisfactory progress is achieved. When the work is substantially complete, the City may retain from the remaining unpaid balance that amount the City Procurement Services Manager, at the advice of the Project Manager, considers adequate for protection of the City, suppliers, subcontractors, laborers, vendors, etc., provided that such retainage shall not exceed five percent (5%) of the amount due, and shall release to the Contractor all the remaining funds associated with completed and acceptable work.

If satisfactory progress has not been made the withheld percentage of the Contract price of any such work, improvement, or construction shall be retained on an invoice-to-invoice basis and shall not be cumulative. In other words, if the Contractor is not performing satisfactorily the City will hold ten percent (10%) of what is actually due to the Contractor. For example, if the Contractor is behind schedule and has successfully completed fifty percent (50%) of the work, the City will only pay forty percent (40%) of the invoice, withholding ten percent (10%) of what is due until the Contractor gets back on schedule.

(2) Whenever a Contractor receives payment pursuant to this section, the Contractor shall make payments to each of the subcontractors of any amount actually received which were included in the Contractor's request for payment to the City for such subcontracts. The Contractor shall make such payments within seven (7) Calendar Days of receipt of payments from the City in the same manner as the City is required to pay the Contractor under this section if the subcontractor is satisfactorily performing under the Contract with the Contractor. The subcontractor shall pay all suppliers, sub-subcontractors, laborers, and any other persons who provide goods, materials, labor, or equipment to the subcontractor any amounts actually received which were included in the subcontractor's request for payment to the Contractor for such persons, in the same manner set forth in this subsection (2) regarding payments by the Contractor to the subcontractor. If the subcontractor fails to make such payments in the required manner, the subcontractor shall pay those suppliers, sub-subcontractors, and laborers interest in the same manner set forth in this subsection (2) regarding payments by the Contractor to the subcontractor.

At the time a subcontractor submits a request for payment to the Contractor, the subcontractor shall also submit to the Contractor a list of the subcontractor's suppliers, sub-subcontractors and laborers. The Contractor

shall be relieved of the requirements of this subsection (2) regarding payment in seven (7) days and interest payment until the subcontractor submits such list. If the Contractor fails to make timely payments to the subcontractor as required by this section, the Contractor shall pay the subcontractor interest as specified by Contract or at the rate of fifteen percent (15%) per annum, whichever is higher, on the amount of the payment which was not made in a timely manner. The interest shall accrue for the period from the required payment date to the date on which payment is made. Nothing in this subsection (2) shall be construed to affect the retention provisions of any Contract.

(3) If the Contractor is not progressing in accordance with the Project Schedule or not performing quality work in accordance with the specifications, the City Procurement Services Manager, at the advice of the Project Manager may withholding retainage up to and including ten percent (10%) of the total contract amount.

108.01 PAYMENTS WITHHELD PRIOR TO FINAL ACCEPTANCE OF WORK

The City may withhold or nullify the whole or part of any certificate of payment to such extent as may be necessary to protect it from loss caused by:

(a) Defective work not remedied.

(b) Claims filed or reasonable evidence indicating probable filing of claims by other parties against the Contractor.

(c) Failure of the Contractor to make payments properly to subcontractors or for material or labor.

(d) Damage to another contractor.

When the above grounds are removed, payment will be made for amounts withheld because of them.

108.02 ACCEPTANCE OF FINAL PAYMENT

If the work is finally accepted by Project Manager under the terms and conditions of the Contract the entire balance found by the Project Manager to be due the Contractor, including the retained percentage, less any retention based on; (1) the Project Manager's estimate of the fair value of the claims against the Contractor; and (2) the cost of completing the incomplete or unsatisfactory items of work with specified amounts for each incomplete or defective item of work; and (3) retentions required by law, shall be due and payable to the Contractor. The date of completion

is the date as specified in the Certificate of Completion issued by the Project Manager.
Upon completion of the work under the Contract and before the Contractor will receive or be paid for the Project Manager's final statement, the City Procurement Services Division shall post a notice in the Colorado Springs Gazette that the City has accepted such work as completed according to the Plans and Specifications and rules set forth in the Contract; that the Contractor is entitled to final settlement; that after the date specified in the Notice, the City will pay the full balance due under the Contract; and that persons having claims for labor or material furnished the Contractor must present their claim to the City Procurement Services Division prior to the date specified for such payment. Nothing herein shall be construed as relieving the Contractor and the Sureties on the Contractor's bonds from any claim or claims for work or labor done or materials or supplies furnished in the execution of the Contract.

The making and acceptance of the final payment shall constitute a waiver of all claims by the Contractor against the City.

If, after the work has been substantially completed, full completion thereof is materially delayed through no fault of the Contractor, and the Project Manager so certifies, the City may, upon Certificate of Completion by the Project Manager, and without terminating the Contract, make payment of the balance due for that portion of the work fully completed and accepted. Such payment shall be made under the terms and conditions governing final payment, and acceptance of the payment shall constitute a waiver of all claims by the Contractor but acceptance of the work shall not constitute a waiver of City claims against the Contractor.

Advertising for Final Payment and processing of the Final Pay Request shall not take place until after the Contractor has submitted Sales and Use Tax Forms to the City and said forms have been reviewed and approved by the City Sales Tax Office.

SCHEDULE C - TECHNICAL SPECIFICATIONS

This section contains the Standard Specifications and Revisions of Standard Specifications. Measurement and Payment for all bid items shall be in accordance with the Standard Specifications or Revisions of Standard Specifications

STANDARD SPECIFICATIONS

The following are the Standard Specifications that apply to this project. In the event there are conflicting Standard Specifications, the order of precedence will be based upon the order in which the Standard Specifications are listed. Section H Measurement and Payment describes which specific Standard Specification sections apply to each bid item.

All contractors are required to have on the job site and utilize the current updated copy of the Standard Specifications applicable to the work.

Any revisions to the Standard Specifications can be found in the Subsection 9.2 of this document.

A. City of Colorado Springs Standard Specifications

1.) The "**City of Colorado Springs Engineering Division Standard Specifications**", except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project. This document is referenced as the "*City Standard Specifications".*

Copies are available from the City of Colorado Springs, Office Services Division, Suite L01, 30 South Nevada Avenue, Colorado Springs, during regular business hours or at the following web address:
https://coloradosprings.gov/public-works/page/standard-specifications-manual

2.) The "**City of Colorado Springs Drainage Criteria Manual, Volume II**", May 2014, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project. This document is referenced as the "*City Drainage Criteria Manual".*

3.) The "**Pikes Peak Region Asphalt Paving Specifications**", Latest Edition, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project.

Copies are available from the City of Colorado Springs, Office Services Division, Suite L01, 30 South Nevada Avenue, Colorado Springs, during regular business hours or at the following web address:

https://coloradosprings.gov/public-works/page/reference-materials

4.) The "**City of Colorado Springs Traffic Controls for Street Construction, Utility Work, and Maintenance Operations**", 10/27/2009 Edition, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project.

Copies are available from the City of Colorado Springs, Office Services Division, Suite L01, 30 South Nevada Avenue, Colorado Springs, during regular business hours or at the following web address:
https://coloradosprings.gov/public-works/page/reference-materials

Per Section 9.0 of the *City Drainage Criteria Manual*, the "*Construction BMP Fact Sheets*" from the ***Urban Drainage Flood Control District Manual, Volume 3*** are applicable. These Fact Sheets can be downloaded at the following website:
http://udfcd.org/volume-three

5.) The **"City of Colorado Springs Traffic Engineering Signage and Pavement Markings Guidelines**", 11/16/2009 Edition, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project.

Copies are available from the City of Colorado Springs, City Engineering Division, Suite L01, 30 South Nevada Avenue, Colorado Springs, during regular business hours.

6.) The "**Colorado Springs City Traffic Signal Installation and Parts Specifications for Contractors**", 11/26/2014 Edition, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project.

Copies are available from the City of Colorado Springs, City Engineering Division, Suite L01, 30 South Nevada Avenue, Colorado Springs, during regular business hours.

B. Colorado Springs Utilities Standard Specifications

1. The Standard Specifications for water line construction and protection shall be the **"Colorado Springs Utilities Water Line Extension and Service Standards"**, revised 2018, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety.

Copies are available from the Colorado Springs Utilities' Development Services, 111 S. Cascade, Suite 105, Colorado Springs, CO 80903, during regular business hours.

2. The Standard Specifications for wastewater line construction and protection shall be the "**Colorado Springs Utilities Wastewater Line Extension and Service Standards**", revised 2017, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety.

   Copies are available from the Colorado Springs Utilities' Development Services, 111 S. Cascade, Suite 105, Colorado Springs, CO 80903, during regular business hours.

3. The Standard Specifications for lighting installation, electrical distribution and electrical transmission line construction and protection shall be the "**Colorado Springs Utilities Electric Line Extension and Service Standards**", revised 2019, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety.

   Copies are available from the Colorado Springs Utilities' Development Services, 111 S. Cascade, Suite 105, Colorado Springs, CO 80903, during regular business hours.

COLORADO DEPARTMENT OF TRANSPORTATION

1. The "**Colorado Department of Transportation Standard Specifications for Road and Bridge Construction**", 2019 version, and all published standard special provisions, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project. This document is referenced as the "*CDOT Standard Specifications".*

2. The aforementioned revisions to the CDOT Standard Specifications are available from the following website:

   https://www.codot.gov/business/designsupport/cdot-construction-specifications/2019-construction-specifications/2019-specs-book

3. The "**Colorado Department of Transportation M&S Standard Plans**", latest version, except as modified hereinafter, which are incorporated in the contract documents by reference as though embodied herein in their entirety, shall apply to this project. This document is reference as the "*CDOT Standard Plans*".

CDOT provides regular updates to the CDOT Standard Plans. The versions of each plan as specified on the "Standard Plans List" in the project plans shall apply to this project. CDOT Standard Plans are available from the following website:

https://www.codot.gov/business/designsupport/2019-and-2012-m-standards/2019-m-standards-plans/2019-m-standards-plans-and-details

North Chelton Road Drainage Improvements
TECHNICAL SPECIFICATIONS

INDEX OF STANDARD SPECIFICATION APPLYING TO PROJECT

200 STREET SECTION
206 BACKFILL OF UTILITY TRENCHES USING CONTROLLED LOW STRENGTH MATERIALS
220 REMOVAL OF STRUCTURES AND OBSTRUCTIONS
240 RESET STRUCTURES
300 AGGREGATE BASE COURSE
400 ASPHALT CONCRETE PAVEMENT
410 ASPHALTIC PRIME COAT AND TACK COAT
430 CONCRETE PAVEMENT
500 CONCRETE
600 STRUCTURAL CONCRETE
620 DRAINAGE CHANNELS
630 STORM DRAINS AND CULVERTS
700 CONTROL OF MATERIALS
800 WORK ZONE TRAFFIC CONTROL
900 SEEDING, FERTILIZER, MULCHING AND SODDING
Standard Drawings
Appendix A - Ingress and Egress from Public Streets or Highways

INDEX OF REVISIONS AND ADDITIONS

220 REMOVAL OF STRUCTURES AND OBSTRUCTIONS
240 RESET STRUCTURES
300 AGGREGATE BASE COURSE
400 ASPHALT CONCRETE PAVEMENT
630 STORM DRAINS AND CULVERTS
900 SEEDING, FERTILIZER, MULCHING AND SODDING
920 EROSION AND SEDIMENT CONTROL DURING CONSTRUCTION
1000 UTILITIES
1100 CONSTRUCTION SURVEYING

REVISION OF SECTION 220

REMOVAL OF STRUCTURES AND OBSTRUCTIONS

Section 220 of the Standard Specifications is hereby revised for this project as follows:

Any dewatering associated with removals during construction shall be considered incidental to the work

Addition to 220.03 Removal of Bridges, Culverts, and Other Drainage Structures

Manholes designated for removal shall be removed in their entirety and disposed of by Contractor.

Addition to 220.04 Removal of Pipe

Removal of water pipes shall include removal of all fittings, valves, hydrants, bends, etc. and is considered incidental to the removal of the water pipe and disposed of by Contractor.

<u>Stormwater Bypass Plan</u>

Contractor shall provide to the City a stormwater bypass plan two (2) weeks prior to removal of reinforced concrete pipe. Removal of the RCP shall not commence until City has provided written approval of the bypass plan and the bypass measures are installed. The Contractor shall be responsible for installation and removal of the bypass measures. The Contractor shall be responsible for maintenance of the temporary system day and night for the full duration of use.

<u>Temporary Water Service</u>

The Contractor is responsible for construction and demolition of waterline with a maximum of an eight (8) hour outage for any water customer at a single instance. The Contractor shall provide a temporary water plan drawing reflecting locations, material types and sizes, and proposed temporary water sources to be utilized. Contractor shall provide to CSU a temporary water plan two (2) weeks prior to any shutdown occurrence. Shutdown of water service shall not commence until CSU has provided written approval of the temporary water plan. Upon review and approval CSU will notify Colorado Springs Fire Department (CSFD) of the hydrant being used as a temporary water source. See Figure 1 below for a potential temporary water connection diagram.

The Contractor shall use new (NSF 61), not previously used, materials that they will disinfect, flush and bactee test under and with CSU oversight and assistance.

The Contractor shall be responsible for maintenance of the temporary system day and night for the full duration of use.

The Contractor shall take measures to protect the temporary system from freezing.

Addition to 220.05 Removal of Pavements, Sidewalks, Curbs, etc.

All asphalt pavement designated for removal shall be broken into pieces and disposed of by Contractor.

Where old pavement construction abuts pavement to be left in place, asphalt shall be sawn to a true line with a vertical face.

220.05b Removal of Vegetation

The plans designate all trees, shrubs, plants, and other objects to remain. Every object that is designated to remain and is damaged shall be repaired or replaced as directed, at the Contractor's expense.

Clearing and grubbing shall extend to the toe of fill or the top of cut slopes, unless otherwise designated.

All surface objects, trees, stumps, roots, and other protruding obstructions not designated to remain shall be cleared and grubbed. In areas to be rounded at the tops of backslopes, stumps shall be removed to at least 2 feet below the surface of the final slope line.

Except in areas to be excavated, all holes resulting from the removal of obstructions shall be backfilled with suitable material and compacted.

Burning of perishable material will not be permitted.

No material or debris shall be disposed of within the project limits without the written permission of the City. Material or debris that is disposed of within the project limits shall be buried to a depth of at least 2 feet and the surface shall be reshaped to match the adjacent ground line.

The Contractor shall clear and grub the areas within the excavation or embankment grading limits and shall include the removal from the ground of brush, roots, sod, grass, sawdust, and other vegetable matter.

Trees designated for removal shall be disposed of by Contractor. Stumps shall be removed to at least 2 feet below the surface of the final slope line.

Trees shall be defined as vegetation with trunk caliper greater than or equal to 4 inches.

Bushes shall be defined as vegetation with trunk caliper less than 4 inches.

Addition to 220.07 Basis of Payment

Asphalt curb shall be considered part of asphalt removal and will not be paid separately.

Payment will be made under:

Pay Item	Pay Unit
Clearing and Grubbing	Acre
Removal of Asphalt Pavement	Square Yard
Removal of Concrete Curb and Gutter	Linear Foot
Removal of Asphalt Sidewalk	Square Yard
Removal of Concrete Sidewalk	Square Yard
Removal of Asphalt Driveway	Square Yard
Removal of Concrete Pan	Square Yard
Removal of Cast Iron Pipe (CIP) Waterline	Linear Foot
Removal of Steel Pipe Waterline	Linear Foot
Removal of PVC Pipe Waterline	Linear Foot
Removal of 24” Reinforced Concrete Pipe (RCP)	Linear Foot
Removal of Manhole	Each
Abandon Pipe/ Flowfill	Cubic Yard
Stormwater Bypass Plan	Lump Sum
Temporary Water Service Plan	Lump Sum

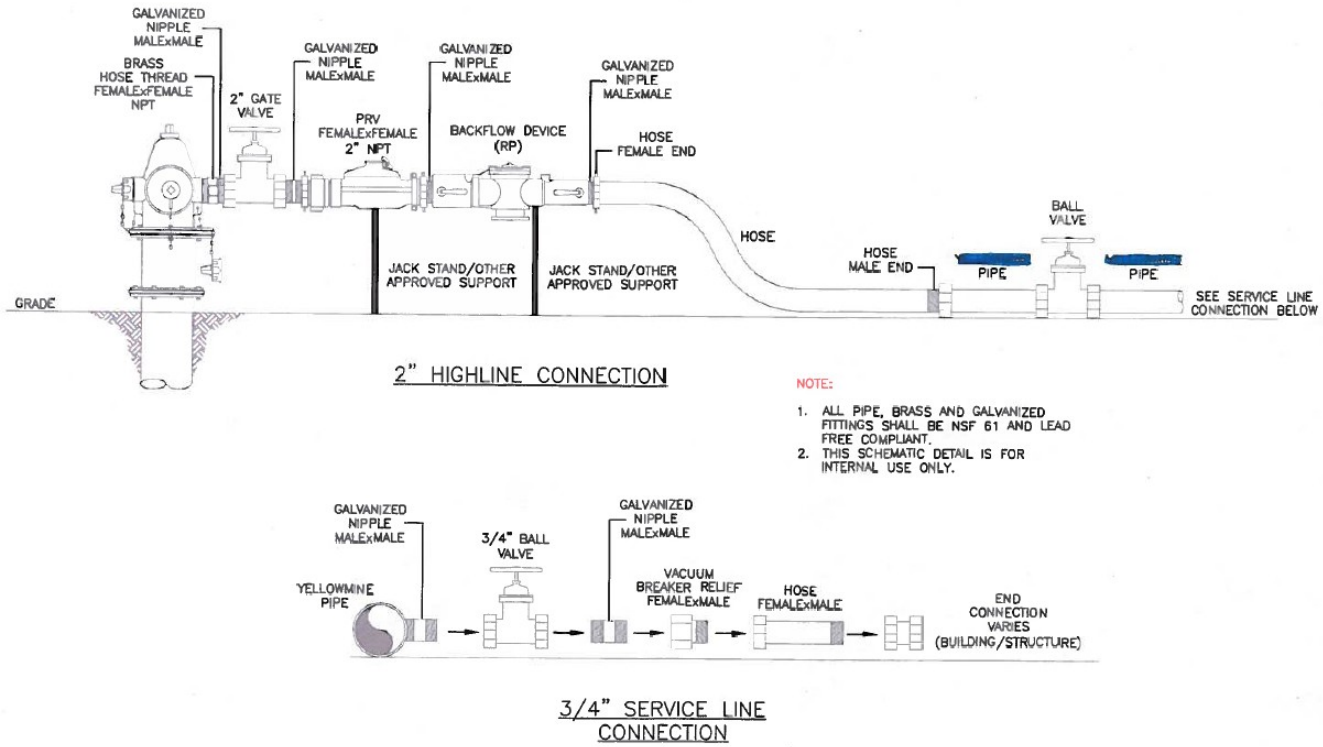

Figure 1: Potential Temporary Water Connection Diagram

END OF REVISION OF SECTION 220

REVISION OF SECTION 240

RESET STRUCTURES

Section 240 of the Standard Specifications is hereby revised for this project as follows:

Addition to 240.02 Construction Requirements

Contractor shall be responsible for locating and restoring to pre-construction condition any irrigation system within the project area. Contractor shall work with irrigation system owner and operate the system prior to construction to verify pre-construction condition.

Existing irrigation system facilities shall be salvaged and stockpiled to be replaced in existing layout. Materials that are damaged must be replaced in kind or approved equivalent.

Signs and posts designated to be reset shall be removed, cleaned, and reset at designated locations, including all work necessary to provide the existing posts with break-away devices, where required. Any post or panel not deemed suitable by City must be replaced in kind or per current City, state, and federal requirements.

Existing landscape rock shall be documented by time stamped photograph prior to removal. Contractor is to salvage existing landscape rock and weed barrier material unless either is deemed unsalvageable, in which case Contractor is to furnish new landscape rock and/or weed barrier material. Contractor shall produce a sample of the new landscape rock and weed barrier material for City approval prior to installation.

Reset of group mailbox shall include installation of the new concrete base, removing existing posts from the concrete base, removal and disposal of the concrete base, and reattaching the post to the base similar to the existing attachment. Contractor shall maintain access to the mailboxes for the USPS and residents at all times.

Reset of guy wire shall include coordination with Colorado Springs Utilities to temporarily support the electric pole, removal of the existing guy anchor and re-installation of the guy wire anchor system similar to the existing condition.

Adjust inlet shall consist of raising, adding concrete and resetting grates and frames to fit the new construction. Contractor to provide an inlet design capable of supporting an HS-20 loading for City approval two (2) weeks prior to adjusting inlet.

Addition to 240.03 Method of Measurement

Reset Irrigation shall be measured and paid on a lump sum basis completed and accepted. Final acceptance to be determined by the City following a field test and satisfactory operation after completion of the work.

Ground signs shall be measured and paid as each assembly of post and panel installed as approved by the City.

Landscape Rock shall be measured and paid for on a square yard basis completed and accepted. Reset of weed barrier is incidental to item and will not be paid separately.

Final acceptance to be determined by the City following acceptance of the material and satisfactory placement of material.

Reset guy wire shall be measured and paid as each assembly removed and reinstalled as approved by the City.

Addition to 240.04 Basis of Payment

Payment will be made under:

Pay Item	Pay Unit
Reset Irrigation System	Lump Sum
Reset Landscaping Rock	Square Yard
Reset Ground Sign	Each
Reset Mail Box	Each
Reset Group Mail Box	Each
Reset Guy Wire	Each
Adjust Inlet	Each

END OF REVISION OF SECTION 240

Additional SECTION 300
AGGREGATE BASE COURSE

Section 300 of the Standard Specifications is hereby revised for this project as follows:

Revision to 302 Material
Aggregate base course shall be CDOT class 6 base course and shall meet all specifications laid out in section 304 if the CDOT 2019 Standard Specifications for Road and Bridge Construction.

END OF REVISION OF SECTION 300

Additional SECTION 400
ASPHALT CONCRETE PAVEMENT

Section 400 of the Standard Specifications is hereby revised for this project as follows:

Addition to 401 Description
Bituminous Curb shall meet all specifications laid out in section 609 of the CDOT 2019 Standard Specifications for Road and Bridge Construction and CDOT M&S Standard Plans.

Addition to 408 Measurement and Payment

Payment will be made under:

Pay Item	Pay Unit
Bituminous Curb Type 6	Linear Foot

END OF REVISION OF SECTION 400

REVISION OF SECTION 630

STORM DRAINS AND CULVERTS

Section 630 of the Standard Specifications is hereby revised for this project as follows:

Please note that dewatering is incidental to the asset installation. Tracer wire system must be installed with storm drainage pipe and is also considered incidental to pipe construction.

Addition to 636.05 Inlets

Type R Inlets shall be constructed in conformance with the current version of CDOT M Standard Plans and Project Special Details.

Denver Type 16 Inlets shall be constructed in conformance with the current version of City and County of Denver Wastewater Management Division Standard Details.

Addition to 636.07 Special Fittings and Connections

Connect to existing inlet shall include required cutting of existing inlet, pipe installation and installation of a cast-in-place concrete collar to hold pipe in place and seal the inlet.

Reconnect storm pipe shall include any required cutting of pipe, additional pipe installation and installation of a cast-in-place concrete collar to hold pipe in place and seal the inlet.

Addition to 638 Measurement and Payment

Payment will be made under:

Pay Item	Pay Unit
Denver Type 16 Inlet (Single)	Each
Denver Type 16 Inlet (Triple)	Each
CDOT Inlet Type R L5 (5 foot)	Each
Connect to Existing Inlet	Each
Reconnect Storm Pipe	Each

END OF REVISION OF SECTION 630

REVISION OF SECTION 900

SEEDING, FERTILIZER, MULCHING AND SODDING

Section 900 of the Standard Specifications is hereby revised for this project as follows:

Revision of 900.05 Basis of Payment

Payment will be made under:

Pay Item	Pay Unit
Seeding	Lump Sum

Addition of 900.06 Application of Seeding

Seeding will be used within the limits of this project to establish vegetation in disturbed areas.

END OF REVISION OF SECTION 900

ADDITION OF SECTION 920

EROSION AND SEDIMENT CONTROL

Section 920 of the Standard Specifications is hereby added for this project as follows:

920.01 Description

Contractor shall reduce the effects of this project on adjacent roadways, streams and private property by implementing Best Management Practices (BMPs) in the following documents:

1. Final Stormwater Management Plan – North Chelton Road Drainage Improvement Design and Water Main Replacement, 12/20/2019 by SEH Inc.
2. City approved project construction drawings.
3. Drainage Criteria Manual Volume 2, Stormwater Quality Policies, Procedures and Best Management Practices (BMPs), City of Colorado Springs Engineering Division.

920.03 Measurement and Payment

The contract price for each item of work noted in the Bid Proposal shall be full compensation for furnishing all materials, tools, equipment, installation and labor necessary to install, maintain, and remove construction BMPs in accordance with the plans and the specifications. Contractor inspection and record keeping will not be paid separately but included in pay item.

Payment will be made under:

Pay Item	Pay Unit
Erosion Control	Lump Sum
Construction Fence	Linear Foot

END OF REVISION OF SECTION 920

REVISION OF SECTION 1000

Utilities

Section 1000 of the Standard Specifications is hereby added to this project as follows:

1000.01 Description

Contractor shall furnish all labor, materials, supplies, equipment, tools, and transportation to perform all operations related to and reasonably incidental to the completion of the utility relocations.

Please note that dewatering is incidental to the asset installation. Tracer wire system must be installed with all underground utilities and is also considered incidental to pipe construction.

Addition to 1000.02 Method of Measurement

4”/6”/8”/12” C900

Plastic waterline shall include associated trenching, bedding and compaction required for installation of line. Corrosion protection and tracer wire are considered incidental to pipe installation and will not be paid for separately.

12” 11.25 Degree Bend; 6”/12” 22.5 Degree Bend; 4”/6”/12” 45 Degree Bend; 8”x6”/12”x6” Swivel Tee; 12”x12” Cross; 12”x4”/ 12”x6”/ 12”x8” Tee; 6”x4”/ 8”x4”/ 8”x6”/ 12”x6” Reducer; 6”/12” High Deflection Coupling

Fittings shall include associated trenching, bedding, joint restraint, polyethylene wrap, thrust blocks, gravity blocks, mechanical joint restraint and recompaction required for installation of fitting, complete in place.

4”/6”/8”/12” Gate Valve

Gate valve shall include associated valve box, valve box cover, operator extension, trenching, bedding, joint restraint, thrust blocks, polyethylene wrap, gravity blocks and compaction required for installation of valve, complete in place.

Fire Hydrant Assembly

Fire hydrant assembly shall include associated trenching, bedding, joint restraint, thrust blocks, polyethylene wrap, gravity blocks and compaction required for installation of fire hydrant, complete in place.

Concrete Reverse Anchor

Concrete reverse anchor shall include associated trenching, bedding and compaction required for installation of anchor. Concrete and rebar is to conform to Detail A4-8 of Colorado Springs Utilities water line extension and service standards.

Flowable Fill

Flowable Fill shall include associated trenching, bedding and compaction required for installation of flowable fill in conformance with Detail A7-6 of Colorado Springs Utilities water line extension and service standards.

Water Service Reconnection

Water Service Reconnection shall include new tap on main, coupler fittings, service pipe of matching size and material as existing service, associated trenching, bedding and compaction, and connection to existing service. Pipe length is illustrated on plan and shall be paid by reconnection completed regardless of actual length variation from plan.

Bollard

Bollard shall include associated trenching and compaction required for installation of bollard in conformance with Detail A5-4 of Colorado Springs Utilities water line extension and service standards.

Addition to 1000.03 Basis of Payment

Payment will be made under:

Pay Item	Pay Unit
4”/6”/8”/12” C900	LF
4”/6”/8”/12” Gate Valve	EACH
12” 11.25 Degree Bend	EACH
6”/12” 22.5 Degree Bend	EACH
4”/6”/12” 45 Degree Bend	EACH
12”x12” Cross	EACH
8”x6”/ 12”x6” Swivel Tee	EACH
12”x4”/ 12”x6”/ 12”x8” Tee	EACH
6”x4”/ 8”x4”/ 8”x6”/ 12”x6” Reducer	EACH
6”/ 12” High Deflection Coupling	EACH
Water Service Reconnection	EACH
Fire Hydrant Assembly	EACH
Bollard	EACH
Flowable Fill	CY
Concrete Reverse Anchor	EACH

END OF SECTION 1000

REVISION OF SECTION 1100

CONSTRUCTION SURVEYING

Section 1100 of the Standard Specifications is hereby added for this project as follows:

1101 DESCRIPTION

This work consists of the construction surveying, calculating, and staking necessary for the construction of all elements of the project, as well as identification of all temporary and permanent easements and/or right-of-way lines. The work shall be done under the supervision of a Professional Land Surveyor (PLS) who is licensed in the State of Colorado.

Locating, preserving, referencing, installing and restoring land monuments such as Primary Control monuments from which the Right of Way or any land boundary will be calculated, described or monumented, Public Land Survey System (PLSS) monuments, General Land Office (GLO) monuments, Bureau of Land Management (BLM) monuments, Mineral Survey (MS) monuments, Right of Way (ROW) monuments, property boundary monuments and offsets, range points, benchmarks, easement monuments, and other monuments that are required by law or regulation to be established by a PLS, and the determination of any land boundary, shall be done under the supervision of a Professional Land Surveyor (PLS) who is licensed in the State of Colorado.

1102 MATERIALS AND EQUIPMENT

The Contractor shall furnish all personnel, survey equipment, safety equipment, materials, and traffic control necessary to perform the required construction surveying and staking. All surveying equipment, including Electronic Distance Meters (EDM), total stations, theodolites, levels, rods, tapes, tripods, tribrachs, and Global Positioning System (GPS) receivers and equipment.

If any survey equipment is found to be functioning outside the manufacturer’s specified tolerance, certification from an approved repair facility showing that the instruments have been repaired, properly adjusted, or both if necessary shall be included in the survey records and submitted to the City Surveyor’s Office before being used.

1103 CONSTRUCTION REQUIREMENTS

1103.01 The Contractor shall check and verify all established Primary horizontal and vertical control points.

All survey records generated shall be the property of the City and shall be available to the City Surveyor’s Office for inspection or reproduction at all times. All survey records shall be transmitted to the City Surveyor’s Office for inclusion into the project records before final project acceptance.

Electronic formats may be acceptable. Please coordinate with the City Surveyor’s Office.

Copies of any new Monument Records filed by the PLS with the State Board of Registration shall be submitted to the City Surveyor prior to filing.

1103.02 Contractor Surveying. The Contractor's PLS shall perform all construction surveying and staking that is necessary for construction of the project.

1103.03 Staking. It is the responsibility of the Contractor's PLS to adhere to industry standards and acceptable practices in regards to staking. Any restaking will be the responsibility of the Contractor's PLS at no cost to the City.

1103.04 Accuracy and Tolerances. It is the responsibility of the Contractor's PLS to adhere to industry standards and applicable standards with regard to horizontal and vertical accuracy tolerances.

1103.05 Responsibility and Inspection. Supervision and coordination of construction surveying and staking is the Contractor's responsibility. The City Surveyor's Office or Engineer may inspect the Contractor's surveying; however such inspection will not relieve the Contractor of any responsibility for accuracy or completeness of work. All Contractor surveying inaccuracies, errors, or omissions shall be corrected at the Contractor's expense.

1103.06 Reset Monuments and Stakes. Survey monuments, benchmarks, and other significant stakes that are damaged, destroyed, or made inaccessible by the progress of construction shall be replaced, transferred or reestablished at the Contractor's expense.

1103.07 Changes. All changes in lines and grades required by field conditions and all discrepancies in grades, alignment, location or dimensions detected by the Contractor shall be immediately submitted to the City in writing. No changes in given data or plans will be allowed unless approved by the City in writing. All changes shall be documented by the Contractor.

1103.08 Pay Quantities Measurements. The City will perform all interim and final measurements deemed necessary by the City to determine contract pay quantities. The Contractor shall establish and maintain Control points and stationing as required for these measurements.

1103.09 Survey Records. Survey records shall be completed as the work is done. Field survey notes for construction surveying and checking by the Contractor shall be recorded in survey records in conformance with industry standards and acceptable practices.

All survey records generated shall be the property of the City and shall be available to the City Surveyor's Office for inspection or reproduction at all times. All survey records shall be transmitted to the City Surveyor's Office for inclusion into the project records before final project acceptance. All survey records shall be stamped with the seal of, and signed by, the responsible PLS.

Electronic submittal of survey records may be acceptable. Please coordinate with the City Surveyor's Office.

1104 METHOD OF MEASUREMENT

Construction surveying will not be measured but will be paid for on a lump sum basis.

1105 BASIS OF PAYMENT

Payment for construction surveying will be the contract lump sum bid and will be full compensation for all surveying work necessary to complete the project to include all resetting of stakes, marks, monuments and preparing survey documentation as required.

Partial payment for construction surveying, as determined by the Engineer, will be made as the work progresses.

Payment will be made under:

Pay Item	Pay Unit
Construction Surveying	Lump Sum

END OF SECTION 1100

SCHEDULE D – SCOPE OF WORK

Construct storm drainage improvements to include piping, manholes and inlets. Construct 12-inch water main and appurtenances, remove existing water main lines and repave North Chelton Road (NCR) from Maizeland to Colorado Springs Charter Academy. Watermain will also have to be extended to south side of Maizeland Road. After utilities are installed, NCR will be repaved.

Project is funded locally through SWENT and CSU.

North Chelton Road (NCR) can be closed for through traffic while construction takes place. Contractor will need to maintain access for local traffic for those residences who live adjacent to NCR or who live on Jend Lane, Austin Lane, Pine Bluff Road and Ceresa Lane (north and east of NCR).

School safety (for students who walk to school and for pupil drop off and pick up) will be an important factor for this project. Contractor shall provide safe corridor of for school pedestrian traffic at all times.

CSU gas will be replacing a 4-inch gas main under NCR during this project from Maizeland to Colorado Springs Charter Academy. Contractor will facilitate their work by completing removals of asphalt necessary for their construction crews to install the gas main or tie over services.

SCHEDULE E – CONSTRUCTION PLAN SET

SCHEDULE F - EXHIBITS

Exhibit 1	Sample Contract
Exhibit 2	Minimum Insurance Requirements
Exhibit 3	Qualification Statement
Exhibit 4	Representations and Certifications
Exhibit 5	Bid Bond
Exhibit 6	Notification of Utilities
Exhibit 7	Geotechnical Report

EXHIBIT 1 SAMPLE CONTRACT

CONSTRUCTION CONTRACT

Contract Number:		Project Name/Title	
Vendor/Contractor			
Contact Name:		Telephone:	
Email Address:			
Address:			
Federal Tax ID #		Please check one:	☐ Corporation ☐ Individual ☐ Partnership
City Contracting Specialist	Name & Phone#	City Dept Rep	Name & Phone# & Department Name
NOT TO EXCEED Contract Amount:		City Account #	Acct Code (5) Fund (3) Dept (4) Project (7)
Contract Type:		Period of Performance:	

1. INTRODUCTION

THIS *TYPE* CONTRACT ("Contract") is made and entered into this ___ day of _____, 2018 by and between the City of Colorado Springs, a Colorado municipal corporation and home rule city, in the County of El Paso, State of Colorado, (the "City"), and _____ (the "Contractor").

THE CITY AND THE CONTRACTOR HEREBY AGREE AS FOLLOWS:

The City has heretofore prepared the necessary Contract Documents for the following Activity: XXXXXXXX.

The Contractor did on the ____ day of _____, 2018 submit to the City the Contractor's written offer and proposal to do the work therein described under the terms and conditions therein set forth and furnish all materials, supplies, labor, services, transportation, tools, equipment, and parts for said work in strict conformity with the accompanying Contract Documents, which are attached hereto and incorporated herein by this reference, including the following:

1. This Contract
2. Appendix A – Additional Terms and Conditions
3. Appendix B – Contractor's Proposal,
4. Appendix C – Statement of Work.
5. Schedule A – Proposal Price Sheet
6. Schedule B – General Construction Terms and Conditions
7. Schedule C – Special Construction Terms and Conditions

8. Schedule D – General Specifications
9. Schedule E – Special Specifications
10. Exhibit 1 – Performance Bond
11. Exhibit 2 – Labor and Material Payment Bond
12. Exhibit 3 – Maintenance Bond
13. Exhibit 4 – Notification of Utilities
14. Exhibit 5 – Project Schedule

2. COMPENSATION/CONSIDERATION

If FFP:

THIS FIRM FIXED PRICE CONTRACT is established at firm fixed amount of $xxxxxxxx.

Subject to the terms and conditions of the Contract Documents, Contractor shall provide all materials, supplies, labor, services, transportation, tools, equipment, and parts to perform _____ services for the City of Colorado Springs in a good and workmanlike manner to the satisfaction of the City for the total contract amount designated above and in the Notice of Award, to be paid by the City to the Contractor.

If T&M

Subject to the terms and conditions of the Contract Documents, Contractor shall provide all materials, supplies, labor, services, transportation, tools, equipment, and parts to perform _____ services for the City of Colorado Springs in a good and workmanlike manner to the satisfaction of the City for the estimated price of _____ , not to exceed $_____ ("Not to Exceed estimate"). If the performance of this Contract involves the services of others or the furnishing of equipment, supplies, or materials, the Contractor agrees to pay for the same in full. At the time of payment by the City, the Contractor shall certify in writing that said payments have been so made.

This is a Time and Material (T&M) type contract. The Not to Exceed estimate is in accordance with the Contractor's T&M proposal and rates, as included in the attached proposal, dated XXXXXX. All labor charges shall be in accordance with the T&M rates provided therein. Invoiced hours shall be subject to City review and approval before payable.

The parties estimate that performance of this Contract will not exceed the Not to Exceed estimate. The Contractor shall notify the City Contracts Specialist in writing whenever it has reason to believe that the costs the Contractor expects to incur under this Contract in the following 60 days, when added to all costs previously incurred, will exceed 75 percent of the estimated cost specified herein; or the total cost for the performance of this Contract will be either greater or substantially less than had been previously estimated. As part of the notification, the Contractor shall

provide the Contracts Specialist a revised estimate of the total cost of performing this Contract.

The City is not liable for any costs above the Not to Exceed estimate, and the Contractor is not obligated to continue performance under this Contract (including actions under the Termination clause of this Contract) or otherwise incur costs in excess of the Not to Exceed estimate specified herein, until the City Contracts Specialist

(i) notifies the Contractor in writing that the estimated cost has been increased and

(ii) provides a revised estimated total not to exceed price of performing this Contract.

IF FIXED UNIT PRICE

THIS FIXED UNIT PRICE CONTRACT is established at the Not to Exceed amount of $xxxxxxxx.

Subject to the terms and conditions of the Contract Documents, Contractor agrees to furnish all materials and to perform all work as set forth in its proposal and as required by the Contract Documents.

All pricing is in accordance with the fixed unit prices found in Schedule A, as proposed by the Contractor. Payment made for actual quantities as set forth in Schedule B, General Construction Terms and Conditions. At no time shall the total obligation of the City exceed the not to exceed amount of this Contract.

3. TERM OF CONTRACT

Contractor will start work promptly after the Notice to Proceed and continue to work diligently until completed. The Contractor shall complete all work on an as ordered basis throughout the Contract period which is **_____ Calendar Days** after the Notice-to-Proceed ("Period of Performance") as per the specifications and drawings. The Contractor shall provide a two-year guarantee on all work performed under this Contract after the job has been completed and accepted.

4. INSURANCE

The Contractor shall provide and maintain acceptable Insurance Policy(s) consistent with the Minimum Insurance Requirements attached as Schedule F, which includes Property, Liability, and as otherwise listed in Schedule F. The City of Colorado Springs shall be reflected as an additional insured on the Property and Liability policy(s).

Further, Contractor understands and agrees that Contractor shall have no right of coverage under any existing or future City comprehensive, self, or personal injury

policies. Contractor shall provide insurance coverage for and on behalf of Contract that will sufficiently protect Contractor, or Contractor's agents, employees, servants or other personnel, in connection with the services which are to be provided by Contractor pursuant to this Contract, including protection from claims for bodily injury, death, property damage, and lost income. Contractor shall provide worker's compensation insurance coverage for Contractor and all Contractor personnel. Contractor shall file applicable insurance certificates with the City and shall also provide additional insurance as indicated in this Contract. ***A CURRENT CERTIFICATE OF INSURANCE IS REQUIRED PRIOR TO COMMENCEMENT OF SERVICES LISTING THE CITY AS ADDITIONALLY INSURED.***

5. RESPONSIBILITY OF THE CONTRACTOR

A. The Contractor shall be responsible for the professional quality, technical accuracy, and the coordination of all Scope of Work services furnished by the Contractor under this Contract. The Contractor shall, without additional compensation, correct or revise any errors or deficiencies in services provided under this Contract to the satisfaction of the City.

B. The City's review, approval of, acceptance of, or payment for the services required under this Contract shall not be construed to operate as a waiver of any rights under this Contract or of any cause of action arising out of the performance of this Contract, and the Contractor shall be and remain liable to the City for any and all damages to the City caused by the Contractor's negligent performance of any of the services furnished under this Contract.

C. The rights and remedies of the City provided for under this Contract are in addition to any other rights and remedies provided by law.

D. If the Contractor is comprised of more than one legal entity, each such entity shall be jointly and severally liable hereunder.

6. WORK OVERSIGHT

A. The extent and character of the work to be done by the Contractor shall be subject to the general approval of the City’s delegated Project Manager.

B. If any of the work or services being performed does not conform with Contract requirements, the City may require the Contractor to perform the work or services again in conformity with Contract requirements, at no increase in Contract amount. When defects in work or services cannot be corrected by re-performance, the City may (1) require the Contractor to take necessary action to ensure that future performance conforms to Contract requirements and (2) reduce the Contract price to reflect the reduced value of the work or services performed.

C. If the Contractor fails to promptly perform the defective work or services again or to take the necessary action to ensure future performance is in conformity with Contract requirements, the City may (1) by Contract or otherwise, perform the services and charge to the Contractor any cost incurred by the City that is directly related to the performance of such work or service or (2) terminate the Contract for breach of contract.

7. SUBCONTRACTORS, ASSOCIATES, AND OTHER CONTRACTORS

A. Any subcontractor, outside associates, or other contractors used by the Contractor in connection with Contractor's work under this Contract shall be limited to individuals or firms that are specifically identified by the Contractor in the Contractor's proposal and agreed to by the City. The Contractor shall obtain the City's Project Manager's written consent before making any substitution of these subcontractors, associates, or other contractors.

B. The Contractor shall include a flow down clause in all of its subcontracts, agreements with outside associates, and agreements with other contractors. The flow down clause shall cause all of the terms and conditions of this Contract, including all of the applicable parts of the Contract Documents, to be incorporated into all subcontracts, agreements with outside associates, and agreements with other contractors. The flow down clause shall provide clearly that there is no privity of contract between the City and the Contractor's subcontractors, outside associates, and other contractors.

8. KEY PERSONNEL

The key personnel listed in the proposal and/or below will be the individuals used in the performance of the work. If any of the listed key personnel leave employment or are otherwise not utilized in the performance of the work, approval to substitute must be obtained by the Contractor from the City's Project Manager. Any substitute shall have the same or a higher standard of qualifications that the key personnel possessed at the time of Contract award.

9. START AND CONTINUANCE OF WORK

It is further agreed that the Contractor will start work promptly and continue to work diligently until this Contract is completed.

10. APPROPRIATION OF FUNDS

This Contract is expressly made subject to the limitations of the Colorado Constitution and Section 7-60 of the Charter of the City of Colorado Springs. Nothing herein shall constitute, nor be deemed to constitute, the creation of a debt or multi-year fiscal obligation or an obligation of future appropriations by the City Council of Colorado Springs, contrary to Article X, § 20, Colo. Const., or any other

constitutional, statutory, or charter debt limitation. Notwithstanding any other provision of this Contract, with respect to any financial obligation of the City which may arise under this Agreement in any fiscal year after the year of execution, in the event the budget or other means of appropriation for any such year fails to provide funds in sufficient amounts to discharge such obligation, such failure (i) shall act to terminate this Contract at such time as the then-existing and available appropriations are depleted, and (ii) neither such failure nor termination shall constitute a default or breach of this Contract, including any sub-agreement, attachment, schedule, or exhibit thereto, by the City. As used herein, the term “appropriation” shall mean and include the due adoption of an appropriation ordinance and budget and the approval of a Budget Detail Report (Resource Allocations) which contains an allocation of sufficient funds for the performance of fiscal obligations arising under this Contract.

11. CHANGES

The Contractor and the City agree and acknowledge as a part of this Contract that no change order or other form or order or directive may be issued by the City which requires additional compensable work to be performed, which work causes the aggregate amount payable under the Contract to exceed the amount appropriated for this Contract as listed above, unless the Contractor has been given a written assurance by the City that lawful appropriations to cover the costs of the additional work have been made or unless such work is covered under a remedy-granting provision of this Contract. The Contractor and the City further agree and acknowledge as a part of this Contract that no change order or other form or order or directive which requires additional compensable work to be performed under this Contract shall be issued by the City unless funds are available to pay such additional costs, and, regardless of any remedy-granting provision included within this Contract, the Contractor shall not be entitled to any additional compensation for any change which increases or decreases the Contract completion date, or for any additional compensable work performed under this Contract, and expressly waives any rights to additional compensation, whether by law or equity, unless, prior to commencing the additional work, the Contractor is given a written change order describing the change in Contract completion date or the additional compensable work to be performed, and setting forth the amount of compensation to be paid, and such change order is signed by the authorized City representative, as defined below. The amount of compensation to be paid, if any, shall be deemed to cover any and all additional, direct, indirect or other cost or expense or profit of the Contractor whatsoever. It is the Contractor's sole responsibility to know, determine, and ascertain the authority of the City representative signing any change order under this Contract.

No change, amendment, or modification to this Contract shall be valid unless duly approved and issued in writing by the City of Colorado Springs Procurement Services Division. The City shall not be liable for any costs incurred by the Contractor resulting from work performed for changes not issued in writing by the City of Colorado Springs Procurement Services Division.

The following personnel are authorized to sign changes, amendments, or modifications to this Contract.

The Project Manager: Changes up to $14,999.99
The City of Colorado Springs Chief of Staff: Changes up to $499,999.99
The Mayor of the City of Colorado Springs: Unlimited

12. ASSIGNMENT

No assignment or transfer by the Contractor of this Contract or any part thereof or of the funds to be received thereunder by the Contractor will be recognized unless such assignment has had the prior written approval of the City and the surety has been given due notice of such assignment. Such written approval by the City shall not relieve the Contractor of the obligations under the terms of this Contract. In addition to the usual recitals in assignment contracts, the following language must be included in the assignment:

It is agreed that the funds to be paid to the assignee under this assignment are subject to a prior lien for services rendered or materials supplied for the performance of the work called for in said contract in favor of all persons, firms, or corporations rendering such services or supplying such materials.

13. CHOICE OF LAW

This Contract is subject to and shall be interpreted under the law of the State of Colorado, and the Charter, City Code, Ordinances, Rules and Regulations of the City of Colorado Springs, Colorado, a Colorado home rule city. Court venue and jurisdiction shall be exclusively in the Colorado District Court for El Paso County, Colorado. The Parties agree that the place of performance for this Contract is deemed to be in the City of Colorado Springs, El Paso County, State of Colorado. The Contractor shall ensure that the Contractor and the Contractor's employees, agents, officers and subcontractors are familiar with, and comply with, applicable Federal, State, and Local laws and regulations as now written or hereafter amended.

14. WORKERS' COMPENSATION INSURANCE

Contractor shall take out and maintain during the Period of Performance, Colorado Worker's Compensation Insurance for the Contractor and all employees of the Contractor. If any service is sublet by the Contractor, the Contractor shall require the subcontractor to provide the same coverage for the subcontractor and subcontractor's employees. Workers' Compensation Insurance shall include occupational disease provisions covering any obligations of the Contractor in accord with the provisions of the Workers' Compensation Act of Colorado.

15. INDEMNIFICATION

Contractor agrees that the Contractor shall indemnify, defend and hold harmless the City, its officers, employees and agents, from and against any and all loss, damage, injuries, claims, cause or causes of action, or any liability whatsoever resulting from, or arising out of, or in connection with the Contractor's obligations or actions under this Contract caused by any willful or negligent error, omission or act or a failure to observe any applicable standard of care by the Contractor or any person employed by it or anyone for whose acts the Contractor is legally liable. In consideration of the award of this Contract, to the extent damages are covered by insurance, the Contractor agrees to waive all rights of subrogation against the City, its subsidiary, parent, associated and/or affiliated entities, successors, or assigns, its elected officials, trustees, employees, agents, and volunteers for losses arising from the work performed by the Contractor for the City.

The indemnification obligation shall survive the expiration or termination of this Contract.

16. INDEPENDENT CONTRACTOR

In the performance of the Contractor's obligations under this Contract, it is understood, acknowledged and agreed between the parties that the Contractor is at all times acting and performing as an independent contractor, and the City shall neither have nor exercise any control or direction over the manner and means by which the Contractor performs the Contractor's obligations under this Contract, except as otherwise stated within the Contract terms. The City shall not provide any direction to the Contractor on the work necessary to complete the project. Contractor understands that it is an independent contractor responsible for knowing how to perform all work or tasks necessary to complete project. The Contractor understands and agrees that the Contractor and the Contractor's employees, agents, servants, or other personnel are not City employees. The Contractor shall be solely responsible for payment of salaries, wages, payroll taxes, unemployment benefits or any other form of compensation or benefit to the Contractor or any of the Contractor's employees, agents, servants or other personnel performing services or work under this Contract, whether it is of a direct or indirect nature. Further in that regard, it is expressly understood and agreed that for such purposes neither the Contractor nor the Contractor's employees, agents, servants or other personnel shall be entitled to any City payroll, insurance, unemployment, worker's compensation, retirement or any other benefits whatsoever.

17. APPLICABLE LAW AND LICENSES

In the conduct of the services or work contemplated in this Contract, the Contractor shall ensure that the Contractor and all subcontractors comply with all applicable state, federal and City and local law, rules and regulations, technical standards or specifications. The Contractor shall qualify for and obtain any required licenses prior to commencement of work.

18. PRIOR AGREEMENTS

This is a completely integrated Contract and contains the entire agreement between the parties. Any prior written or oral agreements or representations regarding this Contract shall be of no effect and shall not be binding on the City. This Contract may only be amended in writing, and executed by duly authorized representatives of the parties hereto.

19. INTELLECTUAL PROPERTY

The Parties hereby agree, and acknowledge, that all products, items writings, designs, models, examples, or other work product of the Contractor produced pursuant to this Contract are works made for hire, and that the City owns, has, and possesses any and all ownership rights and interests to any work products of the Contractor made under this Contract, including any and all copyright, trademark, or patent rights, and that compensation to the Contractor for Agreement and acknowledgment of this intellectual property right section of this Contract is included in any compensation or price whatsoever paid to the Contractor under this Contract. It is the intent of the parties that the City shall have full ownership and control of the Contractor's work products produced pursuant to this Contract, and the Contractor specifically waives and assigns to the City all rights which Contractor may have under the 1990 Visual Artists Rights Act, federal, and state law, as now written or later amended or provided. In the event any products, items writings, designs, models, examples, or other work product produced pursuant to this Contract is deemed by a court of competent jurisdiction not to be a work for hire under federal copyright laws, this intellectual property rights provision shall act as an irrevocable assignment to the City by the Contractor of any and all copyrights, trademark rights, or patent rights in the Contractor's products, items writings, designs, models, examples, or other work product produced pursuant to this Contract, including all rights in perpetuity. Under this irrevocable assignment, the Contractor hereby assigns to the City the sole and exclusive right, title, and interest in and to the Contractor's products, items writings, designs, models, examples, or other work product produced pursuant to this Contract, without further consideration, and agrees to assist the City in registering and from time to time enforcing all copyrights and other rights and protections relating to the Contractor's products, items writings, designs, models, examples, or other work product in any and all countries. It is the Contractor's specific intent to assign all right, title, and interest whatsoever in any and all copyright rights in the Contractor's products, items writings, designs, models, examples, or other work product produced pursuant to this Contract, in any media and for any purpose, including all rights of renewal and extension, to the City. To that end, the Contractor agrees to execute and deliver all necessary documents requested by the City in connection therewith and appoints the City as Contractor's agent and attorney-in-fact to act for and in Contractor's behalf and stead to execute, register, and file any such applications, and to do all other lawfully permitted acts to further the registration, prosecution, issuance, renewals, and extensions of copyrights or other protections with the same legal force and effect as if executed by

the Contractor; further, the parties expressly agree that the provisions of this intellectual property rights section shall be binding upon the parties and their heirs, legal representatives, successors, and assigns.

20. WAIVERS

No waiver of default by the City of any of the terms, covenants, and conditions hereof to be performed, kept, and observed by the Contractor shall be construed, or shall operate, as a waiver of any subsequent default of any of the terms, covenants, or conditions herein contained to be performed, kept, and observed by the Contractor.

21. THIRD PARTIES

It is expressly understood and agreed that enforcement of the terms and conditions of this Contract, and all rights of action relating to such enforcement, shall be strictly reserved to the Parties hereto, and nothing contained in this Contract shall give or allow any such claim or right of action by any other or third person or entity on such Contract. It is the express intention of the Parties hereto that any person or entity, other than the Parties to this Contract, receiving services or benefits under this Contract shall be deemed to be incidental beneficiaries only.

22. TERMINATION

A. Termination for Convenience.
By signing this Contract, Contractor represents that it is a sophisticated business and enters into the Contract voluntarily, has calculated all business risks associated with this Contract, and understands and assumes all risks of being terminated for convenience, whether such risks are known or not known. Contractor agrees that the City may terminate this Contract at any time for convenience of the City, upon written notice to the Contractor. Contractor expressly agrees to and assumes the risk that the City shall not be liable for any costs or fees of whatsoever kind and nature if termination for convenience occurs before Contractor begins any work or portion of the work. Contractor further expressly agrees and assumes the risks that the City shall not be liable for any unperformed work, anticipated profits, overhead, mobilizations costs, set-up, demobilization costs, relocation costs of employees, layoffs or severance costs, administrative costs, productivity costs, losses on disposal of equipment or materials, cost associated with the termination of subcontractors, costs associated with purchase orders or purchases, or any other costs or fees of any kind and nature, if Contractor has started or performed portions of the Contract prior to receiving notice from the City. The City shall be liable only for the portions of work Contractor actually satisfactorily completed up to the point of the issuance of the Notice of Termination for convenience. Upon receipt of this notice the Contractor shall immediately: discontinue all services affected (unless the notice directs otherwise), and deliver to the City all data, drawings, specifications,

reports, estimates, summaries, and other information and materials accumulated in performing this Contract, whether completed or in process.

B. Termination for Cause: The occurrence of any one or more of the following events ("Event of Default") will justify termination for cause:

i. Contractor's failure to perform the work in accordance with the Contract Documents (including, but not limited to, failure to supply sufficient skilled workers or suitable materials or equipment or failure to adhere to the progress schedule as adjusted from time to time.

ii. Contractor's disregard of the laws or regulations of any public body having jurisdiction.

iii. Contractor's disregard of the authority of Project Manager.

iv. Contractor's violation in any material provision of the Contract Documents.

v. Contractor's failure to make prompt payments to its subcontractors, and suppliers of any tier, or laborers or any person working on the work by, through, or under the Contractor or any of them, any all of their employees, officers, servants, members, and agents.

vi. Contractor files a petition commencing a voluntary case under the U.S. Bankruptcy Code, or for liquidation, reorganization, or an arrangement pursuant to any other U.S. or state bankruptcy Laws, or shall be adjudicated a debtor or be declared bankrupt or insolvent under the U.S. Bankruptcy Code, or any other federal or state laws relating to bankruptcy, insolvency, winding-up, or adjustment of debts, or makes a general assignment for the benefit of creditors, or admits in writing its inability to pay its debts generally as they become due, or if a petition commencing an involuntary case under the U.S. Bankruptcy Code or an answer proposing the adjudication of Contractor as a debtor or bankrupt or proposing its liquidation or reorganization pursuant to the Bankruptcy Code or any other U.S. federal or state bankruptcy laws is filed in any court and Contractor consents to or acquiesces in the filing of that pleading or the petition or answer is not discharged or denied within sixty (60) Calendar Days after it is filed.

vii. A custodian, receiver, trustee or liquidator of Contractor, all or substantially all of the assets or business of Contractor, or of Contractor's interest in the Work or the Contract, is appointed in any proceeding brought against Contractor and not discharged within sixty (60) Calendar Days after that appointment, or if Contractor shall consent to or acquiesces in that appointment.

viii. Contractor fails to commence correction of defective work or fails to correct defective work within a reasonable period of time after written notice.

If one or more of the events identified in Paragraphs i-viii above occur, City may give Contractor written notice of the event and direct the event be cured. Any such Notice to Cure will provide Contractor a minimum of ten (10) calendar days to prepare and submit to the Project Manager a plan to correct the Event of Default. If such plan to correct the Event of Default is not submitted to the Project Manager within ten (10) days after the date of the written notice or such plan is unacceptable to the City, the City may, give Contractor (and the Surety, if any) written notice that Contractor's services are being terminated for cause. Upon delivery of the termination notice, City may terminate the services of Contractor in whole or in part, exclude Contractor from the site, and take possession of the work and of all Contractor's tools, appliances, construction equipment, and machinery at the project site, and use the same to the full extent they could be used by Contractor (without liability to Contractor for trespass or conversion), incorporate in the work all materials and equipment stored at the site or for which City has paid Contractor but which are stored elsewhere, and finish the work as City may deem expedient. In such case, Contractor shall not be entitled to receive any further payment until Certificate of Completion of the work. In the event City terminates this Contract for Cause and the cost of completing the work exceeds the unpaid balance of the Contract price, Contractor shall pay City for any costs of completion which exceed the Contract price when combined with all amounts previously paid to Contractor. When exercising any rights or remedies under this paragraph City shall not be required to obtain the lowest price for the work performed. Should the cost of such completion, including all proper charges, be less than the original Contract price, the amount so saved shall accrue to the City. Neither the City nor any officer, agent or employee of the City shall be in any way liable or accountable to the Contractor or the Surety for the method by which the completion of the said work, or any portion thereof, may be accomplished or for the price paid.

Where Contractor's services have been so terminated by City, the termination will not affect any rights or remedies of City against Contractor or Surety then existing or which may thereafter accrue. Any retention or payment of moneys due Contractor by City will not release Contractor from liability.

C. Termination Notice. Upon receipt of a termination notice, whether for convenience or cause, the Contractor shall immediately: discontinue all services affected (unless the notice directs otherwise), and deliver to the City all data, drawings, specifications, reports, estimates, summaries, and other information and materials accumulated in performing this Contract, whether completed or in process.

D. Removal of Equipment. Except as provided above, in the case of termination of this Contract before completion from any cause whatever, the Contractor, if notified to do so by the City, shall promptly remove any part or all of Contractor's equipment and supplies from the property of the City, failing which the City shall have the right to remove such equipment and supplies at the expense of the Contractor.

23. BOOKS OF ACCOUNT AND AUDITING

The Contractor shall make available to the City if requested, true and complete records, which support billing statements, reports, performance indices, and all other related documentation. The City's authorized representatives shall have access during reasonable hours to all records, which are deemed appropriate to auditing billing statements, reports, performance indices, and all other related documentation. The Contractor agrees that it will keep and preserve for at least seven years all documents related to the Contract which are routinely prepared, collected or compiled by the Contractor during the performance of this Contract.

The City's Auditor and the Auditor's authorized representatives shall have the right at any time to audit all of the related documentation. The Contractor shall make all documentation available for examination at the Auditor's request at either the Auditor's or Contractor's offices, and without expense to the City.

24. ILLEGAL ALIENS

Illegal Aliens - Public Contracts for Services - Compliance with Title 8, Article 17.5, Colorado Revised Statutes: The Contractor acknowledges, understands, agrees, and certifies that: In the performance of any work or the provision of any services by the Contractor under this Contract, the Contractor shall not knowingly employ or contract with an illegal alien to perform work under this Contract; or enter into a contract with any subcontractor that fails to certify to the Contractor that the subcontractor shall not knowingly employ or contract with an illegal alien to perform work under this Contract or under the subcontract to this Contract. The Contractor certifies in accord with Section 8-17.5-102(1) C.R.S. that, on the date the Contractor signs this Contract, the Contractor does not knowingly employ or Contract with an illegal alien who will perform work under this Contract and that the Contractor shall participate in the e-verify program or Colorado Department of Labor and Employment program in order to confirm the employment eligibility of all employees who are newly hired for employment or to perform work under this Contract. The Contractor is expressly prohibited from using the e-verify program or Colorado Department of Labor and Employment program procedures to undertake pre-employment screening of job applicants while this Contract and any services under this Contract are being performed. If the Contractor obtains actual knowledge that a subcontractor performing work under this Contract for services knowingly employs or contracts with an illegal alien, the Contractor shall notify the subcontractor and the City within three days that the Contractor has actual knowledge that the subcontractor is employing or contracting with an illegal alien, and terminate the subcontract with the subcontractor if within three days of receiving the notice the subcontractor does not stop employing or contracting with the illegal alien; except that the Contractor shall not terminate the Contract with the subcontractor if during the three days the subcontractor provides information to establish that the subcontractor has not knowingly employed or contracted with an illegal alien. The

Contractor shall comply with any request by the City, federal government, or the Colorado Department of Labor and Employment made in the course of an investigation. If the Contractor violates or fails to comply with any provision of C.R.S. 8-17.5-101 et seq, the City may terminate this Contract for breach of contract. If this Contract is so terminated, the Contractor shall be liable for any actual and consequential damages to the City.

25. COMPLIANCE WITH IMMIGRATION REFORM AND CONTROL ACT OF 1986

Contractor certifies that Contractor has complied with the United States Immigration Reform and Control Act of 1986. All persons employed by Contractor for performance of this Contract have completed and signed Form I-9 verifying their identities and authorization for employment.

26. LABOR

The Contractor shall employ only competent and skilled workmen and foremen in the conduct of work on this Contract. The Contractor shall at all times enforce strict discipline and good order among Contractor's employees. The Project Manager shall have the authority to order the removal from the work of any person, including Contractor's or any subcontractor’s employees, who refuses or neglects to observe any of the provisions of these Plans or Specifications, or who is incompetent, abusive, threatening, or disorderly in conduct and any such person shall not again be employed on the Project.

In accord with the Keep Jobs in Colorado Act, codified at sections 8-17-101, et seq., C.R.S., Colorado labor shall be employed to perform the work to the extent of not less than eighty percent (80%) of each type or class of labor in the several classifications of skilled and common labor employed on this Project et seq.=; provided however, that this paragraph shall not apply if the Project receives federal funding.

In no event shall the City be responsible for overtime pay.

27. GRATUITIES

A. This Contract may be terminated if the Mayor, the Mayor’s designee, and/or the Procurement Services Manager determine, in their sole discretion, that the Contractor or any officer, employee, agent, or other representative whatsoever, of the Contractor offered or gave a gift or hospitality to a City officer, employee, agent or Contractor for the purpose of influencing any decision to grant a City contract or to obtain favorable treatment under any City contract.

B. The terms "hospitality" and "gift" include, but are not limited to, any payment, subscription, advance, forbearance, acceptance, rendering or deposit of money, services, or anything of value given or offered, including but not limited to food, lodging, transportation, recreation or entertainment, token or award.

C. Contract termination under this provision shall constitute a breach of contract by the Contractor, and the Contractor shall be liable to the City for all costs of reletting the contract or completion of the project. Further, if the Contractor is terminated under this provision, or violates this provision but is not terminated, the Contractor shall be subject to debarment under the City's Procurement Regulations. The rights and remedies of the City provided in this clause shall not be exclusive and are in addition to any other rights and remedies provided by law or under this Contract.

28. NON-DISCRIMINATION

A. In accord with section 24-34-402, C.R.S., the Contractor will not discriminate against any employee or applicant for employment because of disability, race, creed, color, sexual orientation, religion, age, national origin, or ancestry. But, with regard to a disability, it is not a discriminatory or an unfair employment practice for an employer to take into consideration disability if there is no reasonable accommodation that the employer can make with regard to the disability, the disability actually disqualifies the person from the job, and the disability has a significant impact on the job. The Contractor will take affirmative action to ensure that applicants are employed, and that employees are treated during employment without regard to their disability, race, creed, color, sexual orientation, religion, age, national origin, or ancestry. Such actions shall include, but not be limited to, the following: employment, upgrading, demotion, or transfer; recruitment or recruitment advertising; layoff or termination; rates of pay or other forms of compensation; and selection for training; including apprenticeship.

B. The Contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices to be provided setting forth the provisions of this nondiscrimination clause.

C. The Contractor will, in all solicitations or advertisements for employees placed by or on behalf of the Contractor, state that all qualified applicants will receive consideration for employment without regard to disability, race, creed, color, sexual orientation, religion, age, national origin, or ancestry.

D. Contractor will cooperate with the City in using Contractor's best efforts to ensure that Disadvantaged Business Enterprises are afforded the maximum opportunity to compete for subcontracts or work under this Contract.

29. ORDER OF PRECEDENCE

Any inconsistency in this Contract shall be resolved by giving precedence in the following order:

A. This Contract document with its terms and conditions
B. Specific Construction Terms and Conditions
C. General Construction Terms and Conditions

D. The Statement of Work
E. Specific Specifications
F. General Specifications
G. Other Appendices, Attachments, Exhibits, or Schedules

30. HEADINGS

The section headings contained in this Contract are for reference purposes only and shall not affect the meaning or interpretation of this Contract.

31. DISPUTES

A. All administrative and contractual disputes arising from or related to this Contract other than those arising under Unanticipated Circumstances provisions (in section107.27 of Schedule B General Construction Terms and Conditions) shall be addressed in the following manner:
   i. If either Party disputes or disagrees with a Contract term or the other Party's interpretation of a Contract term or has any other administrative or contractual dispute not addressed in the Unanticipated Circumstances provisions, such Party shall promptly give the other Party written notice of said dispute.
   ii. The Parties shall hold a meeting as soon as reasonably possible, but in no event later than thirty (30) calendar days from the initial written notice of the dispute, attended by persons with decision-making authority regarding the dispute, to attempt in good faith to negotiate a resolution of the dispute; provided, however, that no such meeting shall be deemed to vitiate or reduce the obligations and liabilities of the Parties or be deemed a waiver by a Party of any remedies to which such Party would otherwise be entitled unless otherwise agreed to by the Parties in writing.
   iii. If, within thirty (30) calendar days after such meeting, the Parties have not succeeded in negotiating a resolution of the dispute, they agree to submit the dispute to non-binding mediation and to bear equally the costs of the mediation.
   iv. The Parties will jointly appoint a mutually acceptable mediator. If they fail to do so within twenty (20) calendar days from the conclusion of the negotiation period, they shall each select a mediator. The two mediators will then appoint a third mediator who shall conduct mediation for the Parties as the sole mediator.
   v. The Parties agree to participate in good faith in the mediation and negotiations for a period of thirty (30) calendar days. The substantive and procedural law of the State of Colorado shall apply to the proceedings. If the Parties are not successful in resolving the dispute through mediation, then the Parties shall be free to pursue any other remedy afforded by the laws of the State of Colorado.
   vi. Until final resolution of any dispute hereunder, the Contractor shall diligently proceed with the performance of this Contract as directed by the

City. For purposes of this Contract, termination for convenience shall not be deemed a dispute. The City of Colorado Springs and the Contractor agree to notify each other in a timely manner of any claim, dispute, or cause of action arising from or related to this Contract, and to negotiate in good faith to resolve any such claim, dispute, or cause of action. To the extent that such negotiations fail, the City of Colorado Springs and the Contractor agree that any lawsuit or cause of action that arises from or is related to this Contract shall be filed with and litigated only by the Colorado District Court for El Paso County, CO.

32. DELIVERY

The City may cancel this Contract or any portion thereof if delivery is not made when and as specified, time being of the essence in this Contract. Contractor shall pay the City for any loss or damage sustained by the City because of failure to perform in accordance with this Contract.

33. PAYMENTS

All invoices shall be sent to the Project Manager identified in this Contract.

The City will pay the Contractor, upon submission of proper invoices, the prices stipulated in the Contract for services rendered and accepted, less any deductions provided in this Contract within 30 days (Net 30). The City will not pay late fees or interest. Any discount payment terms offered on the invoice may be taken by the City.

All payments for Construction will be made in accordance with the Payment provisions found in Schedule B – General Construction Terms and Conditions.

Each invoice must contain at least the following information:

Contract number, issued purchase order number, invoice number, invoice date, timeframe covered by invoice, type and amount of labor and materials used for that time period, dollar amount in unit price, extended price, and total value of invoice.

IF T&M

The City will make payments for services on a monthly basis for services performed during the previous month in accordance with this Contract. All labor Invoices shall include labor categories, rates, hours worked, and total amounts per category. All labor categories and rates charged must be included in this Contract. No other categories or rates will be allowed or payable. All labor invoices are subject to City approval.

Materials will be payable on a reimbursable basis with no additional profit, fee, overhead, handling, or General and Administrative (G&A) costs. All costs for materials shall be approved by the City Contracts Specialist before the costs are incurred and payable.

The City will pay the Contractor, upon submission of proper invoices, the prices stipulated in the Contract for services rendered and accepted, less any deductions provided in this Contract within 30 days (Net 30). The City will not pay late fees or interest. Any discount payment terms offered on the invoice may be taken by the City.

34. INSPECTION OF SERVICES

The Contractor is responsible for performing or having performed all inspections and tests necessary to substantiate that the services furnished under this Contract conform to Contract requirements, including any applicable technical requirements for specified manufacturers' parts. This clause takes precedence over any City inspection and testing required in the Contract's specifications, except for specialized inspections or tests specified to be performed solely by the City.

A. Definition of "services", as used in this clause, includes services performed, workmanship, and material furnished or utilized in the performance of services.

B. The Contractor shall provide and maintain an inspection system acceptable to the City covering the services under this Contract. Complete records of all inspection work performed by the Contractor shall be maintained and made available to the City during Contract performance and for as long afterwards as the Contract requires.

C. The City has the right to inspect and test all services called for by the Contract, to the extent practicable at all times and places during the term of the Contract. The City will perform inspections and tests in a manner that will not unduly delay the work.

D. If the City performs inspections or test on the premises of the Contractor or a subcontractor, the Contractor shall furnish, and shall require subcontractors to furnish, at no increase in Contract price, all reasonable facilities and assistance for the safe and convenient performance of these duties.

35. SECURITY

The City maintains security requirements regarding access to City buildings and other City workplaces and worksites on City property. All Contractor personnel accessing City buildings, workplaces, or worksites, may be required to produce a valid, Government issued picture identification. Contractor personnel lacking such identification may not be allowed access to such sites. No costs incurred by the

Contractor due to City security requirements shall be allowable or payable under this Contract.

36. TIME IS OF THE ESSENCE

In as much as the Contract concerns a needed or required service, the terms, conditions, and provisions of the Contract relating to the time of performance and completion of work are of the essence of this Contract. The Contractor shall begin work on the day specified and shall prosecute the work diligently so as to assure completion of the work within the number of calendar days or date specified, or the date to which the time for completion may have been extended.

37. EMPLOYMENT OF LABOR

The Contractor shall comply with, and defend and hold the City harmless from any violation of all laws and lawful rules and regulations, both of the State of Colorado and of the United States, relating to Workmen's Compensation, unemployment compensation, Social Security, payment for overtime, and all other expenses and conditions of employment under this Contract.

38. SALES TAX

The Contractor must have a tax-exemption certificate from the Colorado Department of Revenue for this project. The certificate does not apply to City of Colorado Springs Sales and Use Tax which shall be applicable. The tax exempt project number and the exemption certificate only applies to County, PPRTA (Pikes Peak Rural Transportation Authority), and State taxes when purchasing construction and building materials **to be incorporated into this project**.

Furthermore, the exemption **does not** include or apply to the purchase or rental of equipment, supplies or materials that **do not become a part of the completed project or structure**. Such purchases and rentals are subject to full applicable taxation.

All contracts with subcontractors must include the City of Colorado Springs Sales and Use Tax on the work covered by the Contract, and other taxes as applicable.

Note: For all equipment, materials and supplies incorporated into the work purchased from vendors or suppliers not licensed to collect City Sales Tax (i.e. out of state suppliers, etc.), City Use Tax is due and payable to the City. The Contractor shall execute and deliver, and shall cause the Contractor’s subcontractors to execute and deliver to the City Sales Tax Office, ST 16 forms listing all said equipment, materials and supplies and the corresponding use tax due, along with payment for said taxes. Any outstanding taxes due may be withheld from the final payment due the Contractor and may result in suspension of Contractor from bidding on City projects.

Forms and instructions can be downloaded at https://coloradosprings.gov/cat/government/tax-information/sales-tax. Questions can be directed to the City Sales Tax Division at (719) 385-5903.

Our Registration Numbers are as follows:
City of Colorado Springs
Federal I.D.: 84-6000573
Federal Excise: A-138557
State Sales Tax: 98-03479

The Contractor's payment or exemption of State of Colorado, El Paso County and City Sales and Use Taxes shall be as specified herein.

39. SEVERABILITY

If any terms, conditions, or provisions of this Contract shall be held unconstitutional, illegal, or void, such finding shall not affect any other terms, conditions, or provisions of this Contract.

40. LIABILITY OF CITY EMPLOYEES

All authorized representatives of the City are acting solely as agents and representatives of the City when carrying out and exercising the power or authority granted to them under the Contract. There shall not be any liability on them either personally or as employees of the City.

41. USE OF CITY NAME OR LOGO

Except as otherwise provided in this Contract, the Contractor shall not refer to this Contract or the City of Colorado Springs in any advertising or promotions in such a manner as to state or imply that the product or service provided is endorsed or preferred by the City of Colorado Springs, its employees, or its Departments, or is considered by these entities to be superior to other products or services. Any use of the name or logo of the City of Colorado Springs in advertising or promotions must be approved in writing by the City of Colorado Springs Contracts Specialist assigned to the Contract prior to such use.

42. TRAVEL

If travel expenses are included as a line item in this Contract, all travel expenses incurred and billable by the Contractor are subject to City approval. Air travel shall be limited to the round trip "economy coach" fare. Travel from the Colorado Springs Airport is encouraged. Unless there are extenuating circumstances, the Contract should take advantage of lower airfares by purchasing tickets more than 14 days in advance of travel. In-state travel by air must be more economical than travel by private vehicle. Use of a private vehicle may be reimbursed per mile at the current rate published by the IRS annually. Short-term parking, long-term parking or cab

fare associated with airport departure and arrival may be allowable expenses. Valet parking will not be allowed unless it is the least expensive or only option. Car rental rates may be reimbursed for car rentals no greater than the intermediate or standard classification. The City will not reimburse any other travel methods or expenses. The City will pay for lodging, meals, and miscellaneous expenses on a per diem basis only, in accordance with the current per deim rates published by the IRS annually. The City will not pay for Contractor expenses exceeding the per deim rates. Receipts for all reimbursable expenses must be provided with the Contractor's invoice.

43. APPENDICES

The following Appendices are made a part of this Agreement:

1. Appendix A – Additional Terms and Conditions
2. Appendix B – Contractor's Proposal,
3. Appendix C – Statement of Work.
4. Appendix D – Project Schedule
5. Appendix E – Exhibits from the RFP
   - Performance Bond (Exhibit 8 of the RFP)
   - Labor and Material Payment Bond (Exhibit 9 of the RFP)
   - Maintenance Bond (Exhibit 10 of the RFP)
   - Notification of Utilities (Exhibit 11 of the RFP)
6. Schedule A – Proposal Price Sheet
7. Schedule B – General Construction Terms and Conditions
8. Schedule C – Special Construction Terms and Conditions
9. Schedule D – General Specifications
10. Schedule E – Special Specifications
11. Schedule F – Insurance Requirements

CONTRACT SIGNATURE PAGE

The Contractor certifies in accord with Section 8-17.5-102(1) C.R.S. that, on the date the Contractor signs this Contract, the Contractor does not knowingly employ or Contract with an illegal alien who will perform work under this Contract and that the Contractor shall participate in the e-verify program or Colorado Department of Labor and Employment program in order to confirm the employment eligibility of all employees who are newly hired for employment or to perform work under this Contract. The Contractor is expressly prohibited from using the e-verify program or Colorado Department of Labor and Employment program procedures to undertake pre-employment screening of job applicants while this Contract and any services under this Contract are being performed.

IN WITNESS WHEREOF, the parties have caused these presents to be executed on the day and the year first above written.

This Contract is executed in one (1) original copy.

THE CITY OF COLORADO SPRINGS, COLORADO:

SECOND PARTY:	
Corporate Name	
Signature	Date
Title	

EXHIBIT 2 MINIMUM INSURANCE REQUIREMENTS

The following listed minimum insurance requirements shall be carried by all contractors and consultants unless otherwise specified in the City's solicitation package, Special Provisions, or Standard Specifications.

1.		Commercial General Liability for limits not less than $1,000,000 combined single limit with $2,000,000 aggregate for bodily injury and property damage for each occurrence. Coverage shall include blanket contractual, broad form property damage, products and completed operations.
2.		Workers' Compensation and Employers Liability as required by statute. Employers Liability coverage is to be carried for a minimum limit of $100,000.
3.		Automobile Liability covering any auto (including owned, hired, and non-owned autos) with a minimum of $1,000,000 each accident combined single limit.

Except for workers' compensation and employer's liability insurance, the **City of Colorado Springs must be named as an additional insured**. Certificates of Insurance must be submitted before commencing the work and provide 30 days' notice prior to any cancellation, non-renewal, or material changes to policies required under the contract.

All coverage furnished by contractor is primary, and any insurance held by the City of Colorado Springs is excess and non-contributory.

The undersigned certifies and agrees to carry and maintain the insurance requirements indicated above throughout the contract Period of Performance.

_____

(Name of Company)

_____

(Signature) *(Date)*

EXHIBIT 3 – QUALIFICATION STATEMENT

CITY OF COLORADO SPRINGS
QUALIFICATION STATEMENT

This statement will provide information which will enable the City to evaluate the qualifications of your firm and staff with regard to the requirements of this Invitation for Bid. Please complete this form in its entirety and submit it (in the number of copies requested) along with the other required proposal documents. If a request in the Qualification Statement is contained in the Bid, indicate the section in the Bid where that information can be found.

(PRINT)
FIRM NAME: _____
ADDRESS: _____
CITY STATE ZIP: _____
AUTHORIZED REPRESENTATIVE: _____
TITLE: _____
AUTHORIZED SIGNATURE: _____
PHONE: _____ FAX: _____
E-MAIL ADDRESS: _____

1. TYPE OF BUSINESS

CORPORATION ☐ INDIVIDUAL ☐
PARTNERSHIP ☐ JOINT VENTURE ☐
OTHER: _____

2. TYPE OF LICENSE & LOCATION

_____
_____
_____

3. TYPE OF SERVICE TO BE PROVIDED FOR RFP: _____
_____

4. NUMBER OF YEARS IN BUSINESS: _____

5. ON A SEPARATE SHEET PROVIDE A BRIEF HISTORY OF YOUR FIRM, STAFF SIZE AND EXPERIENCE. SUBMIT A RESUME FOR THE PROJECT MANAGER AND EACH KEY PERSONNEL ASSIGNED TO THIS PROJECT.

6. WHAT OTHER NAME(S) HAS YOUR COMPANY OPERATED UNDER: _____
_____

7. HAVE YOU OR YOUR FIRM EVER FAILED TO COMPLETE ANY WORK AWARDED TO YOU? YES ☐ NO ☐ IF "YES", EXPLAIN:
_____
_____
_____

8. HAS ANY OFFICER OR PARTNER OF YOUR ORGANIZATION EVER BEEN AN OFFICER OR PARTNER OF ANOTHER ORGANIZATION THAT FAILED TO COMPLETE A CONTRACT WITHIN THE LAST FIVE (5) YEARS? YES ☐ NO ☐
IF "YES", EXPLAIN:

RFP YR-NMBR

9. HAS YOUR FIRM OR ANY PARTNERS OR OFFICERS EVER BEEN INVOLVED IN ANY BANKRUPTCY ACTION? YES ☐ NO ☐ IF "YES", EXPLAIN:

_____
_____
_____
_____

10. ARE YOU PRESENTLY INVOLVED IN ANY LITIGATION WITH ANY GOVERNMENT AGENCY? YES ☐ NO ☐ IF "YES", EXPLAIN TYPE, KIND, PLAINTIFF, DEFENDANT, ETC., AND STATE THE CURRENT STATUS:

_____
_____
_____
_____

11. BANK REFERENCE: _____
ADDRESS: _____
CONTACT: PHONE:

12. LIST THREE (3) SIMILAR PROJECTS (LOCAL OR STATE-WIDE) **FROM LAST FIVE (5) YEARS**-INCLUDE LOCATION OF PROJECT, SIZE OF PROJECT (CONTRACT AMOUNT), CONTACT NAME, ADDRESS, TELEPHONE NUMBERS
NOTE: DETAILED INFORMATION ON THESE PROJECTS MAY ALSO BE REQUESTED IN THE RFP PACKAGE.

1. Location of Project:
Size of Project:
Contract Amount:
Contact Name and Title:
Contract Address:
Contact telephone and FAX Numbers:

2. Location of Project:
Size of Project:
Contract Amount:
Contact Name:
Contact Address:
Contact telephone and FAX Numbers:

3. Location of Project:
Size of Project:
Contract Amount:
Contact Name:
Contact Address:
Contact telephone and FAX Numbers:

13. LIST **CURRENT** SIMILAR PROJECTS (LOCAL OR STATE-WIDE) UNDER CONTRACT-INCLUDE LOCATION OF PROJECT, SIZE OF PROJECT (CONTRACT AMOUNT) CONTACT NAME, ADDRESS, TELEPHONE NUMBERS.
NOTE: DETAILED INFORMATION ON THESE PROJECTS MAY ALSO BE REQUESTED IN THE RFP PACKAGE.

1. Location of Project:
Size of Project:
Contract Amount:
Contact Name and Title:

Contact Address:

Contact telephone and FAX Numbers:

2. Location of Project:
Size of Project:
Contract Amount:
Contact Name and Title:
Contact Address:
Contact telephone and FAX Numbers:

3. Location of Project:
Size of Project:
Contract Amount:
Contact Name and Title:
Contact Address:
Contact telephone and FAX Numbers:

14. LIST OF SUB-CONTRACTORS TO BE USED FOR THIS PROJECT:
(INCLUDE NAME, ADDRESS, TELEPHONE NUMBER, TYPE OF WORK)

1. Name:
Address:
Telephone Number:
Type of Work:

2. Name:
Address:
Telephone Number:
Type of Work:

3. Name:
Address:
Telephone Number:
Type of Work:

IF ADDITIONAL INFORMATION IS PROVIDED ON A SEPARATE SHEET FOR ANY OF THE ITEMS, CLEARLY SPECIFY WHERE IT CAN BE LOCATED IN YOUR BID PACKAGE.

EXHIBIT 4 -- REPRESENTATIONS AND CERTIFICATIONS

1. INSURANCE REQUIREMENTS

Offeror shall comply with all insurance requirements and will submit the Insurance Certificates prior to performance start date. If limits are different from the stated amounts, Offeror shall explain variance. Certain endorsements and "additionally insured" statements may require further clarification and specific statements on a project specific basis and should have been described in the Offeror's Bid.

_____
Initials for 1

2. ETHICS VIOLATIONS

a) The Offeror shall have in place and follow reasonable procedures designed to prevent and detect possible violations described in this clause in its own operations and direct business relationships.
b) Offeror certifies the Offeror has not violated or caused any person to violate, and shall not violate or cause any person to violate, the City's Code of Ethics contained in Article 3, of Chapter 1 of the City Code and in the City's Procurement Rules and Regulations
c) When the Offeror has reasonable grounds to believe that a violation described in this clause may have occurred, the Offeror shall promptly report the possible violation to the City Contracts Specialist in writing.
c) The Offeror must disclose with the signing of this Bid, the name of any officer, director, or agent who is also an employee of the City and any City employee who owns, directly or indirectly, an interest of ten percent (10%) or more in the Offeror's firm or any of its branches.
d) In addition, the Offeror must report any conflict or apparent conflict, current or discovered during the performance of the Contract, to the City Contracts Specialist.
e) The Offeror shall not engage in providing gifts, meals or other amenities to City employees. The right of the Offeror to proceed may be terminated by written notice issued by City Contracts Specialist if Offeror offered or gave a gratuity to an officer, official, or employee of the City and intended by the gratuity to obtain a contract or favorable treatment under a contract.
f) The Offeror shall cooperate fully with the City or any agency investigating a possible violation on behalf of the City. If any violation is determined, the Offeror will properly compensate the City.
g) The Offeror agrees to incorporate the substance of this clause (after substituting "Contractor" for "Offeror") in all subcontracts under this offer.

_____
Initials for 2

3. ILLEGAL ALIENS

If Offeror has any employees or subcontractors, Offeror shall comply with § 8-17.5-101, et seq., C.R.S. regarding Illegal Aliens – Public Contracts for Services, and this section of this Agreement. 8-17.5-102 includes, in part, that:

1. Offeror shall not:
   a. Knowingly employ or contract with an illegal alien to perform work under this Agreement; or
   b. Enter into a contract with a subcontractor that fails to certify to Offeror that the subcontractor shall not knowingly employ or contract with an illegal alien to perform work under this Agreement.
2. Offeror has verified or attempted to verify that Offeror does not employ any illegal aliens and, will participate in the E-Verify Program or State Department program in order to confirm eligibility of all employees who are newly hired to perform work under public contract for services.
3. Offeror will not use E-Verify Program or State Department program procedures to undertake pre-employment screening of job applicants while the public contract for services is being performed.
4. If Offeror obtains actual knowledge that a subcontractor performing work under this Agreement knowingly employs or contracts with an illegal alien, Provider shall:
   a. Notify the subcontractor and the City within three days that Offeror has actual knowledge that the subcontractor is employing or contracting with an illegal alien; and
   b. Terminate the subcontract with the subcontractor if within three days of receiving such notice, the subcontractor does not stop employing or contracting with the illegal alien. However, the Offeror shall not terminate the contract with the subcontractor if during this three day period:
      i. The subcontractor provides information which establishes that the subcontractor has not knowingly employed or contracted with an illegal alien, and
      ii. The Offeror will not employ the illegal aliens in the performance of any City contract.
5. Offeror shall comply with any reasonable request by the Department of Labor and Employment made in the course of an investigation that the Department is undertaking pursuant to the authority established in §8-17.5-102(5), C.R.S.
6. If Offeror violates this provision, the City may terminate the contract for a breach of contract. If the Agreement is terminated, the Offeror shall be liable for actual and consequential damages.

_____
Initials for 3

4. COOPERATION WITH OTHER CONTRACTORS

Other City activities/contracts may be in progress or start during the performance of this

contract. The Offeror shall coordinate the work harmoniously with the other contractors or City personnel, if applicable.

_____
Initials for 4

5. INTERNET USE

Should the Offeror require access to City Internet resources in the performance of this requirement, a “Contractor’s Internet Use Agreement” form must be separately signed by each individual having access to the City Network. The completed Contractor’s Internet Use Agreement will be maintained with this agreement. Inappropriate use of the City Network will be grounds for immediate termination of any awarded contact.

_____
Initials for 5

6. LITIGATION

If awarded a contract, Offeror shall notify the City within five (5) calendar days after being served with a summons, complaint, or other pleading in any matter which has been filed in any federal or state court or administrative agency. The Offeror shall deliver copies of such document(s) to the City's Procurement Services Manager. The term "litigation" includes an assignment for the benefit of creditors, and filings of bankruptcy, reorganization and/or foreclosure.

_____
Initials for 6

7. CONTRACTOR’S REGISTRATION INFORMATION

Offeror’s firm verifies and states that they are (check all that apply):

_____ Large Business (i.e. do not qualify as a small business or non-profit)

_____ Nonprofit

_____ Small Business

_____ Minority Owned Business/Small Disadvantaged Business

_____ Woman Owned Business

_____ Veteran Owned Business

_____ Service-Disabled Veteran Owned Business

_____ HUBZone Business

Note: The City accepts self-certification for these categories in accordance with Small Business Administration (SBA) standards. The SBA size standards are found on the SBA website https://www.sba.gov/content/am-i-small-business-concern.

_____
Initials for 7

8. CONTRACTOR PERSONNEL

a) The Offeror shall appoint one of its key personnel as the "Authorized Representative" who shall have the power and authority to interface with the City and represent the Offeror in all administrative matters concerning this Bid and any awarded contract, including without limitation such administrative matters as correction of problems modifications, and reduction of costs.
b) The Authorized Representative shall be the person identified in the Offeror's Bid, unless the Offeror provides written notice to the City naming another person to serve as its Authorized Representative. Communications received by the City Contracts Specialist from the Authorized Representative shall be deemed to have been received from the Offeror.

The individual, _____ (Name)
with position, _____ (Title)
Can be reached at
Work telephone number: _____
Home telephone number: _____
Cellular telephone number: _____
E-mail address: _____

_____
Initials for 8

9. OFFEROR'S CERTIFICATION

The undersigned hereby affirms that:
a) He/She is a duly authorized agent of the Offeror;
b) He/She has read and agrees to the City's standard terms and conditions attached.
c) The offer is presented in full compliance with the collusive prohibitions of the City of Colorado Springs. The Offeror certifies that no employee of its firm has discussed, or

compared the offer with any other offeror or City employee and has not colluded with any other offeror or City employee.
d) The Offeror certifies that it has checked all of its figures, and understands that the City will not be responsible for any errors or omissions on the part of the Offeror in preparing its Bid.
e) By submitting an offer the Offeror certifies that it has complied and will comply with all requirements of local, state, and federal laws, and that no legal requirements have been or will be violated in making or accepting this solicitation.
I hereby certify that I am submitting the Bid based on my company's capabilities to provide quality products and/or services on time.

_____
Initials for 9

10. OFFEROR CERTIFICATION REGARDING DEBARMENT, SUSPENSION, PROPOSED DEBARMENT, AND OTHER RESPONSIBILITY MATTERS:

1. The Offeror certifies to the best of its knowledge and belief, that (i) the Offeror and/or any of its Principals
    a. Are ( ), Are not ( ) presently debarred, suspended, proposed for debarment, or declared ineligible for the award of contracts by any Federal agency;
    b. Have ( ), Have not ( ), within a three year period preceding this offer, been convicted of or had a civil judgment rendered against them for: commission of fraud or a criminal offense in connection with obtaining, attempting to obtain, or performing a public (federal, state, local) contract or subcontract; violation of Federal or state antitrust statutes relation to the submission of offers; or commission of embezzlement, theft, forgery, bribery, falsification or destruction of records, making false statement, tax evasion, or receiving stolen property; and
    c. Are ( ), Are not ( ) presently indicated for, or otherwise criminally or civilly charged by a governmental entity with, commission of any of the offenses enumerated in any paragraphs above.
2. The Offeror shall provide immediate written notice to the City Contracts Specialist if, at any time prior to contract award, the Offeror learns that its certification was erroneous when submitted or has become erroneous by reasons of changed circumstances.
3. The certification in paragraph 1. above, is a material representation of fact upon which reliance was placed when making award. If it is later determined that the Offeror knowingly rendered an erroneous certification, in addition to other remedies available to the City, the City Contracts Specialist may terminate the contract resulting from this solicitation for default. Termination for default may result in additional charges being levied for the costs incurred by the City to initiate activities to replace the awarded Contractor.

_____
Initials for 10

11. ACCEPTANCE OF CITY CONTRACTS SPECIALIST'S SOLE AUTHORITY FOR CHANGES

Unless otherwise specified in the Contract, the Offeror hereby agrees that any changes to the scope of work, subsequent to the original contract signing, shall be generated in writing and an approval signature shall be obtained from the City Contracts Specialist prior to additional work performance.

_____
Initials for 11

12. CITY CONTRACTOR SAFETY PROGRAM

The Offeror hereby agrees to adhere to a worker safety program for contractor employees on a City job site or location. By initialing below, the Offeror has reviewed the information and will abide by the City Policy which is available for review:

https://coloradosprings.gov/finance/page/procurement-regulations-and-documents

_____
Initials for 12

13. ACCEPTANCE OF CITY ENVIRONMENTALLY PREFERRED PURCHASING (EPP) POLICY

The City of Colorado Springs is committed to buying more environmentally preferable goods and services, as long as they meet performance needs, are available within a reasonable time and at a reasonable cost. The Offeror hereby acknowledges review of this policy by initialing below.

https://coloradosprings.gov/finance/page/procurement-regulations-and-documents

_____
Initials for 13

14. FRAUD, WASTE, AND ABUSE

Everyone has a duty to report any suspected unlawful act impacting the City of Colorado Springs operations and its enterprises. Anyone who becomes aware of the existence or apparent existence of fraud, waste, and abuse in City of Colorado Springs

is encouraged to report such matters to the City Auditor's Office in writing or on the telephone hotline 385-2387 (ADTR). Written correspondence can be mailed to:

City Auditor
P.O. Box 2241
Colorado Springs CO 80901

Or via email CityAuditManagement@springsgov.com. Any of these mechanisms allow for anonymous reporting. For more information, please go to the website https://coloradosprings.gov/cityfraud.

_____
Initials for 14

Name of Company:

Federal Tax ID Number:

DUNS Number:

Principle Place of Business:

_____
Signature of Authorized Representative

Printed Name:

Title:

Date:

EXHIBIT 5 CITY OF COLORADO SPRINGS BID BOND

1. KNOW ALL MEN BY THESE PRESENTS, THAT:

_____
(Name)

_____ As Principal, hereinafter called Principal, and
(Address)

_____
(SURETY Name)

a corporation organized and existing under the laws of the State of:

_____
(SURETY Address)

and AUTHORIZED TO DO BUSINESS IN THE STATE OF COLORADO, as Surety, hereinafter called Surety, are held firmly bound to the CITY OF COLORADO SPRINGS, COLORADO, as Obligee, hereinafter called the Obligee, in the sum of: (Insert Bid Amount in Words)

($ DOLLARS),

_____

lawful money of the United States of America, for payment of which sum well and truly to be made, the Principal and the Surety bind themselves, their heirs, executors, successors and assigns, jointly and severally, firmly by these presents.

2. WHEREAS, the Principal has submitted to the Obligee,

a contract bid dated the _____ day of _____ For the following contract:

_____

3. NOW THEREFORE, THE CONDITION OF THIS OBLIGATION IS SUCH THAT, If Principals bid is accepted by Obligee and Principal is awarded the contract in whole or in part, and the Principal shall enter into the contract with the Obligee in accordance with the terms of such bid, and give such Payment, Performance, and Maintenance bond or bonds as may be specified in the bidding or contract documents with good and sufficient surety for the faithful performance of such Contract and for the prompt payment of labor and material furnished in the prosecution thereof, or in the event of the failure of the Principal to enter such contract and give such bond or bonds, if the Principal shall promptly pay to the Obligee the amount of this bond as set forth herein above, then this obligation shall be null and void, otherwise this obligation to remain in full force and effect.

Signed and sealed on the dates set forth below:

_____ FOR: _____
(Witness) (Principals Name)

BY: _____

ITS: _____

(Seal) This _____ day of _____

_____ FOR: _____
(Witness) (Surety's Name)

BY: _____

ITS: _____

(Seal) This _____ Day of _____

Bond # _____ This Bond __(is) __ (is not) a SBA Guaranteed Bond.

EXHIBIT 6 – NOTIFICATION OF UTILITIES

General Information

It is the responsibility of the Contractor to notify all applicable utilities (including, but not limited to Colorado Springs Utilities) for utility locations at least two business days or twenty-four hours prior to commencing any work. Should any street be closed off for any amount of time, the Contractor must notify the Traffic Department. See the City of Colorado Springs Standard Specifications General Provisions for more information regarding utilities.

The City of Colorado Springs Standard Specifications and General Provisions indicated on the RFP for this project are included by reference. The above document may be reviewed or purchased at the City Administration Building, Engineering Division, at 30 South Nevada, Suite 403, Colorado Springs, Colorado, between the hours of 8:00 A.M. and 5:00 P.M., Monday through Friday, except holidays.

Telephone References

1.	Utility Notification Center of Colorado	1-800-922-1987
2.	Colorado Springs Utilities Electric	(719) 448-4811
3.	Colorado Springs Utilities Water, Wastewater	(719) 448-4200
4.	Traffic Department	(719) 385-5908
5.	Colorado Springs Utilities Gas Emergencies	(719) 520-0100
6.	Cable Television	(719) 633-6616
7.	Telephone	1-800-954-0211

Standard Utility Color Code

1.	Natural Gas	Yellow
2.	Electric	Red
3.	Water	Blue
4.	Wastewater	Green

Contractor Responsibilities

1. Contact Colorado Springs Utilities, and/or other applicable utilities company or provider, at least twenty four hours prior to starting the project so that our service inspector can make contact on the job site.

2. All replacement taps will have to be coordinated and notification must be given to Colorado Springs Utilities twenty four hours prior to scheduling.

3. Any water interruption to properties involved must be notified at least twenty-four hours prior to shut down and coordinated with a service inspector.

4. If in the event a property or business is involved that cannot be without water the Contractor will be responsible for keeping them in water while the shut down is in effect.

5. If for any reason when water is restored after the shut down that a property has no water and Colorado Springs Utilities is contacted to determine the problem, the Contractor will be responsible for digging, regardless of the time of day to restore service. Contractor must provide Colorado Springs Utilities with a name and telephone number of an after hours contact in case of emergency.

6. All services which would be replaced will have to meet our water specifications and be approved by the Water service inspector.

7. All materials pertaining to lowering or replacing water service lines, regardless of size, will be the responsibility of the Contractor unless otherwise specified in Engineering

Specifications and Plans.

8. If for any reason it would not be feasible to shut down and notify affected properties, it would be the responsibility of the Contractor to provide temporary water for the houses or businesses involved.

Pre-excavation Checklist

1. Indicate all gas and other utility lines a set of construction plans.

2. Notify City of Colorado Springs Underground Utility Line Locators at least two business days in advance at the division numbers listed above.

3. Utilities locations should be marked on the ground by City Locators.

4. All employees should be briefed on the marking and the standard utility color codes.

5. Employees should be trained on excavation and safety procedures for natural gas lines.

6. When excavation approaches gas lines, employees should expose lines by careful hand digging and probing.

7. Contact the City Forester for any tree protection requirements that may be included on contract specifications

SHANNON & WILSON, INC.
GEOTECHNICAL AND ENVIRONMENTAL CONSULTANTS

April 27, 2018

Short Elliot Hendrickson, Inc.
2000 S. Colorado Blvd, Suite 6000
Denver, Colorado 80222

Attn: Mr. Scott Jardine, PE

RE: NORTH CHELTON ROAD DRAINAGE IMPROVEMENTS, COLORADO SPRINGS, COLORADO

This report presents the results of our subsurface exploration program for the North Chelton Road Drainage Improvements for Short Elliott Hendrickson, Inc. (SEH). The report summarizes our subsurface exploration and laboratory testing program, discusses regional geology and subsurface conditions within the project area, and discusses excavation potential of the subsurface materials. Our scope of work included the following tasks:

- Observation and logging of four boring, including obtaining permits, coordinating traffic control, completing utility locates, coordinating the drilling subcontractor, and measuring groundwater levels;
- Laboratory testing of selected soil samples; and
- Preparation of this geotechnical letter report.

Our work was completed in general accordance with our subcontract agreement with SEH, dated March 21, 2018. The scope of our services did not include any environmental assessment or evaluation regarding the presence or absence of wetlands or hazardous or toxic materials in the soil, surface water, groundwater, or air, on or below the site. The scope of our services did not include any evaluation regarding disposal of contaminated soils or groundwater, should any be encountered.

PROJECT AND SITE DESCRIPTION

The project is located in Colorado Springs, Colorado along North Chelton Road from the Colorado Springs Charter Academy (CSCA) to Maizeland Road, (Figure 1). The project involves construction of a storm drain within North Chelton Road. The proposed length of the storm drain is approximately 0.5 miles. The pipeline begins on the north side of the Colorado

Springs Charter Academy and travels to the east of the school and then south to North Chelton Road. The proposed pipeline alignment then follows the North Chelton Road alignment to Maizeland Road. North Chelton Road is a residential street that is generally sloping down toward Maizeland Road.

FIELD EXPLORATIONS AND LABORATORY TESTING

A field exploration and laboratory testing program was implemented to evaluate subsurface soil, bedrock, and groundwater conditions. The field exploration program included drilling four borings (designated SW-01 through SW-04) along the proposed alignment.

The approximate boring locations are shown in the Site and Exploration Plan (Figure 2). The borings were drilled to a depth of approximately 10 feet below ground surface. During drilling, the Shannon & Wilson, Inc. (Shannon & Wilson) representative collected soil and bedrock samples and prepared a field log of each boring. Soil classifications were based on ASTM International (ASTM) Designation: D2487, Standard Practice for Classification of Soils for Engineering Purposes (Unified Soil Classification System), and ASTM Designation: D2488, Standard Practice for Description and Identification of Soils (Visual-Manual Procedure). The system is referred to as the Unified Soil Classification System and is summarized in Figure 3. The boring logs are presented as Figures 4 through 7.

Disturbed samples were obtained in general accordance with the Standard Penetration Test (SPT) (ASTM Designation: D1586). The SPT consists of driving a 2-inch outside diameter (O.D.), 1.375-inch inside diameter split-spoon sampler a distance of 18 inches with a 140-pound hammer free-falling a distance of 30 inches. An automatic hammer system was used to advance the samplers. During sampling, the Shannon & Wilson field representative recorded the number of blows for each 6-inch increment of penetration and summed the blow counts for the last two 6-inch increments. This sum is recorded as the penetration resistance number, or N-value. The N-values provide a means for evaluating the relative density or compactness of cohesionless (granular) soils and consistency or stiffness of cohesive (fine-grained) soils (see Figure 3). The N-values are shown on the boring log. Representative portions of the split-spoon sample obtained in conjunction with the SPT were placed in plastic jars and transported to our laboratory.

Samples were also obtained using a modified California (MC) barrel sampler. The MC test procedure is similar to the SPT, except a larger diameter barrel sampler (2½-inch O.D., lined with 2-inch-diameter brass tubing) is used and only driven 12 inches. During sampling, the

Shannon & Wilson field representative recorded the number of blows for each 6-inch increment of penetration. Representative samples were sealed in the brass liner tubes with plastic caps and transported to our laboratory.

Geotechnical laboratory testing included natural water content tests and were completed on samples retrieved from the borings. The natural water content of each sample is presented on each boring log.

REGIONAL GEOLOGY AND SUBSURFACE CONDITIONS

Regional Geologic Setting

We reviewed publicly available geologic maps covering the project area (Carroll and Crawford, 2000[1] and Scott and Wobus, 1973[2]), which indicated bedrock of the Dawson and Laramie Formations at or near the ground surface. The Dawson Formation is described as arkose sandstone and interbedded gray claystone overlying the Laramie Formation described as interbedded sandstone, siltstone, shale, and coal. Surficial deposits were not described in the reviewed geologic maps; however, Scott and Wobus indicated the project area could be partially covered by eolian (windblown) sands.

Subsurface Conditions

Boring SW-01, located in the sod area north of CSCA, encountered approximately 2 inches of sod and topsoil followed by fill consisting of loose sand with silt and clay pipe debris to a depth of approximately 4 feet. Stiff, sandy clay was then encountered to a depth of about 9 feet, underlain by medium dense sand with silt to the termination depth of the boring. Borings SW-02 through SW-04 were drilled through North Chelton Road and encountered 4 to 5 inches of existing asphalt at each boring location. Beneath the asphalt boring SW-02 encountered loose to medium dense sand with clay and silt to the termination depth of the boring. Boring SW-03 encountered loose sand with silt to a depth of 4.5 feet underlain by loose, clayey sand. Boring SW-04 encountered loose to medium dense sand with silt to a depth of 7 feet followed by loose to medium dense, clayey sand and medium dense sand with silt.

---

[1] Carroll, C.J., and Crawford, T.A., 2000, Geologic map of the Colorado Springs quadrangle, El Paso County, Colorado: Colorado Geological Survey, Open-File Report OF-00-3, scale 1:24,000.
[2] Scott, G.R., and Wobus, R.A., 1973, Reconnaissance geologic map of Colorado Springs and vicinity, Colorado: U.S. Geological Survey, Miscellaneous Field Studies Map MF-482, scale 1:62,500.

Bedrock was not encountered in any of our borings.

Groundwater was not observed in any borings upon completion of drilling. Fluctuations in groundwater level are possible and likely depend on many factors, including seasonal variations and local precipitation.

Our observations are specific to the locations, depths, and dates noted on the exploration logs may not be applicable to all areas of the site. While the subsurface conditions were relatively consistent, there is no amount of explorations or laboratory testing that can precisely predict the characteristics, quality, or distribution of subsurface conditions at every location throughout the site. Variations in the subsurface conditions may occur between and below the borings. Also, the passage of time or intervening causes (natural and manmade) may result in changes to the conditions of the site and subsurface conditions.

EXCAVATION POTENTIAL

As discussed above, bedrock was not encountered during our subsurface explorations. Based on the geologic mapping of the project area shallow sandstone and claystone layers may be encountered during construction between boring locations. If excavation in bedrock is required it could be difficult, necessitating the use of hydraulic excavators and dozers with ripper attachments.

LIMITATIONS

This report was prepared for the exclusive use of SEH and their representatives for the design of the North Chelton Road Drainage Improvements. It should be made available to prospective contractors for information on factual data only, and not as a warranty of subsurface conditions, such as those interpreted from the exploration log and presented in the discussion of subsurface conditions included in this report.

We assume that the explorations are representative of the subsurface conditions at the site; that is, the subsurface conditions everywhere are not significantly different from those disclosed by the explorations. Unanticipated soil conditions are commonly encountered and cannot fully be determined by taking samples from borings. Such unexpected conditions frequently require that additional expenditures be made to attain properly constructed projects. Therefore, some contingency fund is recommended to accommodate such potential extra costs.

Within the limitations of the scope, schedule and budget, this report was prepared in accordance with generally accepted professional geotechnical engineering principles and practice in this area at the time we prepared our letter report. We make no other warranty, either express or implied. The data presented in this letter report were based on our understanding of the project as described in this letter report and the site conditions as interpreted from the current explorations.

We appreciate the opportunity to be of service to you on this project. If you have any questions or require further information, please contact me at 303-825-3800.

Sincerely,

SHANNON & WILSON, INC.

COLORADO REGISTERED
JOSEPH C GOODE III
4/27/18
52381
PROFESSIONAL ENGINEER

Reviewed By:

Joseph Goode III, PE
Senior Geotechnical Engineer

Gregory R. Fischer, PhD, PE
Senior Vice President

JCG:RDD:GRF/jcg

Enc: Figure 1 – Vicinity Map
Figure 2 – Site and Exploration Plan
Figure 3 – Soil Description and Log Key (3 sheets)
Figure 4 – Log of Boring SW-01
Figure 5 – Log of Boring SW-02
Figure 6 – Log of Boring SW-03
Figure 7 – Log of Boring SW-04
Important Info About Your Geotechnical Report

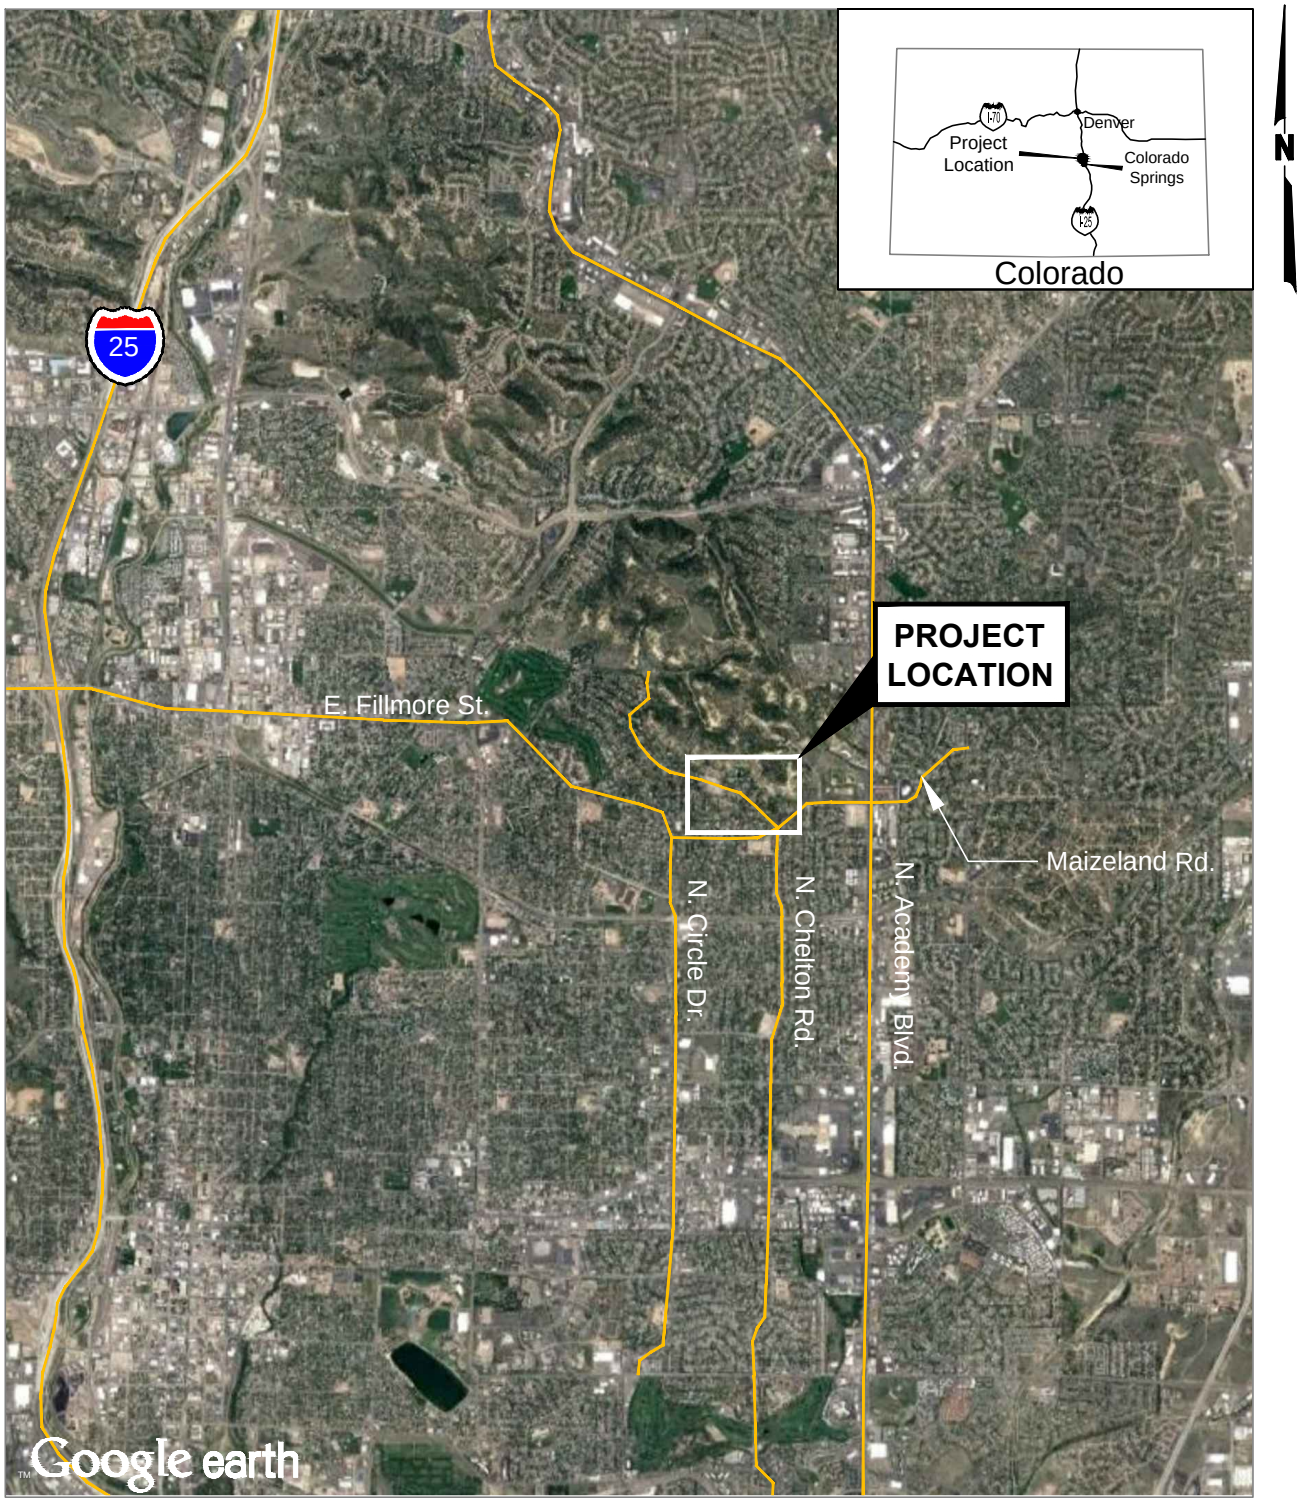

0 1 2

Approximate Scale in Miles

NOTE

Map adapted from aerial imagery provided by Google Earth Pro, reproduced by permission granted by Google Earth ™ Mapping Service.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

VICINITY MAP

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
GEOTECHNICAL AND ENVIRONMENTAL CONSULTANTS

FIG. 1

Filename: I:\EF\23-1 DEN\01600S\01695 Chelton Road St\001 Geotechnical\Drafting\01695-002_Fig_1&2.dwg Date: 04-25-2018 Login: jcg

LEGEND

SW-01 Boring Designation and Approximate Location

0 200 400

Approximate Scale in Feet

NOTE

Map adapted from aerial imagery provided by Google Earth Pro, reproduced by permission granted by Google Earth™ Mapping Service.

N

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

SITE AND EXPLORATION PLAN

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
GEOTECHNICAL AND ENVIRONMENTAL CONSULTANTS

FIG. 2

Filename: I:\EF\23-1 DEN\01600s\01695 Chelton Road St\001 Geotechnical\Drafting\01695-002_Fig_1&2.dwg Date: 04-25-2018 Login: jcg

Shannon & Wilson, Inc. (S&W), uses a soil identification system modified from the Unified Soil Classification System (USCS). Elements of the USCS and other definitions are provided on this and the following pages. Soil descriptions are based on visual-manual procedures (ASTM D2488) and laboratory testing procedures (ASTM D2487), if performed.

S&W INORGANIC SOIL CONSTITUENT DEFINITIONS

CONSTITUENT[2]	FINE-GRAINED SOILS (50% or more fines)[1]	COARSE-GRAINED SOILS (less than 50% fines)[1]
Major	***Silt, Lean Clay, Elastic Silt,*** or ***Fat Clay***[3]	***Sand*** or ***Gravel***[4]
Modifying (Secondary) Precedes major constituent	30% or more coarse-grained: ***Sandy*** or ***Gravelly***[4]	More than 12% fine-grained: ***Silty*** or ***Clayey***[3]
Minor Follows major constituent	15% to 30% coarse-grained: ***with Sand*** or ***with Gravel***[4]	5% to 12% fine-grained: ***with Silt*** or ***with Clay***[3]
	30% or more total coarse-grained *and* lesser coarse-grained constituent is 15% or more: ***with Sand*** or ***with Gravel***[5]	15% or more of a second coarse-grained constituent: ***with Sand*** or ***with Gravel***[5]

[1]All percentages are by weight of total specimen passing a 3-inch sieve.
[2]The order of terms is: *Modifying Major with Minor*.
[3]Determined based on behavior.
[4]Determined based on which constituent comprises a larger percentage.
[5]Whichever is the lesser constituent.

MOISTURE CONTENT TERMS

Dry	Absence of moisture, dusty, dry to the touch
Moist	Damp but no visible water
Wet	Visible free water, from below water table

STANDARD PENETRATION TEST (SPT) SPECIFICATIONS

Hammer: 140 pounds with a 30-inch free fall. Rope on 6- to 10-inch-diam. cathead 2-1/4 rope turns, > 100 rpm

NOTE: If automatic hammers are used, blow counts shown on boring logs should be adjusted to account for efficiency of hammer.

Sampler: 10 to 30 inches long
Shoe I.D. = 1.375 inches
Barrel I.D. = 1.5 inches
Barrel O.D. = 2 inches

N-Value: Sum blow counts for second and third 6-inch increments.
Refusal: 50 blows for 6 inches or less; 10 blows for 0 inches.

NOTE: Penetration resistances (N-values) shown on boring logs are as recorded in the field and have not been corrected for hammer efficiency, overburden, or other factors.

PARTICLE SIZE DEFINITIONS

DESCRIPTION	SIEVE NUMBER AND/OR APPROXIMATE SIZE
FINES	< #200 (0.075 mm = 0.003 in.)
SAND	
Fine	#200 to #40 (0.075 to 0.4 mm; 0.003 to 0.02 in.)
Medium	#40 to #10 (0.4 to 2 mm; 0.02 to 0.08 in.)
Coarse	#10 to #4 (2 to 4.75 mm; 0.08 to 0.187 in.)
GRAVEL	
Fine	#4 to 3/4 in. (4.75 to 19 mm; 0.187 to 0.75 in.)
Coarse	3/4 to 3 in. (19 to 76 mm)
COBBLES	3 to 12 in. (76 to 305 mm)
BOULDERS	> 12 in. (305 mm)

RELATIVE DENSITY / CONSISTENCY

COHESIONLESS SOILS		COHESIVE SOILS	
N, SPT, BLOWS/FT.	RELATIVE DENSITY	N, SPT, BLOWS/FT.	RELATIVE CONSISTENCY
< 4	Very loose	< 2	Very soft
4 - 10	Loose	2 - 4	Soft
10 - 30	Medium dense	4 - 8	Medium stiff
30 - 50	Dense	8 - 15	Stiff
> 50	Very dense	15 - 30	Very stiff
		> 30	Hard

WELL AND BACKFILL SYMBOLS

Bentonite Cement Grout	Surface Cement Seal
Bentonite Grout	Asphalt or Cap
Bentonite Chips	Slough
Silica Sand	Inclinometer or Non-perforated Casing
Perforated or Screened Casing	Vibrating Wire Piezometer

PERCENTAGES TERMS [1, 2]

Trace	< 5%
Few	5 to 10%
Little	15 to 25%
Some	30 to 45%
Mostly	50 to 100%

[1]Gravel, sand, and fines estimated by mass. Other constituents, such as organics, cobbles, and boulders, estimated by volume.

[2]Reprinted, with permission, from ASTM D2488 - 09a Standard Practice for Description and Identification of Soils (Visual-Manual Procedure), copyright ASTM International, 100 Barr Harbor Drive, West Conshohocken, PA 19428. A copy of the complete standard may be obtained from ASTM International, www.astm.org.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

SOIL DESCRIPTION AND LOG KEY

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
Geotechnical and Environmental Consultants

FIG. 3
Sheet 1 of 3

2013_BORING_CLASS1 23-1-01695-001 CHELTON ROAD.GPJ SWNEW.GDT 4/25/18

UNIFIED SOIL CLASSIFICATION SYSTEM (USCS)
(Modified From USACE Tech Memo 3-357, ASTM D2487, and ASTM D2488)

MAJOR DIVISIONS			GROUP/GRAPHIC SYMBOL		TYPICAL IDENTIFICATIONS
COARSE-GRAINED SOILS *(more than 50% retained on No. 4 sieve)*	Gravels *(more than 50% of coarse fraction retained on No. 4 sieve)*	Gravel *(less than 5% fines)*	GW		Well-Graded Gravel; Well-Graded Gravel with Sand
			GP		Poorly Graded Gravel; Poorly Graded Gravel with Sand
		Silty or Clayey Gravel *(more than 12% fines)*	GM		Silty Gravel; Silty Gravel with Sand
			GC		Clayey Gravel; Clayey Gravel with Sand
	Sands *(50% or more of coarse fraction passes the No. 4 sieve)*	Sand *(less than 5% fines)*	SW		Well-Graded Sand; Well-Graded Sand with Gravel
			SP		Poorly Graded Sand; Poorly Graded Sand with Gravel
		Silty or Clayey Sand *(more than 12% fines)*	SM		Silty Sand; Silty Sand with Gravel
			SC		Clayey Sand; Clayey Sand with Gravel
FINE-GRAINED SOILS *(50% or more passes the No. 4 sieve)*	Silts and Clays *(liquid limit less than 50)*	Inorganic	ML		Silt; Silt with Sand or Gravel; Sandy or Gravelly Silt
			CL		Lean Clay; Lean Clay with Sand or Gravel; Sandy or Gravelly Lean Clay
		Organic	OL		Organic Silt or Clay; Organic Silt or Clay with Sand or Gravel; Sandy or Gravelly Organic Silt or Clay
	Silts and Clays *(liquid limit 50 or more)*	Inorganic	MH		Elastic Silt; Elastic Silt with Sand or Gravel; Sandy or Gravelly Elastic Silt
			CH		Fat Clay; Fat Clay with Sand or Gravel; Sandy or Gravelly Fat Clay
		Organic	OH		Organic Silt or Clay; Organic Silt or Clay with Sand or Gravel; Sandy or Gravelly Organic Silt or Clay
HIGHLY-ORGANIC SOILS	Primarily organic matter, dark in color, and organic odor		PT		Peat or other highly organic soils (see ASTM D4427)

NOTE: No. 4 size = 4.75 mm = 0.187 in.; No. 200 size = 0.075 mm = 0.003 in.

NOTES

1. Dual symbols *(symbols separated by a hyphen, i.e., SP-SM, Sand with Silt)* are used for soils with between 5% and 12% fines or when the liquid limit and plasticity index values plot in the CL-ML area of the plasticity chart. Graphics shown on the logs for these soil types are a combination of the two graphic symbols (e.g., SP and SM).

2. Borderline symbols *(symbols separated by a slash, i.e., CL/ML, Lean Clay to Silt; SP-SM/SM, Sand with Silt to Silty Sand)* indicate that the soil properties are close to the defining boundary between two groups.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

SOIL DESCRIPTION AND LOG KEY

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
Geotechnical and Environmental Consultants

FIG. 3
Sheet 2 of 3

2013_BORING_CLASS2 23-1-01695-001 CHELTON ROAD.GPJ SWNEW.GDT 4/25/18

GRADATION TERMS

Poorly Graded	Narrow range of grain sizes present or, within the range of grain sizes present, one or more sizes are missing (Gap Graded). Meets criteria in ASTM D2487, if tested.
Well-Graded	Full range and even distribution of grain sizes present. Meets criteria in ASTM D2487, if tested.

CEMENTATION TERMS[1]

Weak	Crumbles or breaks with handling or slight finger pressure
Moderate	Crumbles or breaks with considerable finger pressure
Strong	Will not crumble or break with finger pressure

PLASTICITY[2]

DESCRIPTION	VISUAL-MANUAL CRITERIA	APPROX. PLASITICTY INDEX RANGE
Nonplastic	A 1/8-in. thread cannot be rolled at any water content.	< 4
Low	A thread can barely be rolled and a lump cannot be formed when drier than the plastic limit.	4 to 10
Medium	A thread is easy to roll and not much time is required to reach the plastic limit. The thread cannot be rerolled after reaching the plastic limit. A lump crumbles when drier than the plastic limit.	10 to 20
High	It take considerable time rolling and kneading to reach the plastic limit. A thread can be rerolled several times after reaching the plastic limit. A lump can be formed without crumbling when drier than the plastic limit.	> 20

ADDITIONAL TERMS

Mottled	Irregular patches of different colors.
Bioturbated	Soil disturbance or mixing by plants or animals.
Diamict	Nonsorted sediment; sand and gravel in silt and/or clay matrix.
Cuttings	Material brought to surface by drilling.
Slough	Material that caved from sides of borehole.
Sheared	Disturbed texture, mix of strengths.

PARTICLE ANGULARITY AND SHAPE TERMS[1]

Angular	Sharp edges and unpolished planar surfaces.
Subangular	Similar to angular, but with rounded edges.
Subrounded	Nearly planar sides with well-rounded edges.
Rounded	Smoothly curved sides with no edges.
Flat	Width/thickness ratio > 3.
Elongated	Length/width ratio > 3.

[1]Reprinted, with permission, from ASTM D2488 - 09a Standard Practice for Description and Identification of Soils (Visual-Manual Procedure), copyright ASTM International, 100 Barr Harbor Drive, West Conshohocken, PA 19428. A copy of the complete standard may be obtained from ASTM International, www.astm.org.
[2]Adapted, with permission, from ASTM D2488 - 09a Standard Practice for Description and Identification of Soils (Visual-Manual Procedure), copyright ASTM International, 100 Barr Harbor Drive, West Conshohocken, PA 19428. A copy of the complete standard may be obtained from ASTM International, www.astm.org.

ACRONYMS AND ABBREVIATIONS

ATD	At Time of Drilling
Diam.	Diameter
Elev.	Elevation
ft.	Feet
FeO	Iron Oxide
gal.	Gallons
Horiz.	Horizontal
HSA	Hollow Stem Auger
I.D.	Inside Diameter
in.	Inches
lbs.	Pounds
MgO	Magnesium Oxide
mm	Millimeter
MnO	Manganese Oxide
NA	Not Applicable or Not Available
NP	Nonplastic
O.D.	Outside Diameter
OW	Observation Well
pcf	Pounds per Cubic Foot
PID	Photo-Ionization Detector
PMT	Pressuremeter Test
ppm	Parts per Million
psi	Pounds per Square Inch
PVC	Polyvinyl Chloride
rpm	Rotations per Minute
SPT	Standard Penetration Test
USCS	Unified Soil Classification System
q_u	Unconfined Compressive Strength
VWP	Vibrating Wire Piezometer
Vert.	Vertical
WOH	Weight of Hammer
WOR	Weight of Rods
Wt.	Weight

STRUCTURE TERMS[1]

Interbedded	Alternating layers of varying material or color with layers at least 1/4-inch thick; singular: bed.
Laminated	Alternating layers of varying material or color with layers less than 1/4-inch thick; singular: lamination.
Fissured	Breaks along definite planes or fractures with little resistance.
Slickensided	Fracture planes appear polished or glossy; sometimes striated.
Blocky	Cohesive soil that can be broken down into small angular lumps that resist further breakdown.
Lensed	Inclusion of small pockets of different soils, such as small lenses of sand scattered through a mass of clay.
Homogeneous	Same color and appearance throughout.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

SOIL DESCRIPTION AND LOG KEY

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
Geotechnical and Environmental Consultants

FIG. 3
Sheet 3 of 3

2013_BORING_CLASS3 23-1-01695-001 CHELTON ROAD.GPJ SWNEW.GDT 4/25/18

Total Depth:	10 ft.	Latitude:		Drilling Method:	Solid-Stem Auger	Hole Diam.:	4 in.
Top Elevation:	~	Longitude:		Drilling Company:	Entech Engineering	Rod Type.:	AWJ
Vert. Datum:		Station:		Drill Rig Equipment:	Simco 2800 HS (HT)	Hammer Type:	Automatic
Horiz. Datum:		Offset:		Other Comments:	Drilled at pre-mark location		

SOIL DESCRIPTION *Refer to the report text for a proper understanding of the subsurface materials and drilling methods. The stratification lines indicated below represent the approximate boundaries between material types, and the transition may be gradual.*	Depth, ft.	Symbol	Pocket Pen., tsf	Samples	Ground Water	Depth, ft.
2 inches of sod and topsoil.	0.2					
Loose, dark brown, *Poorly Graded Sand with Silt (SP-SM);* moist; roots in upper 6 inches, clay pipe debris at 2 feet. Fill				S-1		
Stiff, brown to gray, *Sandy Lean Clay (CL);* moist; occasionally grading to clayey sand.	3.8		3.25	S-2	Groundwater Not Encountered During Drilling.	5
Medium dense, light brown, *Poorly Graded Sand with Silt (SP-SM);* moist; trace of gravel.	9.3 10.0		0.5	S-3		10
BOTTOM OF BORING COMPLETED ON 4/19/2018						15 20

PENETRATION RESISTANCE (blows/foot)

▲ Hammer Wt. & Drop: *140 lbs / 30 inches*

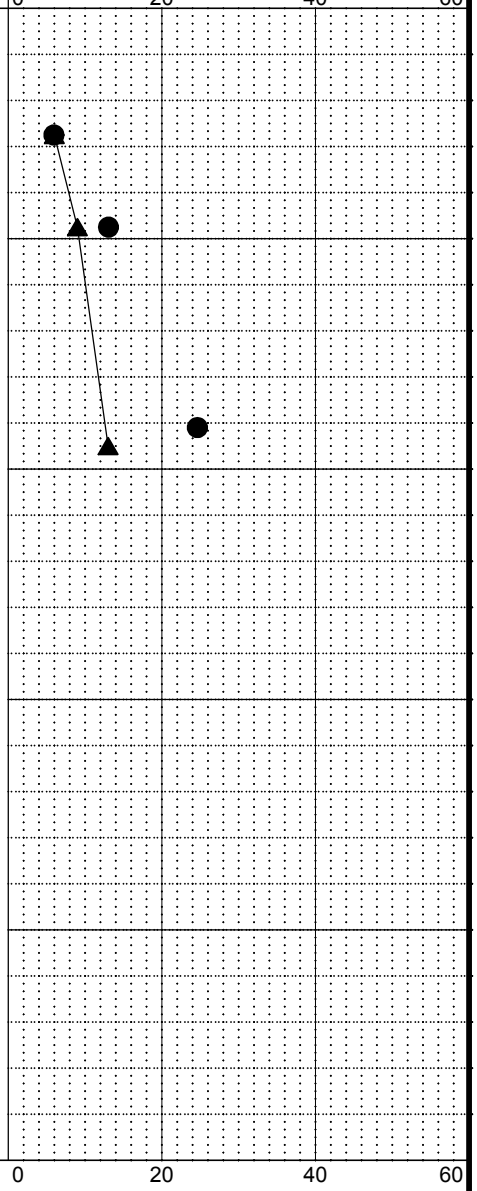

● % Water Content

LEGEND

* Sample Not Recovered

Standard Penetration Test

Modified California Sampler

NOTES

1. Refer to Figure A-1 for explanation of symbols, codes, abbreviations and definitions.
2. The discussion in the text of this report is necessary for a proper understanding of the nature of the subsurface materials.
3. Groundwater level, if indicated above, is for the date specified and may vary.
4. USCS designation is based on visual-manual classification and selected lab testing.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

LOG OF BORING SW-01

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
Geotechnical and Environmental Consultants

FIG. 4

REV 3

MASTER_LOG_E_POCKETPEN_LAT&LONG 23-1-01695-001 CHELTON ROAD.GPJ 4/27/18

Total Depth:	*10.5 ft.*	Latitude:		Drilling Method:	*Solid-Stem Auger*	Hole Diam.:	*4 in.*
Top Elevation:	*~*	Longitude:		Drilling Company:	*Entech Engineering*	Rod Type.:	*AWJ*
Vert. Datum:		Station:		Drill Rig Equipment:	*Simco 2800 HS (HT)*	Hammer Type:	*Automatic*
Horiz. Datum:		Offset:		Other Comments:	*Drilled at pre-mark location*		

SOIL DESCRIPTION *Refer to the report text for a proper understanding of the subsurface materials and drilling methods. The stratification lines indicated below represent the approximate boundaries between material types, and the transition may be gradual.*	Depth, ft.	Symbol	Samples	Ground Water	Depth, ft.
4 inches of asphalt.	0.3			Groundwater Not Encountered During Drilling.	
Loose to medium dense, brown to light brown, *Poorly Graded Sand with Clay (SP-SC);* moist; occasional iron oxide staining, interbedded clayey sand. - 1 inch poorly graded sand lense at 3.3 feet.			S-1 S-2		
Loose to medium dense, light brown, *Poorly Graded Sand with Silt (SP-SM);* moist; occasional iron oxide staining.	5.4		S-3		
BOTTOM OF BORING COMPLETED ON 4/19/2018	10.5				

PENETRATION RESISTANCE (blows/foot)

▲ Hammer Wt. & Drop: *140 lbs / 30 inches*

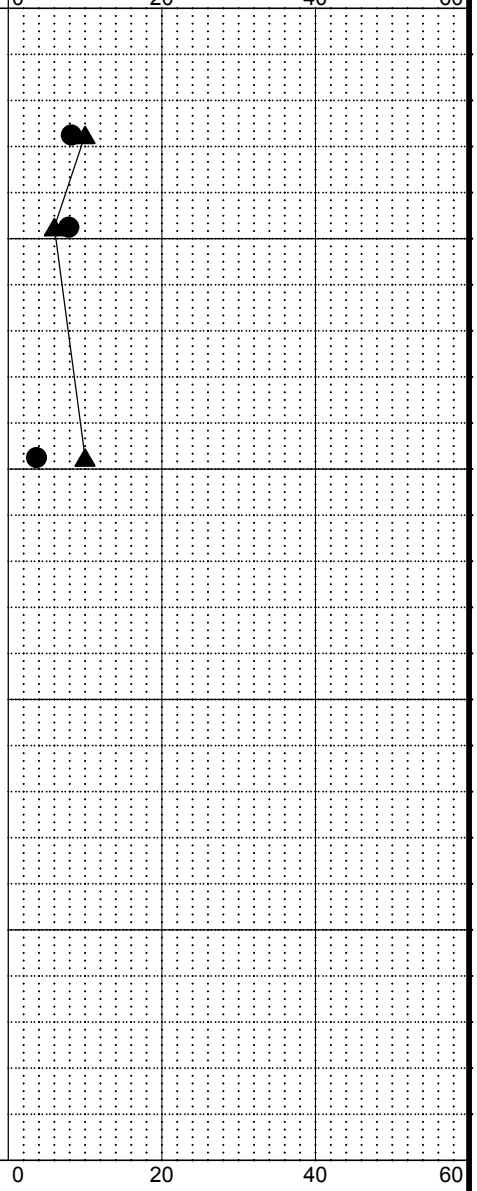

● % Water Content

LEGEND

* Sample Not Recovered

⊥ Standard Penetration Test

NOTES

1. Refer to Figure A-1 for explanation of symbols, codes, abbreviations and definitions.
2. The discussion in the text of this report is necessary for a proper understanding of the nature of the subsurface materials.
3. Groundwater level, if indicated above, is for the date specified and may vary.
4. USCS designation is based on visual-manual classification and selected lab testing.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

LOG OF BORING SW-02

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
Geotechnical and Environmental Consultants

FIG. 5

REV 3

MASTER_LOG_E_POCKETPEN_LAT&LONG 23-1-01695-001 CHELTON ROAD.GPJ 4/27/18

Total Depth:	*10.5 ft.*	Latitude:		Drilling Method:	*Solid-Stem Auger*	Hole Diam.:	*4 in.*
Top Elevation:	*~*	Longitude:		Drilling Company:	*Entech Engineering*	Rod Type.:	*AWJ*
Vert. Datum:		Station:		Drill Rig Equipment:	*Simco 2800 HS (HT)*	Hammer Type:	*Automatic*
Horiz. Datum:		Offset:		Other Comments:	*Drilled at pre-mark location*		

SOIL DESCRIPTION *Refer to the report text for a proper understanding of the subsurface materials and drilling methods. The stratification lines indicated below represent the approximate boundaries between material types, and the transition may be gradual.*	Depth, ft.
5 inches of asphalt.	0.4
Loose, dark brown, *Poorly Graded Sand with Silt (SP-SM);* moist.	4.5
Loose, dark brown to light brown, *Clayey Sand (SC);* moist; occasional iron oxide staining from 4 to 5.5 feet. - Interbedded poorly graded sand with clay below 9 feet.	10.5
BOTTOM OF BORING COMPLETED ON 4/19/2018	

Symbol | Samples: S-1, S-2, S-3 | Ground Water: Groundwater Not Encountered During Drilling. | Depth, ft.

PENETRATION RESISTANCE (blows/foot)

▲ Hammer Wt. & Drop: *140 lbs / 30 inches*

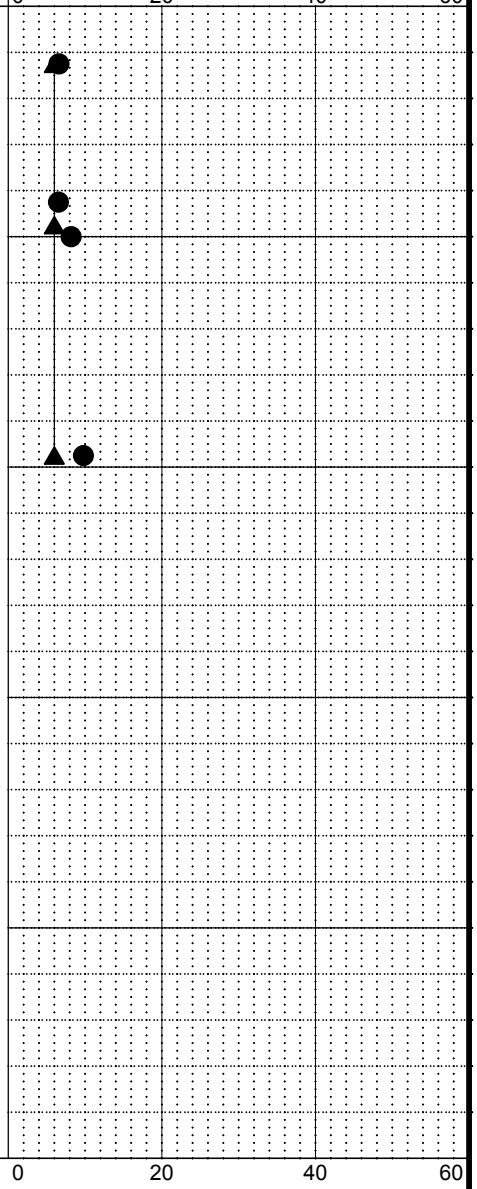

● % Water Content

LEGEND

* Sample Not Recovered

⊥ Standard Penetration Test

NOTES

1. Refer to Figure A-1 for explanation of symbols, codes, abbreviations and definitions.
2. The discussion in the text of this report is necessary for a proper understanding of the nature of the subsurface materials.
3. Groundwater level, if indicated above, is for the date specified and may vary.
4. USCS designation is based on visual-manual classification and selected lab testing.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

LOG OF BORING SW-03

April 2018 | 23-1-01695-001

SHANNON & WILSON, INC.
Geotechnical and Environmental Consultants

FIG. 6

REV 3

MASTER_LOG_E_POCKETPEN_LAT&LONG 23-1-01695-001 CHELTON ROAD.GPJ 4/27/18

Total Depth:	*10.5 ft.*	Latitude:		Drilling Method:	*Solid-Stem Auger*	Hole Diam.:	*4 in.*
Top Elevation:	*~*	Longitude:		Drilling Company:	*Entech Engineering*	Rod Type.:	*AWJ*
Vert. Datum:		Station:		Drill Rig Equipment:	*Simco 2800 HS (HT)*	Hammer Type:	*Automatic*
Horiz. Datum:		Offset:		Other Comments:	*Drilled 6.5 feet northeast from pre-mark location*		

SOIL DESCRIPTION *Refer to the report text for a proper understanding of the subsurface materials and drilling methods. The stratification lines indicated below represent the approximate boundaries between material types, and the transition may be gradual.*	Depth, ft.
4 inches of asphalt.	0.3
Loose to medium dense, dark brown, *Poorly Graded Sand with Silt (SP-SM);* moist.	7.3
Loose to medium dense, brown, *Clayey Sand (SC);* moist.	9.1
Medium dense, light brown, *Poorly Graded Sand with Silt (SP-SM);* moist.	10.5
BOTTOM OF BORING COMPLETED ON 4/19/2018	

Symbol | Samples: S-1, S-2, S-3 | Ground Water: Groundwater Not Encountered During Drilling.

PENETRATION RESISTANCE (blows/foot)

▲ Hammer Wt. & Drop: *140 lbs / 30 inches*

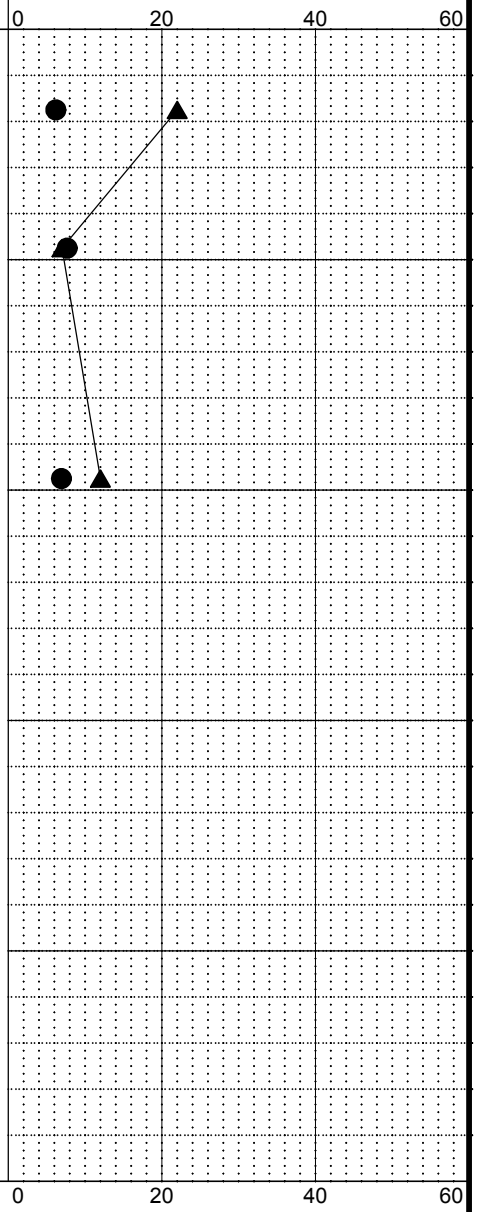

● % Water Content

LEGEND

* Sample Not Recovered

Modified California Sampler

Standard Penetration Test

NOTES

1. Refer to Figure A-1 for explanation of symbols, codes, abbreviations and definitions.
2. The discussion in the text of this report is necessary for a proper understanding of the nature of the subsurface materials.
3. Groundwater level, if indicated above, is for the date specified and may vary.
4. USCS designation is based on visual-manual classification and selected lab testing.

North Chelton Road
Drainage Improvements
Colorado Springs, Colorado

LOG OF BORING SW-04

April 2018 23-1-01695-001

SHANNON & WILSON, INC.
Geotechnical and Environmental Consultants

FIG. 7

REV 3

MASTER_LOG_E_POCKETPEN_LAT&LONG 23-1-01695-001 CHELTON ROAD.GPJ 4/27/18

IMPORTANT INFORMATION ABOUT YOUR GEOTECHNICAL/ENVIRONMENTAL REPORT

CONSULTING SERVICES ARE PERFORMED FOR SPECIFIC PURPOSES AND FOR SPECIFIC CLIENTS.

Consultants prepare reports to meet the specific needs of specific individuals. A report prepared for a civil engineer may not be adequate for a construction contractor or even another civil engineer. Unless indicated otherwise, your consultant prepared your report expressly for you and expressly for the purposes you indicated. No one other than you should apply this report for its intended purpose without first conferring with the consultant. No party should apply this report for any purpose other than that originally contemplated without first conferring with the consultant.

THE CONSULTANT'S REPORT IS BASED ON PROJECT-SPECIFIC FACTORS.

A geotechnical/environmental report is based on a subsurface exploration plan designed to consider a unique set of project-specific factors. Depending on the project, these may include: the general nature of the structure and property involved; its size and configuration; its historical use and practice; the location of the structure on the site and its orientation; other improvements such as access roads, parking lots, and underground utilities; and the additional risk created by scope-of-service limitations imposed by the client. To help avoid costly problems, ask the consultant to evaluate how any factors that change subsequent to the date of the report may affect the recommendations. Unless your consultant indicates otherwise, your report should not be used: (1) when the nature of the proposed project is changed (for example, if an office building will be erected instead of a parking garage, or if a refrigerated warehouse will be built instead of an unrefrigerated one, or chemicals are discovered on or near the site); (2) when the size, elevation, or configuration of the proposed project is altered; (3) when the location or orientation of the proposed project is modified; (4) when there is a change of ownership; or (5) for application to an adjacent site. Consultants cannot accept responsibility for problems that may occur if they are not consulted after factors which were considered in the development of the report have changed.

SUBSURFACE CONDITIONS CAN CHANGE.

Subsurface conditions may be affected as a result of natural processes or human activity. Because a geotechnical/environmental report is based on conditions that existed at the time of subsurface exploration, construction decisions should not be based on a report whose adequacy may have been affected by time. Ask the consultant to advise if additional tests are desirable before construction starts; for example, groundwater conditions commonly vary seasonally.

Construction operations at or adjacent to the site and natural events such as floods, earthquakes, or groundwater fluctuations may also affect subsurface conditions and, thus, the continuing adequacy of a geotechnical/environmental report. The consultant should be kept apprised of any such events, and should be consulted to determine if additional tests are necessary.

MOST RECOMMENDATIONS ARE PROFESSIONAL JUDGMENTS.

Site exploration and testing identifies actual surface and subsurface conditions only at those points where samples are taken. The data were extrapolated by your consultant, who then applied judgment to render an opinion about overall subsurface conditions. The actual interface between materials may be far more gradual or abrupt than your report indicates. Actual conditions in areas not sampled may differ from those predicted in your report. While nothing can be done to prevent such situations, you and your consultant can work together to help reduce their impacts. Retaining your consultant to observe subsurface construction operations can be particularly beneficial in this respect.

A REPORT'S CONCLUSIONS ARE PRELIMINARY.

The conclusions contained in your consultant's report are preliminary because they must be based on the assumption that conditions revealed through selective exploratory sampling are indicative of actual conditions throughout a site. Actual subsurface conditions can be discerned only during earthwork; therefore, you should retain your consultant to observe actual conditions and to provide conclusions. Only the consultant who prepared the report is fully familiar with the background information needed to determine whether or not the report's recommendations based on those conclusions are valid and whether or not the contractor is abiding by applicable recommendations. The consultant who developed your report cannot assume responsibility or liability for the adequacy of the report's recommendations if another party is retained to observe construction.

THE CONSULTANT'S REPORT IS SUBJECT TO MISINTERPRETATION.

Costly problems can occur when other design professionals develop their plans based on misinterpretation of a geotechnical/environmental report. To help avoid these problems, the consultant should be retained to work with other project design professionals to explain relevant geotechnical, geological, hydrogeological, and environmental findings, and to review the adequacy of their plans and specifications relative to these issues.

BORING LOGS AND/OR MONITORING WELL DATA SHOULD NOT BE SEPARATED FROM THE REPORT.

Final boring logs developed by the consultant are based upon interpretation of field logs (assembled by site personnel), field test results, and laboratory and/or office evaluation of field samples and data. Only final boring logs and data are customarily included in geotechnical/environmental reports. These final logs should not, under any circumstances, be redrawn for inclusion in architectural or other design drawings, because drafters may commit errors or omissions in the transfer process.

To reduce the likelihood of boring log or monitoring well misinterpretation, contractors should be given ready access to the complete geotechnical engineering/environmental report prepared or authorized for their use. If access is provided only to the report prepared for you, you should advise contractors of the report's limitations, assuming that a contractor was not one of the specific persons for whom the report was prepared, and that developing construction cost estimates was not one of the specific purposes for which it was prepared. While a contractor may gain important knowledge from a report prepared for another party, the contractor should discuss the report with your consultant and perform the additional or alternative work believed necessary to obtain the data specifically appropriate for construction cost estimating purposes. Some clients hold the mistaken impression that simply disclaiming responsibility for the accuracy of subsurface information always insulates them from attendant liability. Providing the best available information to contractors helps prevent costly construction problems and the adversarial attitudes that aggravate them to a disproportionate scale.

READ RESPONSIBILITY CLAUSES CLOSELY.

Because geotechnical/environmental engineering is based extensively on judgment and opinion, it is far less exact than other design disciplines. This situation has resulted in wholly unwarranted claims being lodged against consultants. To help prevent this problem, consultants have developed a number of clauses for use in their contracts, reports, and other documents. These responsibility clauses are not exculpatory clauses designed to transfer the consultant's liabilities to other parties; rather, they are definitive clauses that identify where the consultant's responsibilities begin and end. Their use helps all parties involved recognize their individual responsibilities and take appropriate action. Some of these definitive clauses are likely to appear in your report, and you are encouraged to read them closely. Your consultant will be pleased to give full and frank answers to your questions.

The preceding paragraphs are based on information provided by the
ASFE/Association of Engineering Firms Practicing in the Geosciences, Silver Spring, Maryland
